WEEK 43, 2026

2027 Data and Engineering Delivery Plan

Every initiative QS Technology is carrying into 2027: what it is, who owns it, when it builds and what it costs.

Cyber & Infra · Data · Core · Sector Intelligence · D&E · University Services

AT A GLANCE

109	6	42
INITIATIVES	PORTFOLIOS	IN BUILD OR RELEASE


Read the portfolio Kanban for where work sits by stage, the tables for the detail, and each portfolio section for its delivery schedule. Priority, area, technical risk and build windows are set where they have been agreed and inferred from the weekly reports otherwise.

Generated 19 October 2026 · internal use

Contents

Delivery schedule 3
Portfolio Kanban 4
Tech Transformation by Quarter 5
Cyber & Infra · Table 6
Data · Table 7
Core · Table 10
Sector Intelligence · Table 12
D&E · Table 14
University Services · Table 16
Cyber & Infra · Schedule 18
Data · Schedule 19
Core · Schedule 20
Sector Intelligence · Schedule 21
D&E · Schedule 22
University Services · Schedule 23

2027 Data and Engineering Delivery Plan

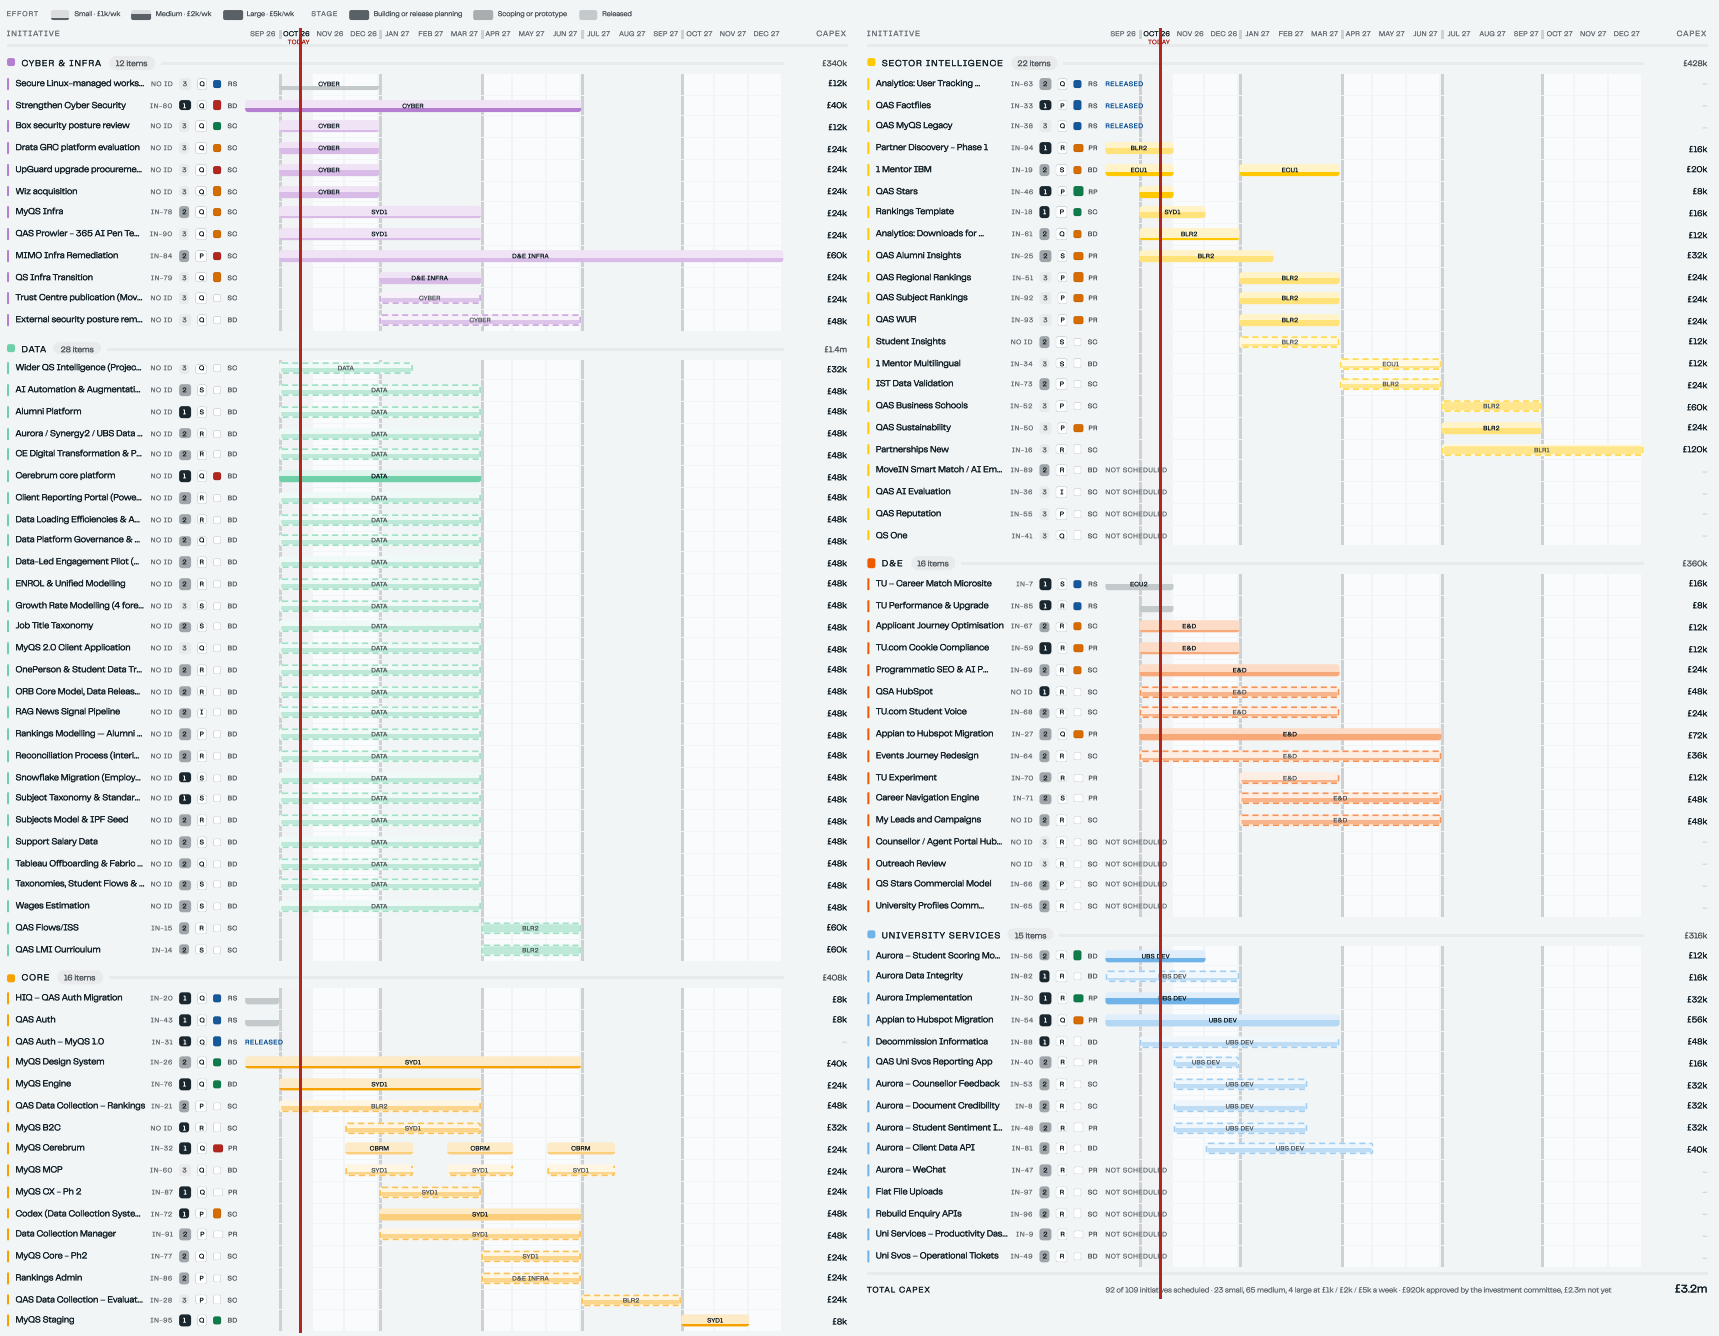

Portfolio Kanban

109 projects across 6 portfolios, by stage.

BY PORTFOLIO

Cyber & Infra	12
Data	28
Core	16
Sector Intelligence	22
D&E	16
University Services	15

BY STAGE

Scoping	40
Prototype	18
Building	40
Release planning	2
Released	9

STACK

QAS	41
Legacy	10
Other	58


WATCH LIST

6 with critical technical risk
CM, MI + MO, Cerebrum, Pulse (inc Cyber)

15 with high technical risk
CN (1M), SI, USP, Data Collection, Events / Outreach, MyQS, CX

0 with no owner on the Kanban

68 placeholders with no roadmap profile yet

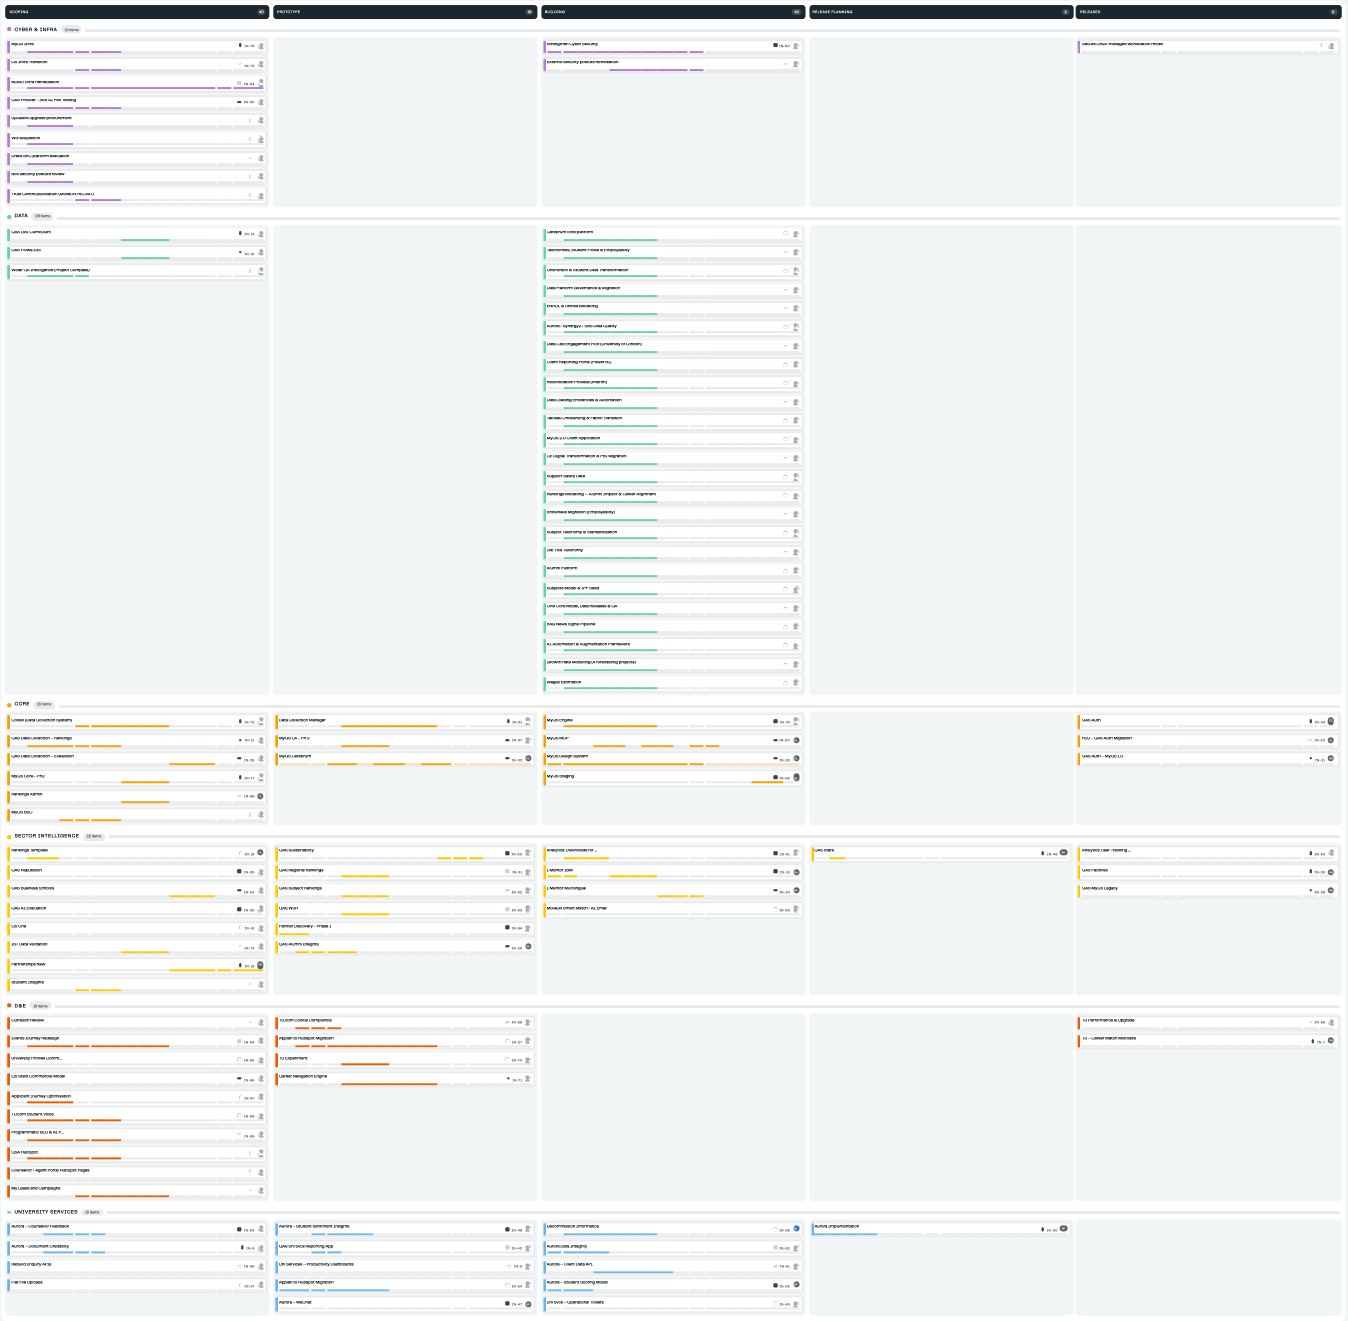


2027 Data and Engineering Delivery Plan

Tech Transformation by Quarter Q1 2025 – Q4 2027

New or replatformed Retired

27 ARRIVING 16 RETIRED

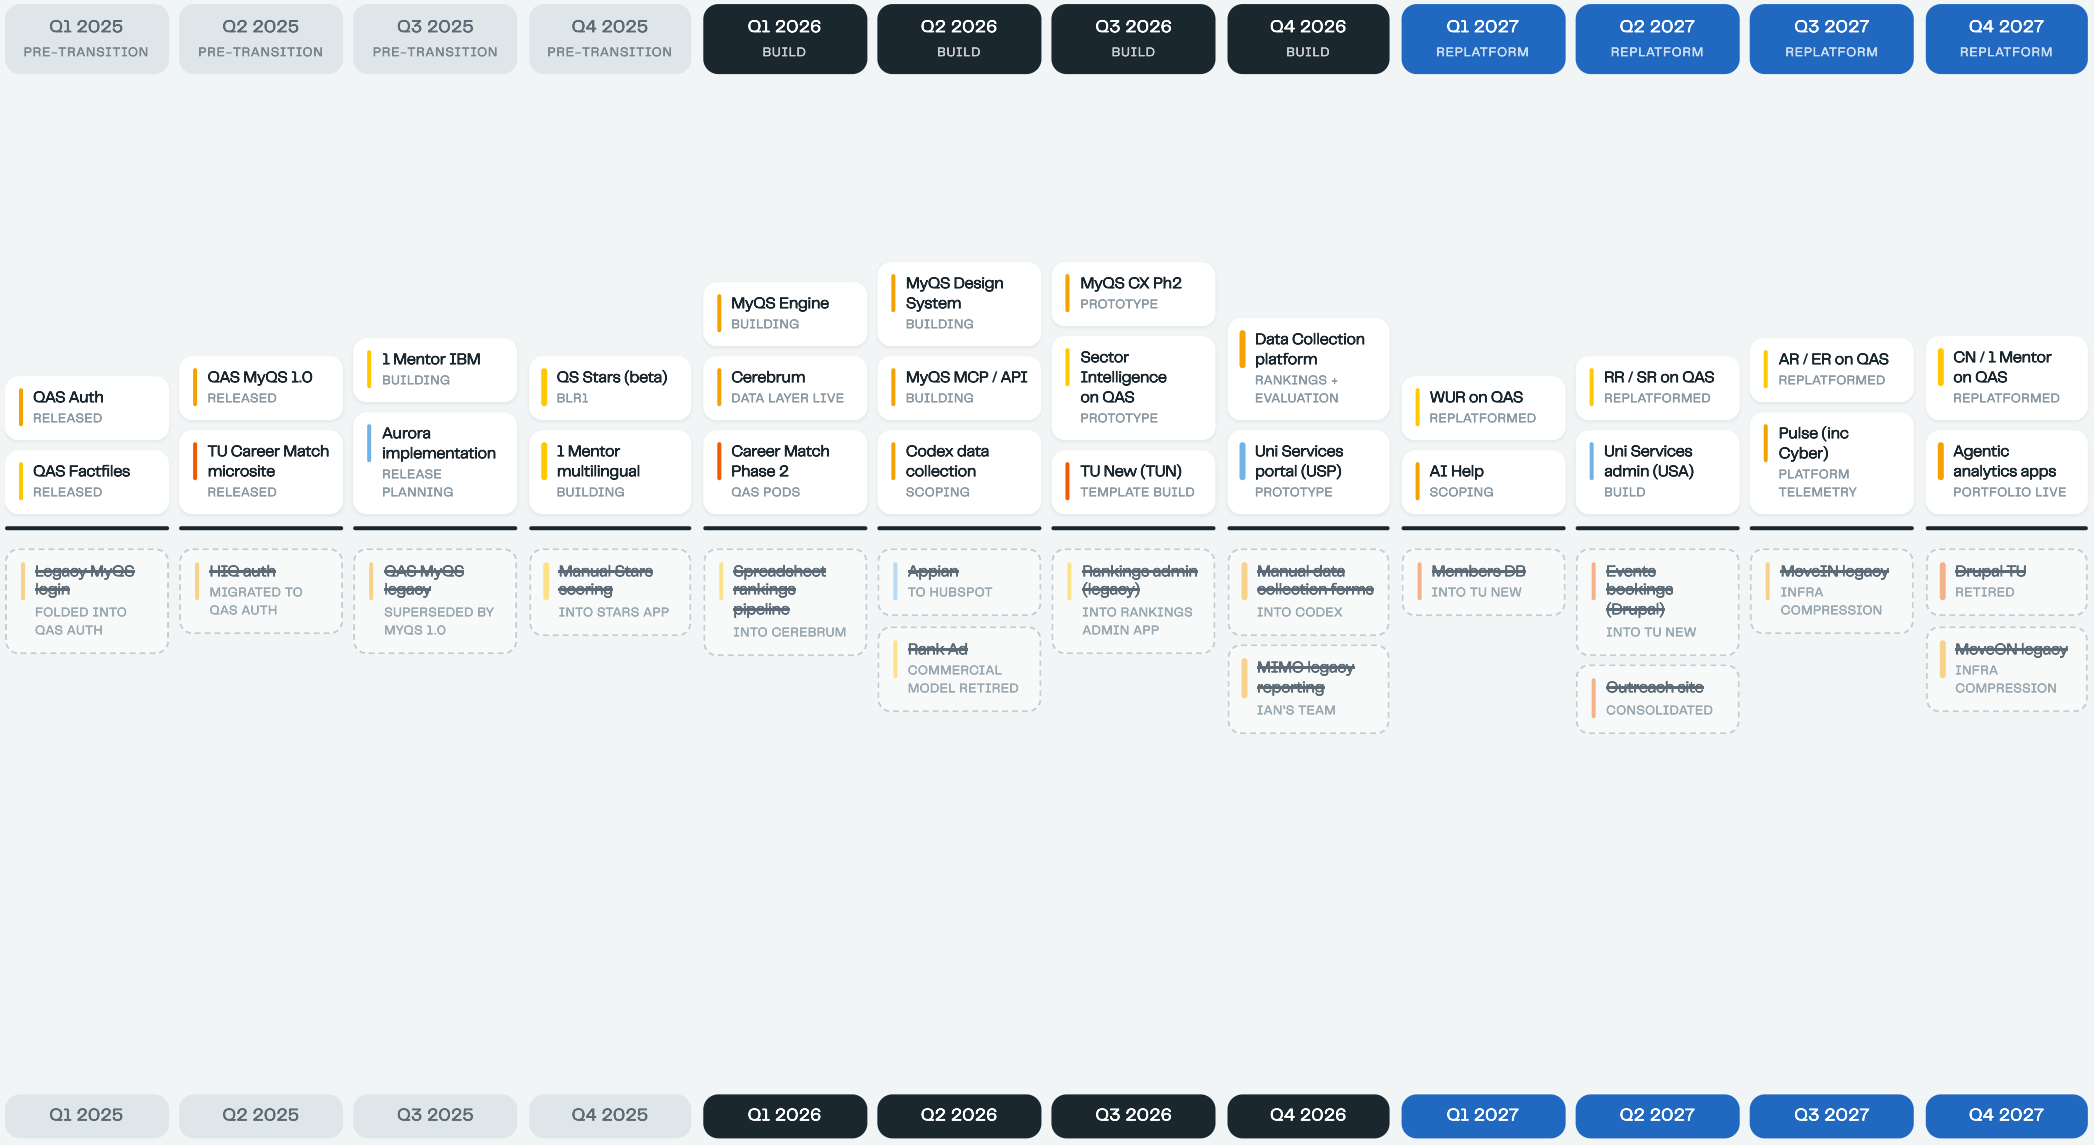

Inferred from the current product portfolio and the QAS transition plan. Quarters are calendar quarters.

Generated 19 October 2026 from the roadmap Kanban. Leads, readiness and technical risk are inherited from roadmap product profiles and are working placeholders.

2027 Data and Engineering Delivery Plan

Cyber & Infra · Table 12 projects

PROJECT ▲	STACK	STAGE	LEADS	DESCRIPTION	EXPECTED BUILD	TECHNICAL RISK	READY CHECK
Box security posture review NO ID · PLACEHOLDER	OTHER	SCOPING	PB T T	Additional discovery sessions were held with the Marketing and Creative teams to	Oct 26 – Dec 26	LOW	TW4
Drata GRC platform evaluation NO ID · PLACEHOLDER	OTHER	SCOPING	PB T T	Discussions regarding Drata were delayed due to stakeholder availability constraints, but the	Oct 26 – Dec 26	MODERATE	TW4
External security posture remediation NO ID · PLACEHOLDER	OTHER	BUILDING	PB T T	Work with multiple teams on externally visible security issues and vulnerabilities contributed to	Jan 27 – Jun 27	TBC	TW5
MIMO Infra Remediation IN-84 · MI + MO	LEGACY	SCOPING	PB T A	MoveIN infrastructure and the tooling that sits on it. Legacy estate carried by a small	Oct 26 – Dec 27	CRITICAL	TW4 REVIEW
MyQS Infra IN-78 · MYQS	QAS	SCOPING	PB CL CL	The single application shell QS staff and clients log into. Everything in the portfolio surfaces	Oct 26 – Mar 27	MODERATE	TW4 ELT
QAS Prowler – 365 AI Pen Testing IN-90 · PLACEHOLDER	QAS	SCOPING	PB T T	Creation of a daily penetration test of all QAS assets and attack surfaces. Logs into Outline,	Oct 26 – Mar 27	MODERATE	TW4
QS Infra Transition IN-79 · PLACEHOLDER	OTHER	SCOPING	PB T J	Not yet profiled for the roadmap. Scope, leads and readiness to be confirmed.	Jan 27 – Mar 27	MODERATE	TW5
Secure Linux-managed workstation model NO ID · PLACEHOLDER	OTHER	RELEASED	PB T T	Rebuilding Rowan's laptop with Ubuntu 26 LTS, Secure Boot, TPM-backed encryption and Entra	Released	TBC	Live
Strengthen Cyber Security IN-80 · PULSE (INC CYBER)	QAS	BUILDING	PB T T	Platform health, monitoring and the cyber hardening programme. Gives one view of	Sep 26 – Jun 27	CRITICAL	TW4 REVIEW
Trust Centre publication (MoveON HECVAT) NO ID · PLACEHOLDER	OTHER	SCOPING	PB T T	Outstanding items in the MoveON HECVAT questionnaire continued to be reviewed and	Jan 27 – Mar 27	TBC	TW5
UpGuard upgrade procurement NO ID · PLACEHOLDER	OTHER	SCOPING	PB T T	Procurement of the UpGuard upgrade continued with only incremental updates, and	Oct 26 – Dec 26	CRITICAL	TW4
Wiz acquisition NO ID · PLACEHOLDER	OTHER	SCOPING	PB T T	Procurement activity for acquiring Wiz continued alongside UpGuard as a key enabler	Oct 26 – Dec 26	MODERATE	TW4

Generated 19 October 2026 from the roadmap Kanban. Leads, readiness and technical risk are inherited from roadmap product profiles and are working placeholders.

2027 Data and Engineering Delivery Plan

PROJECT ▲	STACK	STAGE	LEADS	DESCRIPTION	EXPECTED BUILD	TECHNICAL RISK	READY CHECK
AI Automation & Augmentation Framework NO ID · PLACEHOLDER	OTHER	BUILDING	DP T T	Layer 1 baseline scores complete; Layer 2 v1 implemented but found six structural	Oct 26 – Mar 27	TBC	TW4
Alumni Platform NO ID · PLACEHOLDER	OTHER	BUILDING	MS T T	Migrated Snowflake profile datasets handed to Charlie; analytics being	Oct 26 – Mar 27	TBC	TW4
Aurora / Synergy2 / UBS Data Quality NO ID · PLACEHOLDER	OTHER	BUILDING	DP T T	Synergy2 TEST environment live for BI; Deferred/Declined journeys backfilled;	Oct 26 – Mar 27	TBC	TW4
CE Digital Transformation & PBI Migration NO ID · PLACEHOLDER	OTHER	BUILDING	DP T T	Supporting lead-scoring model and B2B/B2C funnel work with Natalie's	Oct 26 – Mar 27	TBC	TW4
Cerebrum core platform NO ID · PLACEHOLDER	OTHER	BUILDING	DP T T	Institution identity now read from platform registry; false merge-reviews	Oct 26 – Mar 27	TBC	TW4
Client Reporting Portal (Power BI) NO ID · PLACEHOLDER	OTHER	BUILDING	DP T T	Greenlight session booked 7 Oct ahead of 16 Oct access target; Sean Coffey's	Oct 26 – Mar 27	TBC	TW4
Data Loading Efficiencies & Automation NO ID · PLACEHOLDER	OTHER	BUILDING	DP T T	Contact Matching v2 running across all clients; historical source-tag migration	Oct 26 – Mar 27	TBC	TW4
Data Platform Governance & Migration NO ID · PLACEHOLDER	OTHER	BUILDING	DP T T	Most Data Science repos moved GitLab→GitHub; Prefect IaC	Oct 26 – Mar 27	TBC	TW4
Data-Led Engagement Pilot (University of London) NO ID · PLACEHOLDER	OTHER	BUILDING	DP T T	Campaign build complete; Stirling lined up as the next campaign. Blocker:	Oct 26 – Mar 27	TBC	TW4
ENROL & Unified Modelling NO ID · PLACEHOLDER	OTHER	BUILDING	DP T T	First model sign-off reporting workflow delivered; course-of-interest models	Oct 26 – Mar 27	TBC	TW4

Generated 19 October 2026 from the roadmap Kanban. Leads, readiness and technical risk are inherited from roadmap product profiles and are working placeholders.

PROJECT ▲	STACK	STAGE	LEADS	DESCRIPTION	EXPECTED BUILD	TECHNICAL RISK	READY CHECK
Growth Rate Modelling (4 forecasting projects) NO ID · PLACEHOLDER	OTHER	BUILDING	DP T T	24 country workbooks rebuilt on the new CAGR methodology (review under	Oct 26 – Mar 27	TBC	TW4
Job Title Taxonomy NO ID · PLACEHOLDER	OTHER	BUILDING	DP T T	QSIDs now in hand for the migration. Blocker: Migration delayed until the	Oct 26 – Mar 27	TBC	TW4
MyQS 2.0 Client Application NO ID · PLACEHOLDER	OTHER	BUILDING	DP T T	Stirling prototype expected mid-Nov–early Dec. Blocker: Full build/launch	Oct 26 – Mar 27	TBC	TW4
OnePerson & Student Data Transformation NO ID · PLACEHOLDER	OTHER	BUILDING	DP T T	QS Apply and Appian added as sources; People Data Labs scoping under way;	Oct 26 – Mar 27	TBC	TW4
ORB Core Model, Data Releases & QA NO ID · PLACEHOLDER	OTHER	BUILDING	DP T T	New gap-filling methods tested; test run complete with revised global totals; India	Oct 26 – Mar 27	TBC	TW4
QAS Flows/ISS IN-15 · PLACEHOLDER	QAS	SCOPING	SK DP SH	Not yet profiled for the roadmap. Scope, leads and readiness to be confirmed.	Apr 27 – Jun 27	TBC	TW6
QAS LMI Curriculum IN-14 · PLACEHOLDER	QAS	SCOPING	MS D CL	Not yet profiled for the roadmap. Scope, leads and readiness to be confirmed.	Apr 27 – Jun 27	TBC	TW6
RAG News Signal Pipeline NO ID · PLACEHOLDER	OTHER	BUILDING	DP T T	Country-sources pipeline rebuilt to match the international design; 21	Oct 26 – Mar 27	TBC	TW4
Rankings Modelling — Alumni Impact & Career Alignment NO ID · PLACEHOLDER	OTHER	BUILDING	DP T T	Restructured to Sam's new spec; subject standardisation, seniority and skill-	Oct 26 – Mar 27	TBC	TW4
Reconciliation Process (interim) NO ID · PLACEHOLDER	OTHER	BUILDING	DP T T	VW_RECON_RESULT built in Synergy2; Griffith interim list due 7 Oct. Blocker:	Oct 26 – Mar 27	TBC	TW4

2027 Data and Engineering Delivery Plan

PROJECT ▲	STACK	STAGE	LEADS	DESCRIPTION	EXPECTED BUILD	TECHNICAL RISK	READY CHECK
Snowflake Migration (Employability) NO ID · PLACEHOLDER	OTHER	BUILDING	DP T T	Raw/processed GCP pipeline finalised for profile datasets; same approach	Oct 26 – Mar 27	TBC	TW4
Subject Taxonomy & Standardization NO ID · PLACEHOLDER	OTHER	BUILDING	DP T T	v2.1 shared for sign-off; Studyportals and UBS mappings finalised and sent for	Oct 26 – Mar 27	TBC	TW4
Subjects Model & IPF Seed NO ID · PLACEHOLDER	OTHER	BUILDING	DP T T	Major milestone: university-by-subject data collected for 26 countries (2.5m	Oct 26 – Mar 27	TBC	TW4
Support Salary Data NO ID · PLACEHOLDER	OTHER	BUILDING	DP T T	Passed PDL's refreshed inferred salary field (with min/max ranges) to LMI;	Oct 26 – Mar 27	TBC	TW4
Tableau Offboarding & Fabric Transition NO ID · PLACEHOLDER	OTHER	BUILDING	DP T T	Non-renewal notice issued 28 Sep; scoping sent to	Oct 26 – Mar 27	TBC	TW4
Taxonomies, Student Flows & Employability NO ID · PLACEHOLDER	OTHER	BUILDING	DP T T	Programme-to-subject mapper deployed to AWS Lambda/Bedrock; Job	Oct 26 – Mar 27	TBC	TW4
Wages Estimation NO ID · PLACEHOLDER	OTHER	BUILDING	DP T T	2025 median wage estimates complete for 22 of 24 countries; occupational tag	Oct 26 – Mar 27	TBC	TW4
Wider QS Intelligence (Project Compass) NO ID · PLACEHOLDER	OTHER	SCOPING	DP T T	Groundwork complete (ISS, Rankings, GSF walkthroughs); concept previewed	Oct 26 – Jan 27	TBC	TW4

Generated 19 October 2026 from the roadmap Kanban. Leads, readiness and technical risk are inherited from roadmap product profiles and are working placeholders.

2027 Data and Engineering Delivery Plan

PROJECT ▲	STACK	STAGE	LEADS	DESCRIPTION	EXPECTED BUILD	TECHNICAL RISK	READY CHECK
Codex (Data Collection System) IN-72 · DATA COLLECTION	QAS	SCOPING	PB DP SH	Codex, the single intake system for rankings and evaluation submissions.	Jan 27 – Jun 27	MODERATE	TW5 ELT
Data Collection Manager IN-91 · DATA COLLECTION	QAS	PROTOTYPE	PB MX MB	Codex, the single intake system for rankings and evaluation submissions.	Jan 27 – Jun 27	HIGH	TW5 ELT
HIQ – QAS Auth Migration IN-20 · PLACEHOLDER	OTHER	RELEASED	PB T CL	Not yet profiled for the roadmap. Scope, leads and readiness to be confirmed.	Released	TBC	Live
MyQS B2C NO ID · PLACEHOLDER	OTHER	SCOPING	PB T CL	Not yet profiled for the roadmap. Scope, leads and readiness to be confirmed.	Dec 26 – Mar 27	TBC	TW4
MyQS Cerebrum IN-32 · CEREBRUM	QAS	PROTOTYPE	PB CL CL	The governed data layer behind every product, holding the QS ontology and	Dec 26 – Jan 27 · Mar 27 – Apr 27 · Jun 27 – Jul 27 Heavy maintenance outside build	CRITICAL	TW4 ELT
MyQS Core – Ph2 IN-77 · MYQS	QAS	SCOPING	PB CL CL	The single application shell QS staff and clients log into. Everything in the	Apr 27 – Jun 27	HIGH	TW6 ELT
MyQS CX – Ph 2 IN-87 · CX	QAS	PROTOTYPE	L CL CL	Client-facing experience and admin tooling layered over MyQS. Covers	Jan 27 – Mar 27	HIGH	TW5 REVIEW
MyQS Design System IN-26 · MYQS	QAS	BUILDING	PB CL CL	The single application shell QS staff and clients log into. Everything in the	Sep 26 – Jun 27 Heavy maintenance outside build	LOW	TW4 ELT
MyQS Engine IN-76 · MYQS	QAS	BUILDING	PB T CL	The single application shell QS staff and clients log into. Everything in the	Oct 26 – Mar 27	LOW	TW4 ELT
MyQS MCP IN-60 · MYQS	QAS	BUILDING	PB CL CL	The single application shell QS staff and clients log into. Everything in the	Dec 26 – Jan 27 · Mar 27 – Apr 27 · Jun 27 – Jul 27	HIGH	TW4 ELT

2027 Data and Engineering Delivery Plan

PROJECT ▲	STACK	STAGE	LEADS	DESCRIPTION	EXPECTED BUILD	TECHNICAL RISK	READY CHECK
MyQS Staging IN-95 · MYQS	QAS	BUILDING	PB AS MB	The single application shell QS staff and clients log into. Everything in the	Oct 27 – Nov 27	LOW	TW7 ELT
QAS Auth IN-43 · PLACEHOLDER	QAS	RELEASED	PB T CL	Not yet profiled for the roadmap. Scope, leads and readiness to be confirmed.	Released	TBC	Live
QAS Auth – MyQS 1.0 IN-31 · PLACEHOLDER	QAS	RELEASED	PB T CL	Not yet profiled for the roadmap. Scope, leads and readiness to be confirmed.	Released	TBC	Live
QAS Data Collection – Evaluation IN-28 · DATA COLLECTION	QAS	SCOPING	LK DP SH	Codex, the single intake system for rankings and evaluation submissions.	Jul 27 – Sep 27	HIGH	TW7 ELT
QAS Data Collection – Rankings IN-21 · DATA COLLECTION	QAS	SCOPING	LK DP SH	Codex, the single intake system for rankings and evaluation submissions.	Oct 26 – Mar 27	HIGH	TW4 ELT
Rankings Admin IN-86 · PLACEHOLDER	OTHER	SCOPING	LK DP CL	Not yet profiled for the roadmap. Scope, leads and readiness to be confirmed.	Apr 27 – Jun 27	TBC	TW6

PROJECT ▲	STACK	STAGE	LEADS	DESCRIPTION	EXPECTED BUILD	TECHNICAL RISK	READY CHECK
1 Mentor IBM IN-19 · CN (1M)	QAS	BUILDING	MS T SH	Career navigation delivered through 1 Mentor as the master white label. Serves	Sep 26 – Oct 26 · Jan 27 – Mar 27	MODERATE	TW4 REVIEW
1 Mentor Multilingual IN-34 · CN (1M)	QAS	BUILDING	MS T SH	Career navigation delivered through 1 Mentor as the master white label. Serves	Apr 27 – Jun 27	HIGH	TW6 REVIEW
Analytics: Downloads for ... IN-61 · SI	QAS	BUILDING	MM CB MB	Sector intelligence products sold to institutions, including partner discovery	Oct 26 – Dec 26	MODERATE	TW4 ELT
Analytics: User Tracking ... IN-63 · SI	QAS	RELEASED	PB CB MB	Sector intelligence products sold to institutions, including partner discovery	Released	HIGH	Live
IST Data Validation IN-73 · PLACEHOLDER	OTHER	SCOPING	LK T SH	Not yet profiled for the roadmap. Scope, leads and readiness to be confirmed.	Apr 27 – Jun 27	TBC	TW6
MoveIN Smart Match / AI Email IN-89 · PLACEHOLDER	OTHER	BUILDING	T T MH	Not yet profiled for the roadmap. Scope, leads and readiness to be confirmed.	Build window TBC	TBC	TBC
Partner Discovery – Phase 1 IN-94 · SI	QAS	PROTOTYPE	IL CB MB	Sector intelligence products sold to institutions, including partner discovery	Sep 26 – Oct 26	MODERATE	TW4 ELT
Partnerships New IN-16 · SI	QAS	SCOPING	IL DP SH	Sector intelligence products sold to institutions, including partner discovery	Jul 27 – Dec 27	HIGH	TW7 ELT
QAS AI Evaluation IN-36 · PLACEHOLDER	QAS	SCOPING	LK T T	Not yet profiled for the roadmap. Scope, leads and readiness to be confirmed.	Build window TBC	TBC	TBC
QAS Alumni Insights IN-25 · SI	QAS	PROTOTYPE	MS CL CL	Sector intelligence products sold to institutions, including partner discovery	Oct 26 – Jan 27	MODERATE	TW4 ELT
QAS Business Schools IN-52 · PLACEHOLDER	QAS	SCOPING	MM DP SH	Not yet profiled for the roadmap. Scope, leads and readiness to be confirmed.	Jul 27 – Sep 27	TBC	TW7

PROJECT ▲	STACK	STAGE	LEADS	DESCRIPTION	EXPECTED BUILD	TECHNICAL RISK	READY CHECK
QAS Factfiles IN-33 · PLACEHOLDER	QAS	RELEASED	LK T SH	Not yet profiled for the roadmap. Scope, leads and readiness to be confirmed.	Released	TBC	Live
QAS MyQS Legacy IN-38 · MYQS	QAS	RELEASED	PB AS MB	The single application shell QS staff and clients log into. Everything in the	Released	HIGH	Live
QAS Regional Rankings IN-51 · RR	LEGACY	PROTOTYPE	MM DP SH	Regional rankings across Asia, Latin America, Europe and the Arab region.	Jan 27 – Mar 27	MODERATE	TW5 REVIEW
QAS Reputation IN-55 · PLACEHOLDER	QAS	SCOPING	MM DP SH	Not yet profiled for the roadmap. Scope, leads and readiness to be confirmed.	Build window TBC	TBC	TBC
QAS Stars IN-46 · STARS	QAS	RELEASE PLANNING	LK T SH	The QS Stars audit and rating product. Furthest advanced of the	Oct 26	LOW	TW4 ELT
QAS Subject Rankings IN-92 · SR	LEGACY	PROTOTYPE	MM MX SN	Rankings by subject and broad faculty area. The widest rankings dataset by	Jan 27 – Mar 27	MODERATE	TW5 REVIEW
QAS Sustainability IN-50 · PLACEHOLDER	QAS	PROTOTYPE	MM DP SH	Not yet profiled for the roadmap. Scope, leads and readiness to be confirmed.	Jul 27 – Sep 27	MODERATE	TW7
QAS WUR IN-93 · WUR	LEGACY	PROTOTYPE	MM MX SN	The World University Rankings, QS' flagship ranking and the highest-profile	Jan 27 – Mar 27	MODERATE	TW5 REVIEW
QS One IN-41 · PLACEHOLDER	OTHER	SCOPING	MH T SH	Not yet profiled for the roadmap. Scope, leads and readiness to be confirmed.	Build window TBC	TBC	TBC
Rankings Template IN-18 · PLACEHOLDER	OTHER	SCOPING	PB CL CL	Not yet profiled for the roadmap. Scope, leads and readiness to be confirmed.	Oct 26 – Nov 26	LOW	TW4
Student Insights NO ID · PLACEHOLDER	OTHER	SCOPING	T T T	Not yet profiled for the roadmap. Scope, leads and readiness to be confirmed.	Jan 27 – Mar 27	TBC	TW5

2027 Data and Engineering Delivery Plan

PROJECT ▲	STACK	STAGE	LEADS	DESCRIPTION	EXPECTED BUILD	TECHNICAL RISK	READY CHECK
Appian to Hubspot Migration IN-27 · PLACEHOLDER	OTHER	PROTOTYPE	N T SP	Not yet profiled for the roadmap. Scope, leads and readiness to be confirmed.	Oct 26 – Jun 27	MODERATE	TW4
Applicant Journey Optimisation IN-67 · PLACEHOLDER	OTHER	SCOPING	N T T	Not yet profiled for the roadmap. Scope, leads and readiness to be confirmed.	Oct 26 – Dec 26	MODERATE	TW4
Career Navigation Engine IN-71 · CM	QAS	PROTOTYPE	N CB RP	Career Match, the first QAS-native consumer product. Matches students	Jan 27 – Jun 27	CRITICAL	TW5 ELT
Counsellor / Agent Portal HubSpot Pages NO ID · PLACEHOLDER	OTHER	SCOPING	N T T	Not yet profiled for the roadmap. Scope, leads and readiness to be confirmed.	Build window TBC	TBC	TBC
Events Journey Redesign IN-64 · EVENTS / OUTREACH	LEGACY	SCOPING	N T VV	Event bookings, outreach sites and the members database. Consolidating into	Oct 26 – Jun 27	HIGH	TW4 REVIEW
My Leads and Campaigns NO ID · PLACEHOLDER	OTHER	SCOPING	N T T	Not yet profiled for the roadmap. Scope, leads and readiness to be confirmed.	Jan 27 – Jun 27	TBC	TW5
Outreach Review NO ID · PLACEHOLDER	OTHER	SCOPING	N T T	Not yet profiled for the roadmap. Scope, leads and readiness to be confirmed.	Build window TBC	TBC	TBC
Programmatic SEO & AI P... IN-69 · PLACEHOLDER	OTHER	SCOPING	N T T	Not yet profiled for the roadmap. Scope, leads and readiness to be confirmed.	Oct 26 – Mar 27	MODERATE	TW4
QS Stars Commercial Model IN-66 · STARS	QAS	SCOPING	N CB MB	The QS Stars audit and rating product. Furthest advanced of the	Build window TBC	MODERATE	TBC
QSA HubSpot NO ID · PLACEHOLDER	OTHER	SCOPING	N T SP	Not yet profiled for the roadmap. Scope, leads and readiness to be confirmed.	Oct 26 – Mar 27	TBC	TW4

2027 Data and Engineering Delivery Plan

PROJECT ▲	STACK	STAGE	LEADS	DESCRIPTION	EXPECTED BUILD	TECHNICAL RISK	READY CHECK
TU – Career Match Microsite IN-7 · CM	QAS	RELEASED	N CB RP	Career Match, the first QAS-native consumer product. Matches students	Released	CRITICAL	Live
TU Experiment IN-70 · PLACEHOLDER	OTHER	PROTOTYPE	N T T	Not yet profiled for the roadmap. Scope, leads and readiness to be confirmed.	Jan 27 – Mar 27	TBC	TW5
TU Performance & Upgrade IN-85 · TUO	LEGACY	RELEASED	N T MB	Top Universities as it runs today on Drupal. Keeps the traffic and revenue	Released	LOW	Live
TU.com Cookie Compliance IN-59 · TUO	LEGACY	PROTOTYPE	N T MB	Top Universities as it runs today on Drupal. Keeps the traffic and revenue	Oct 26 – Dec 26	MODERATE	TW4 REVIEW
TU.com Student Voice IN-68 · PLACEHOLDER	OTHER	SCOPING	N T T	Not yet profiled for the roadmap. Scope, leads and readiness to be confirmed.	Oct 26 – Mar 27	TBC	TW4
University Profiles Comm... IN-65 · PLACEHOLDER	OTHER	SCOPING	N T T	Not yet profiled for the roadmap. Scope, leads and readiness to be confirmed.	Build window TBC	TBC	TBC

Generated 19 October 2026 from the roadmap Kanban. Leads, readiness and technical risk are inherited from roadmap product profiles and are working placeholders.

2027 Data and Engineering Delivery Plan

PROJECT ▲	STACK	STAGE	LEADS	DESCRIPTION	EXPECTED BUILD	TECHNICAL RISK	READY CHECK
Appian to Hubspot Migration IN-54 · PLACEHOLDER	OTHER	PROTOTYPE	JH T T	Not yet profiled for the roadmap. Scope, leads and readiness to be confirmed.	Sep 26 – Mar 27	MODERATE	TW4
Aurora – Client Data API IN-81 · USA	LEGACY	BUILDING	S MA MK	The admin and reporting side of university services. Includes data	Dec 26 – Apr 27	MODERATE	TW4 REVIEW
Aurora – Counsellor Feedback IN-53 · USP	QAS	SCOPING	S MA MK	Aurora-based portal for university services clients. Covers student	Nov 26 – Feb 27	HIGH	TW4 REVIEW
Aurora – Document Credibility IN-8 · USP	QAS	SCOPING	S MA MK	Aurora-based portal for university services clients. Covers student	Nov 26 – Feb 27	HIGH	TW4 REVIEW
Aurora – Student Scoring Model IN-56 · USP	QAS	BUILDING	S MA MK	Aurora-based portal for university services clients. Covers student	Sep 26 – Nov 26	LOW	TW4 REVIEW
Aurora – Student Sentiment Insights IN-48 · USP	QAS	PROTOTYPE	S MA MK	Aurora-based portal for university services clients. Covers student	Nov 26 – Feb 27	HIGH	TW4 REVIEW
Aurora – WeChat IN-47 · USP	QAS	PROTOTYPE	S MA MK	Aurora-based portal for university services clients. Covers student	Build window TBC	HIGH	TBC
Aurora Data Integrity IN-82 · USA	LEGACY	BUILDING	DP MA MK	The admin and reporting side of university services. Includes data	Sep 26 – Dec 26	MODERATE	TW4 REVIEW
Aurora Implementation IN-30 · USP	QAS	RELEASE PLANNING	S MA MK	Aurora-based portal for university services clients. Covers student	Sep 26 – Dec 26	LOW	TW4 REVIEW
Decommission Informatica IN-88 · PLACEHOLDER	OTHER	BUILDING	GL T T	Not yet profiled for the roadmap. Scope, leads and readiness to be confirmed.	Oct 26 – Mar 27	TBC	TW4


PROJECT ▲	STACK	STAGE	LEADS	DESCRIPTION	EXPECTED BUILD	TECHNICAL RISK	READY CHECK
Flat File Uploads IN-97 · PLACEHOLDER	OTHER	SCOPING	S T T	Transfer and data uploads from universities into the system.	Build window TBC	TBC	TBC
QAS Uni Svcs Reporting App IN-40 · USA	LEGACY	PROTOTYPE	S MA MK	The admin and reporting side of university services. Includes data	Nov 26 – Dec 26	MODERATE	TW4 REVIEW
Rebuild Enquiry APIs IN-96 · PLACEHOLDER	OTHER	SCOPING	DP T T	Rebuild of the enquiry APIs. AWS costs are still being paid on the service	Build window TBC	TBC	TBC
Uni Services – Productivity Dashboards IN-9 · PLACEHOLDER	OTHER	PROTOTYPE	S T T	Not yet profiled for the roadmap. Scope, leads and readiness to be confirmed.	Build window TBC	TBC	TBC
Uni Svcs – Operational Tickets IN-49 · PLACEHOLDER	OTHER	BUILDING	S T T	Not yet profiled for the roadmap. Scope, leads and readiness to be confirmed.	Build window TBC	TBC	TBC

SECTION 1 OF 6

Cyber & Infra

12 initiatives · delivery schedule

9 scoping
2 building
1 released

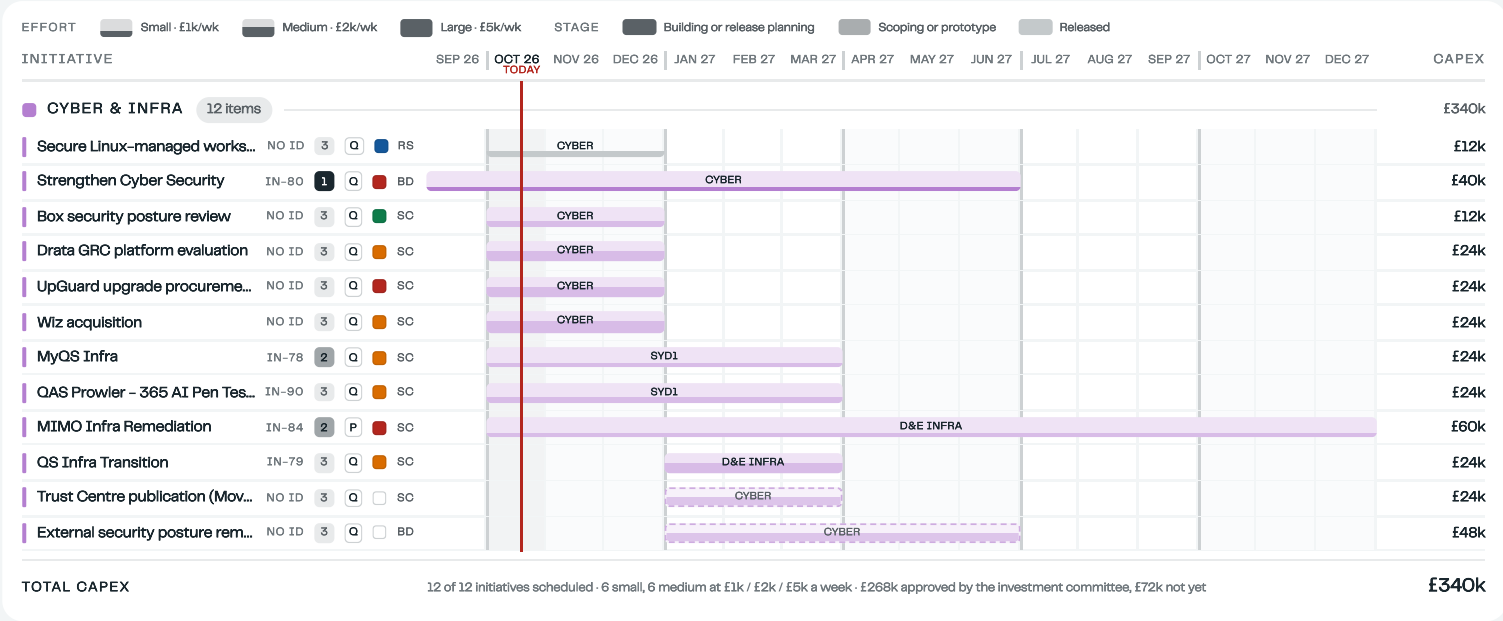


SECTION 2 OF 6

Data

28 initiatives · delivery schedule

3 scoping
25 building

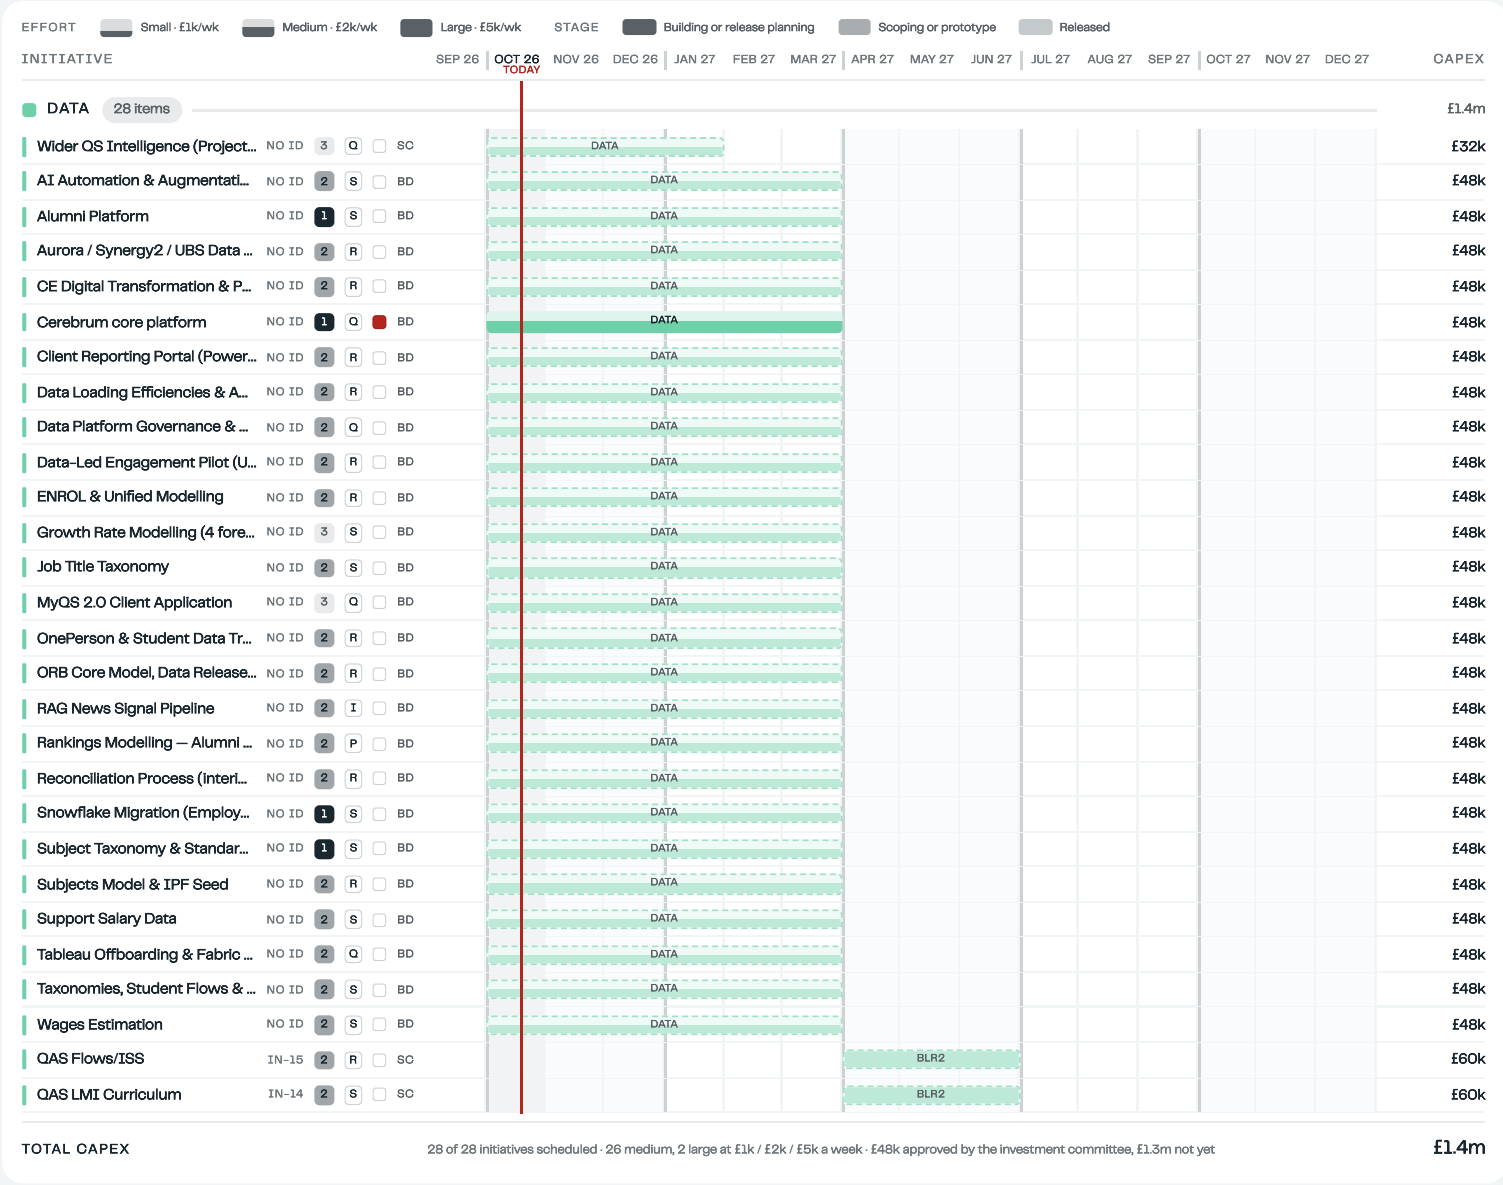


SECTION 3 OF 6

Core

16 initiatives · delivery schedule

6 scoping
3 prototype
4 building
3 released

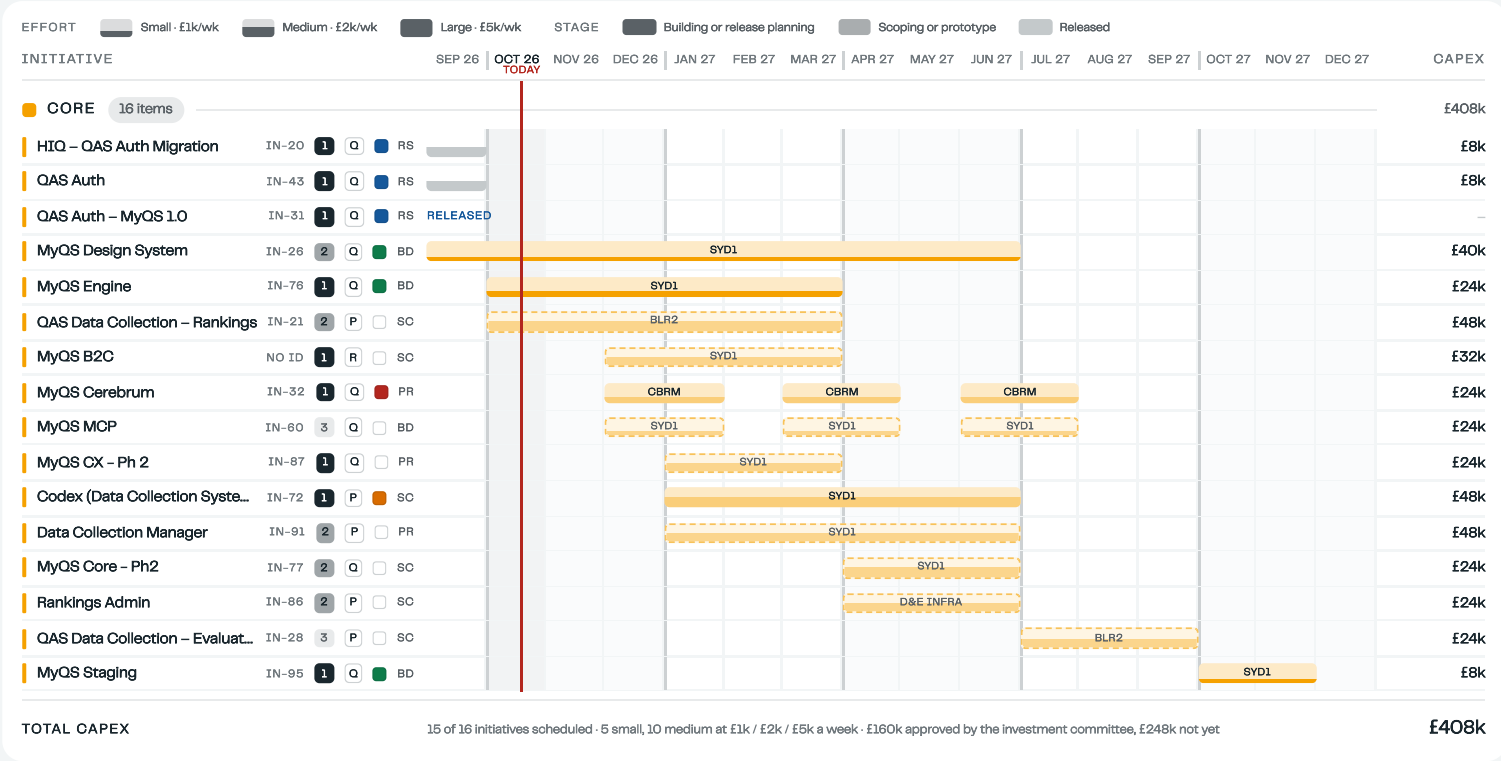


SECTION 4 OF 6

Sector Intelligence

22 initiatives · delivery schedule

8 scoping
6 prototype
4 building
1 release planning
3 released

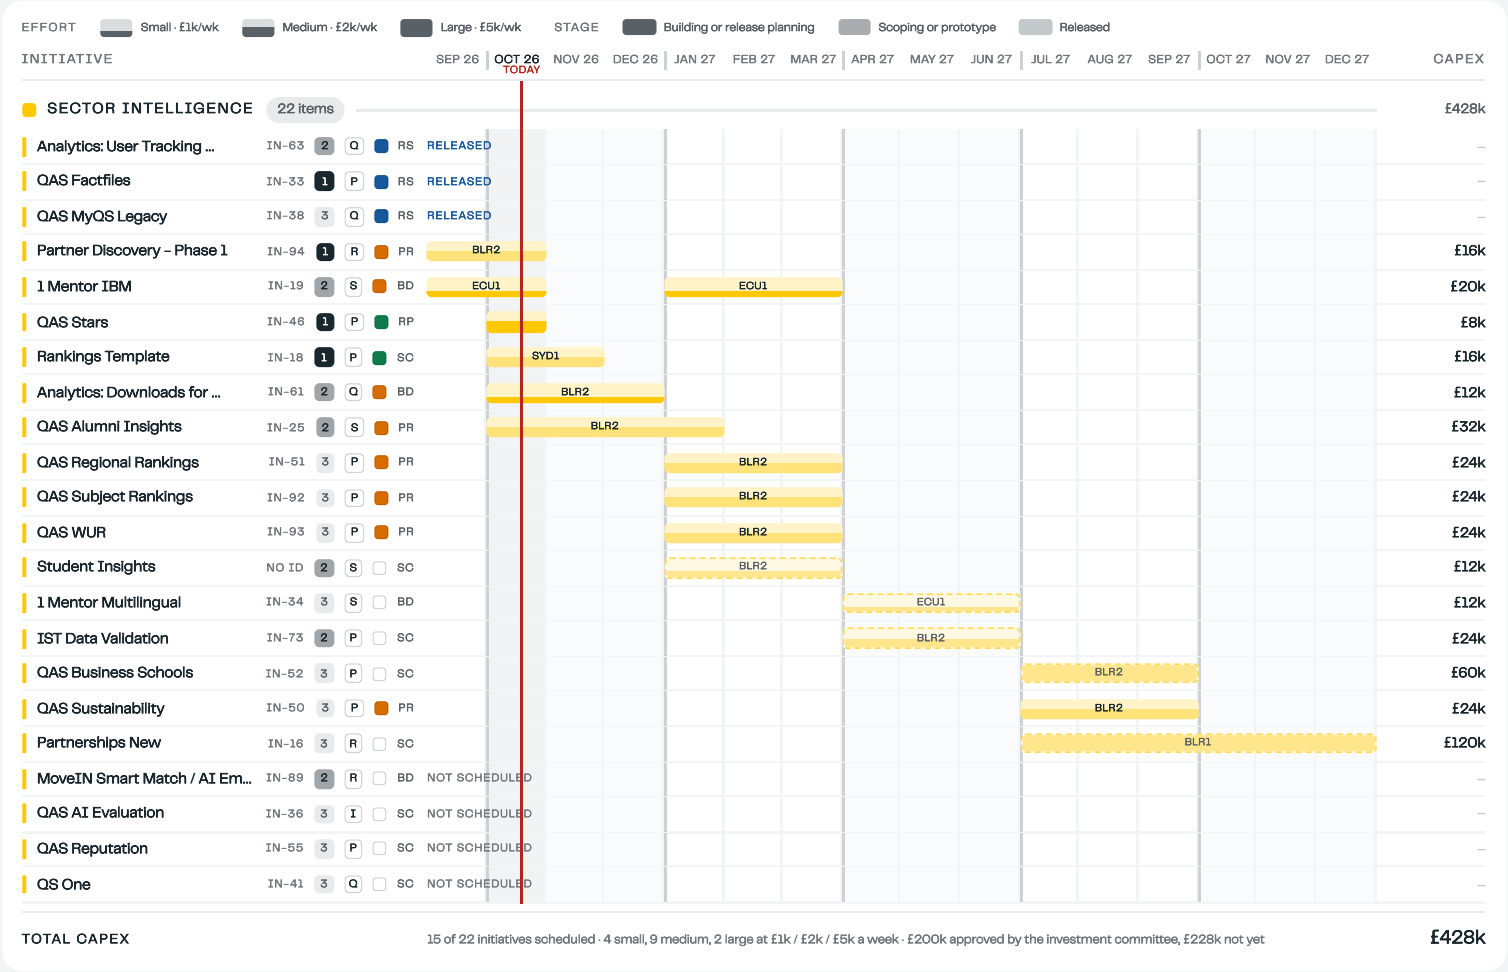


SECTION 5 OF 6

D&E

16 initiatives · delivery schedule

10 scoping
4 prototype
2 released

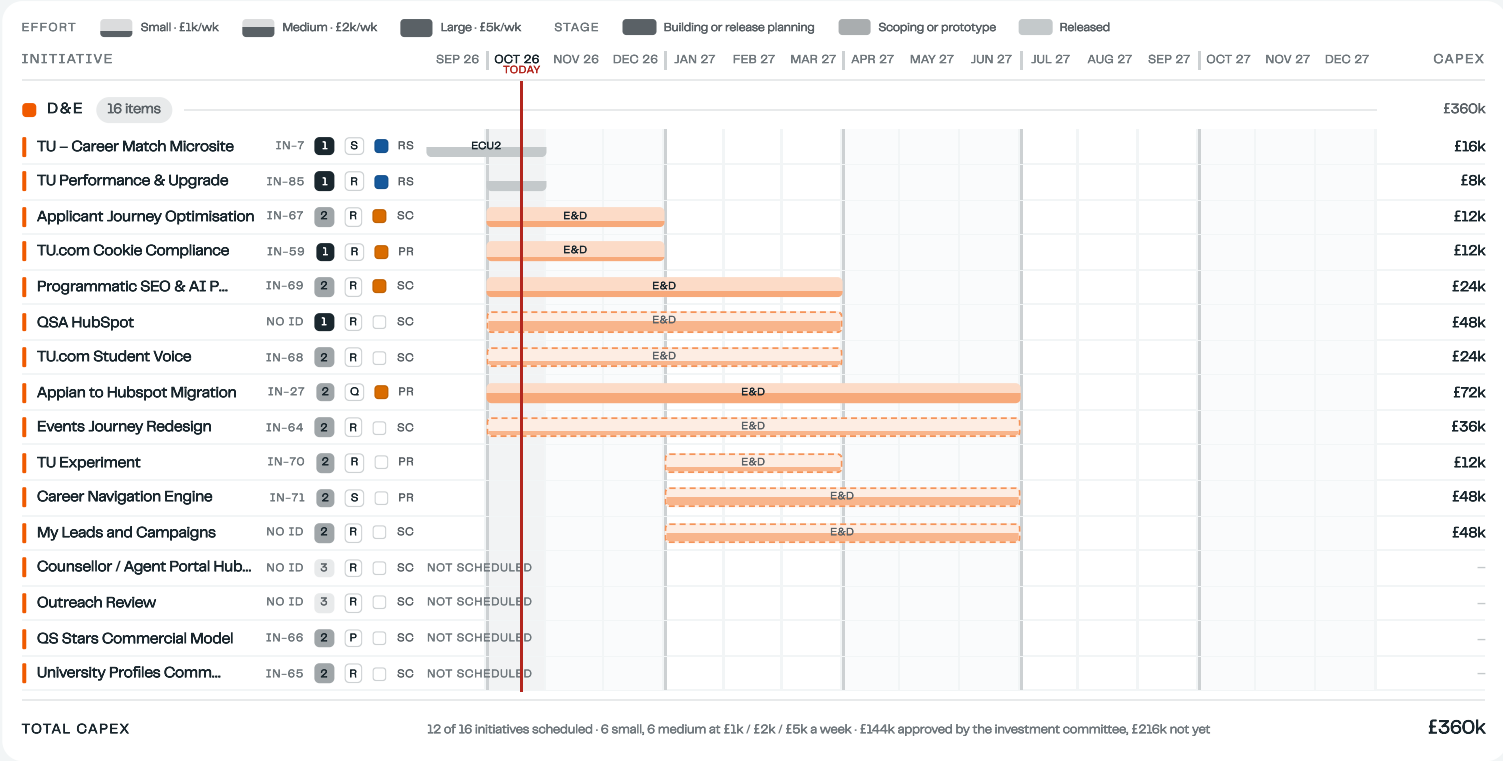

SECTION 6 OF 6

University Services

15 initiatives · delivery schedule

4 scoping
5 prototype
5 building
1 release planning

