Q3 – 2026 · WEEKS 33–41 · AUGUST TO OCTOBER 2026

2027 Data and Engineering Delivery Plan

Q3 – 2026 Patterns

What the weekly reports say when read together, rather than one week at a time. Every figure on the pages that follow is counted from the reports themselves.

Generated 19 October 2026 from the Week 33 to 41 reports · internal use

RECOMMENDATIONS

1 Close the standing risks, or accept them in writing

9 initiatives have carried a risk in two or more separate weeks, led by TU Performance & Upgrade, TU – Career Match Microsite, Appian to Hubspot Migration. A risk that survives a quarter of weekly reporting is not being managed by the report; give each one an owner and a date, or record it as accepted.

2 Reconcile the plan with what is actually moving

12 initiatives are inside their build window but have appeared in at most one weekly report — MyQS Infra, QAS Prowler – 365 AI Pen Testing, MyQS Engine. Either the work has not started, or it is not being reported. Both are worth knowing before the next committee.

3 Put the unapproved build in front of the investment committee

31 initiatives are in build without approval, carrying £3.7m of pod cost against £2.6m approved. This is spend already in motion; approve it, stop it, or stage it.

4 Name the off-plan work

340 of 576 delivery items across the quarter (59%) could not be tied to an initiative, concentrated in CX Systems and Digital and Events. Give the recurring ones an initiative number so the plan reflects the real workload.

5 Spread the single points of ownership

Patrick Brothers carries 27 initiatives and David Paterson 27. The quarter leans on a handful of people; succession for those two is the cheapest resilience available.

6 Protect what has momentum

12 initiatives reported in five or more weeks, led by MyQS Design System, 1 Mentor IBM, QAS Stars. These are the ones with real cadence — guard their teams from reallocation before the quarter closes.

Contents

Recommendations 3
Persistent risks 4
Momentum and inertia 5
Concentration 6
Funding exposure 7
Work off the plan 8
Engineering activity 9

Read across weeks 33 to 41, 8 published reports. Each one follows from a pattern in the pages that follow.

1 Close the standing risks, or accept them in writing

9 initiatives have carried a risk in two or more separate weeks, led by TU Performance & Upgrade, TU – Career Match Microsite, Appian to Hubspot Migration. A risk that survives a quarter of weekly reporting is not being managed by the report; give each one an owner and a date, or record it as accepted.

2 Reconcile the plan with what is actually moving

12 initiatives are inside their build window but have appeared in at most one weekly report — MyQS Infra, QAS Prowler – 365 AI Pen Testing, MyQS Engine. Either the work has not started, or it is not being reported. Both are worth knowing before the next committee.

3 Put the unapproved build in front of the investment committee

31 initiatives are in build without approval, carrying £3.7m of pod cost against £2.6m approved. This is spend already in motion; approve it, stop it, or stage it.

4 Name the off-plan work

340 of 576 delivery items across the quarter (59%) could not be tied to an initiative, concentrated in CX Systems and Digital and Events. Give the recurring ones an initiative number so the plan reflects the real workload.

5 Spread the single points of ownership

Patrick Brothers carries 27 initiatives and David Paterson 27. The quarter leans on a handful of people; succession for those two is the cheapest resilience available.

6 Protect what has momentum

12 initiatives reported in five or more weeks, led by MyQS Design System, 1 Mentor IBM, QAS Stars. These are the ones with real cadence — guard their teams from reallocation before the quarter closes.

A risk that keeps coming back is a decision that has not been taken. These carried across the quarter, newest wording shown.

TU Performance & Upgrade
IN-85 · WEEKS 33, 34, 36, 37

Angular upgrade: new servers testing continues. Drupal upgrade: waiting for the new environment setup for the last round of testing.

TU – Career Match Microsite
IN-7 · WEEKS 33, 35, 36, 37

Microsite moving to urgent-only mode. Starting next week, the Microsite pod addresses only urgent and priority items; no further general feature work is queued.

Appian to Hubspot Migration
IN-54 · WEEKS 36, 37, 38

Contact Matching unavailable in Sandbox: issues promoting data from production to sandbox due to missing data objects. Tag data ingestion: need to agree how tag data should be ingested so it loads correctly...

Decommission Informatica
IN-88 · WEEKS 36, 37, 38

Informatica will not be renewed. Procurement has been notified of the decision not to renew. LSBU is paused: its S3 flat-file replacement is on hold pending tender outcome.

QAS Auth
IN-43 · WEEKS 33, 34, 35

User load needs QA and sign-off. The identity load is applied with minor loose ends still to close; it needs a QA pass and formal sign-off before it can be called done.

Partnerships New
IN-16 · WEEKS 34, 35, 37

QPD back-office is inaccessible on live. Decision needed on where this will live.

Strengthen Cyber Security
IN-80 · WEEKS 37, 38

Box platform constraints. Discovery sessions continue to reinforce that Box configurations and business processes are highly interconnected. This may significantly limit the security controls that can be...

QAS Stars
IN-46 · WEEKS 33, 37

QAS Stars data copy. Decision needed on how data copy will be handled on the new QAS Stars stack.

HIQ – QAS Auth Migration
IN-20 · WEEKS 33, 34

HolonIQ needs connecting to QAS Pulse. Now that HolonIQ is in production, its events still need to reach the Pulse pipeline.

2027 Data and Engineering Delivery Plan

Counted as the number of separate weekly reports an initiative appeared in. On the right, initiatives inside their build window that the reports have barely mentioned.

MOMENTUM · REPORTED IN FIVE WEEKS OR MORE

MyQS Design System	IN-26 · 8 WEEKS
1 Mentor IBM	IN-19 · 7 WEEKS
QAS Stars	IN-46 · 7 WEEKS
TU Performance & Upgrade	IN-85 · 7 WEEKS
Appian to Hubspot Migration	IN-54 · 6 WEEKS
QAS Auth	IN-43 · 6 WEEKS
Partnerships New	IN-16 · 6 WEEKS
TU – Career Match Microsite	IN-7 · 6 WEEKS
Strengthen Cyber Security	IN-80 · 5 WEEKS
MyQS CX - Ph 2	IN-87 · 5 WEEKS
Decommission Informatica	IN-88 · 5 WEEKS
MyQS Cerebrum	IN-32 · 5 WEEKS

INERTIA · IN BUILD, SILENT

MyQS Infra	IN-78 · NO UPDATES
QAS Prowler – 365 AI Pen Testing	IN-90 · NO UPDATES
MyQS Engine	IN-76 · NO UPDATES
QSA HubSpot	NO ID · NO UPDATES
QAS Data Collection – Rankings	IN-21 · 1 WEEK
Analytics: Downloads for ...	IN-61 · 1 WEEK
Events Journey Redesign	IN-64 · 1 WEEK
Applicant Journey Optimisation	IN-67 · 1 WEEK
TU.com Student Voice	IN-68 · 1 WEEK
Programmatic SEO & AI P...	IN-69 · 1 WEEK
TU.com Cookie Compliance	IN-59 · 1 WEEK
Aurora – Student Scoring Model	IN-56 · 1 WEEK

Who the plan depends on, and which teams carry the reported delivery. Both are counted from the plan and the reports, not from headcount.

INITIATIVES PER PRODUCT LEAD

Patrick Brothers	27 INITIATIVES
David Paterson	27 INITIATIVES
Natalie	16 INITIATIVES
Selma	11 INITIATIVES
Leigh Kamolins	7 INITIATIVES
Michael Morgan	7 INITIATIVES
Martí Serrano	5 INITIATIVES
Ian Lynes	2 INITIATIVES
Liron	1 INITIATIVES
Susie Knight	1 INITIATIVES
Monica Hornumg Cawtan	1 INITIATIVES

DELIVERY ITEMS REPORTED PER TEAM

Digital and Events	52 ITEMS
CX Systems	50 ITEMS
QS Application System	44 ITEMS
SYD1	40 ITEMS
MoveIN	33 ITEMS
Cyber	28 ITEMS
BLR2	24 ITEMS
BLR1	22 ITEMS
MoveON	22 ITEMS
UBS Development	20 ITEMS
ECU2	20 ITEMS

2027 Data and Engineering Delivery Plan

Funding exposure £3.7m unapproved

31 initiatives are building now without investment approval, carrying £3.7m of pod cost against £2.6m that has it.

UNAPPROVED BUILD BY PORTFOLIO

Data	25 · £3.0M
D&E	3 · £420K
University Services	2 · £200K
Core	1 · £120K

LARGEST UNAPPROVED COMMITMENTS

Events Journey Redesign	IN-64 · £180K
QAS Data Collection – Rankings	IN-21 · £120K
TU.com Student Voice	IN-68 · £120K
Decommission Informatica	IN-88 · £120K
QSA HubSpot	NO ID · £120K
Taxonomies, Student Flows & Employability	NO ID · £120K
OnePerson & Student Data Transformation	NO ID · £120K
Data Platform Governance & Migration	NO ID · £120K
ENROL & Unified Modelling	NO ID · £120K
Aurora / Synergy2 / UBS Data Quality	NO ID · £120K
Data-Led Engagement Pilot (University of London)	NO ID · £120K
Client Reporting Portal (Power BI)	NO ID · £120K

2027 Data and Engineering Delivery Plan

340 of 576 delivery items across the quarter could not be tied to an initiative. Where the same item comes back week after week, the plan is missing a line.

UNLINKED DELIVERY BY TEAM


CX Systems	49 ITEMS
Digital and Events	37 ITEMS
MoveON	22 ITEMS
SYD1	20 ITEMS
BLR1	19 ITEMS
MoveIN	18 ITEMS
Infrastructure	17 ITEMS
QS Application System	17 ITEMS
D&E	14 ITEMS
UBS	13 ITEMS
Cerebrum	12 ITEMS
ECU2	12 ITEMS

THE SAME WORK, THREE WEEKS OR MORE

Agenda builder	DIGITAL AND EVENTS · 8 WEEKS
HUB1	BLR1 · 6 WEEKS
Aircall	CX SYSTEMS · 6 WEEKS
Sakari	CX SYSTEMS · 6 WEEKS
HUB2	BLR1 · 5 WEEKS
Niswey	CX SYSTEMS · 4 WEEKS
MoveON	INFRASTRUCTURE · 4 WEEKS
MoveIN	INFRASTRUCTURE · 4 WEEKS
CMT module conversion from React to Drupal	DIGITAL AND EVENTS · 4 WEEKS
QS Events	CX SYSTEMS · 3 WEEKS
SIP	CX SYSTEMS · 3 WEEKS
GME rankings	DIGITAL AND EVENTS · 3 WEEKS

Productivity Heatmap NOV 24 – OCT 26

Lines of code committed a day.

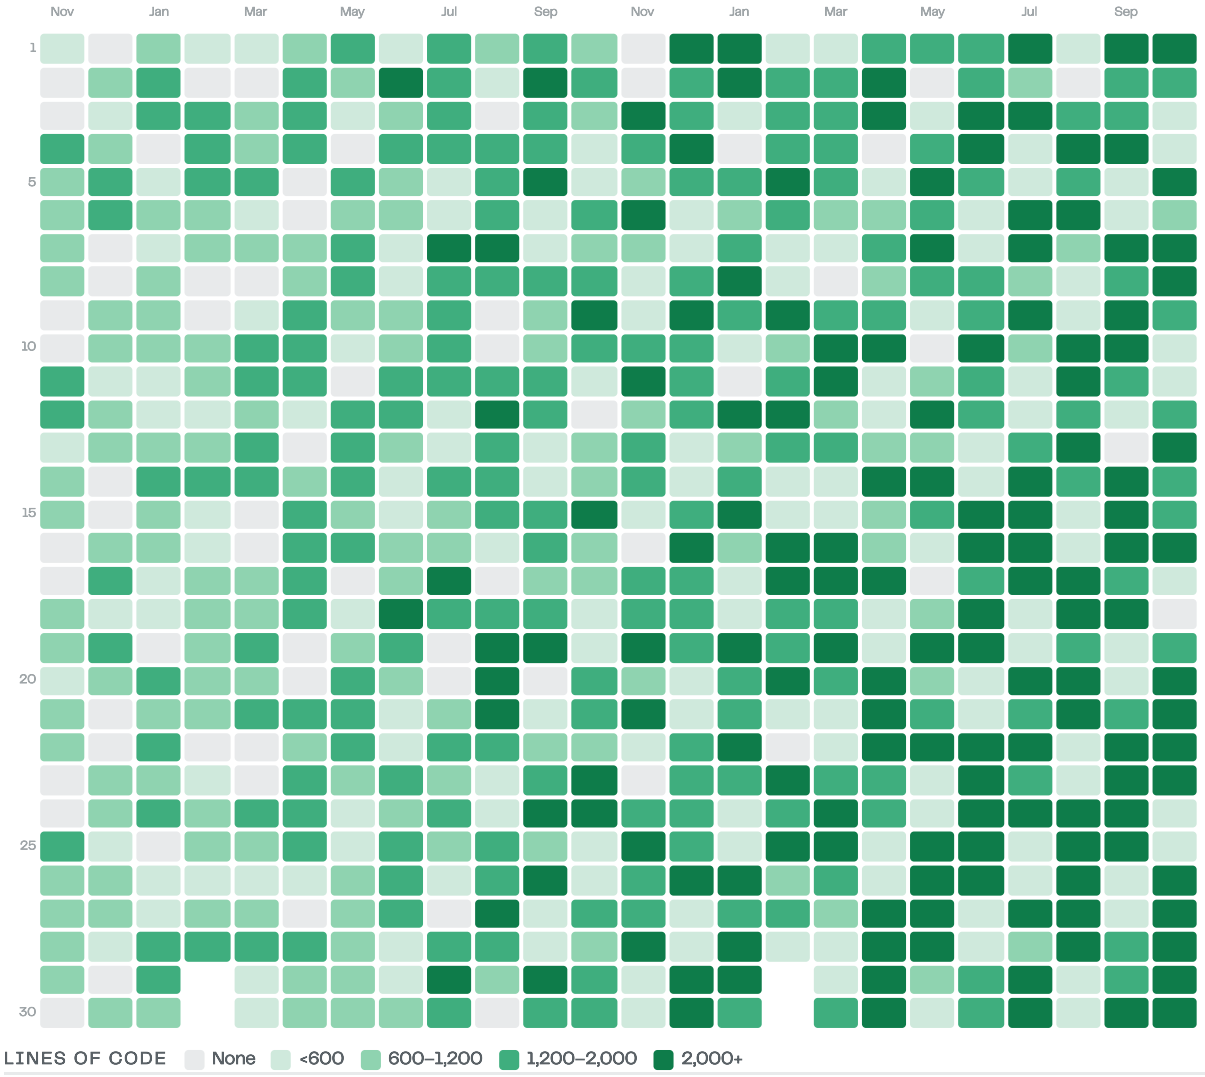

AI Code Intensity NOV 24 – OCT 26

Share of committed code written by AI.

