WEEK 33 · 10–15 AUGUST 2026

2027 Data and Engineering Delivery Plan

Week 33 Delivery Report

What moved this week, initiative by initiative, with the delivery schedule it sits in.

Cyber & Infra · Data · Core · Sector Intelligence · D&E · University Services

THE WEEK AT A GLANCE

Cyber & Infra 2 UPDATES

Outcomes. Infrastructure reported work with no initiative behind it. MoveIN: Investigated Elasticsearch indexing and Memcached eviction issues, with configuration changes applied.

Risks & decisions. MoveON downtime. Downtime was encountered owing to a disk failure on the MoveON Telemaxx hosting. VM migration to shared storage has been implemented and a RAID rebuild begun. D&E patching budget.

Core 5 INITIATIVES

Outcomes. 5 initiatives moved, led by HIQ – QAS Auth Migration, MyQS Cerebrum, QAS Auth. Migration work is complete in dev. Behind: the production deployment is still outstanding.

Risks & decisions. HIQ – QAS Auth Migration: HolonIQ to QAS migration. Finished in dev but not deployed to production. QAS Auth: the global profile-completion flow is not live.

Sector Intelligence 3 INITIATIVES

Outcomes. 3 initiatives moved, led by QAS Stars, 1 Mentor IBM, Partnerships New. Shipped all P1/P2 text changes (IPS-2317, IPS-2332), the route rename (stars-new to stars), an accordion responsiveness fix and brand colour updates. The Stars dashboard is now production-ready.

Risks & decisions. QAS Stars: some category tabs (Online Learning, Subject Ranking and others) show as 'Not validated' in Snowflake and are filtered out; the data team must confirm before QA sign-off. 1 Mentor IBM: IBM SSO integration.

D&E 2 INITIATIVES

Outcomes. 2 initiatives moved, led by TU – Career Match Microsite, TU Performance & Upgrade. Significantly expanded the data behind Career Matcher, enabling more precise matches across a broader range of careers. In the testing stage of the upgrade, with bug fixing of issues reported.

Risks & decisions. TU – Career Match Microsite: Limited new feature work. The microsite is essentially feature complete; the team is waiting for the next priority, such as Alumni Insights, or new requirements from Product. TU Performance & Upgrade: Angular upgrade.

University Services 1 INITIATIVE

Outcomes. 1 initiatives moved, led by Aurora Data Integrity. V2 fixes the issues inherent in the contact matching created by Huble. Throughput speed is massively enhanced and duplication issues are removed. This will now be rolled out to all portals.


Risks & decisions. Aurora Data Integrity: Missing data from migration files. The BI team missed contacts and Course of Interest (COI) objects in their alpha and delta extracts; work is under way to find what is missing and update all portals. Missing data from migration files.


Contents

Delivery schedule 3
Engineering activity 4
Cyber & Infra 5
Core 7
Sector Intelligence 10
D&E 14
University Services 16

2027 Data and Engineering Delivery Plan


Delivery schedule 109 initiatives

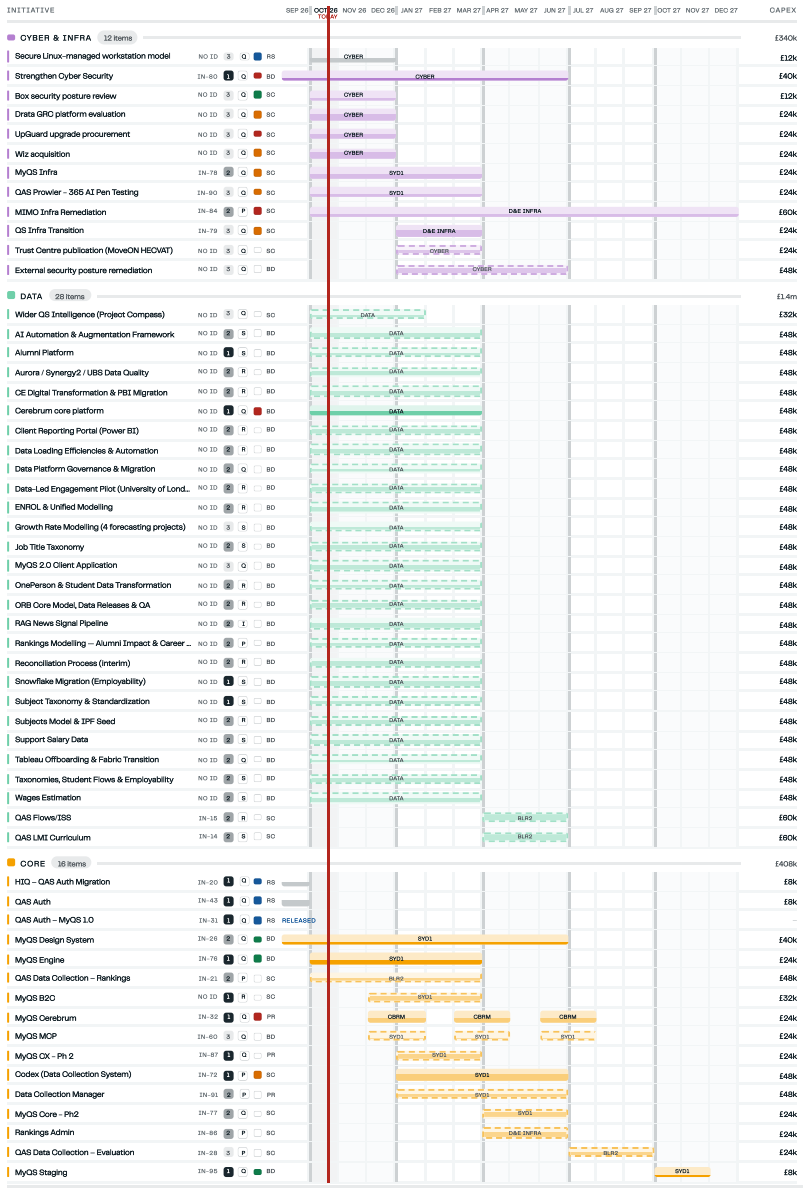

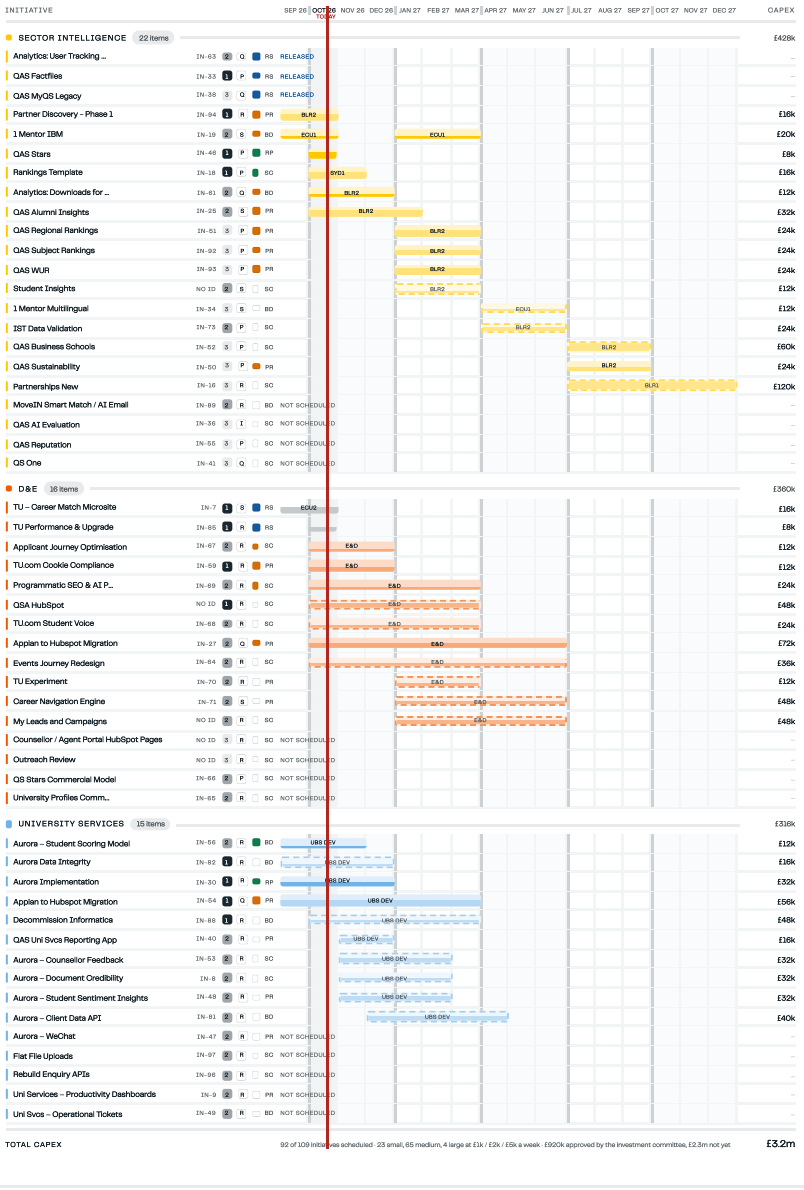


Productivity Heatmap NOV 24 – OCT 26

Lines of code committed a day.

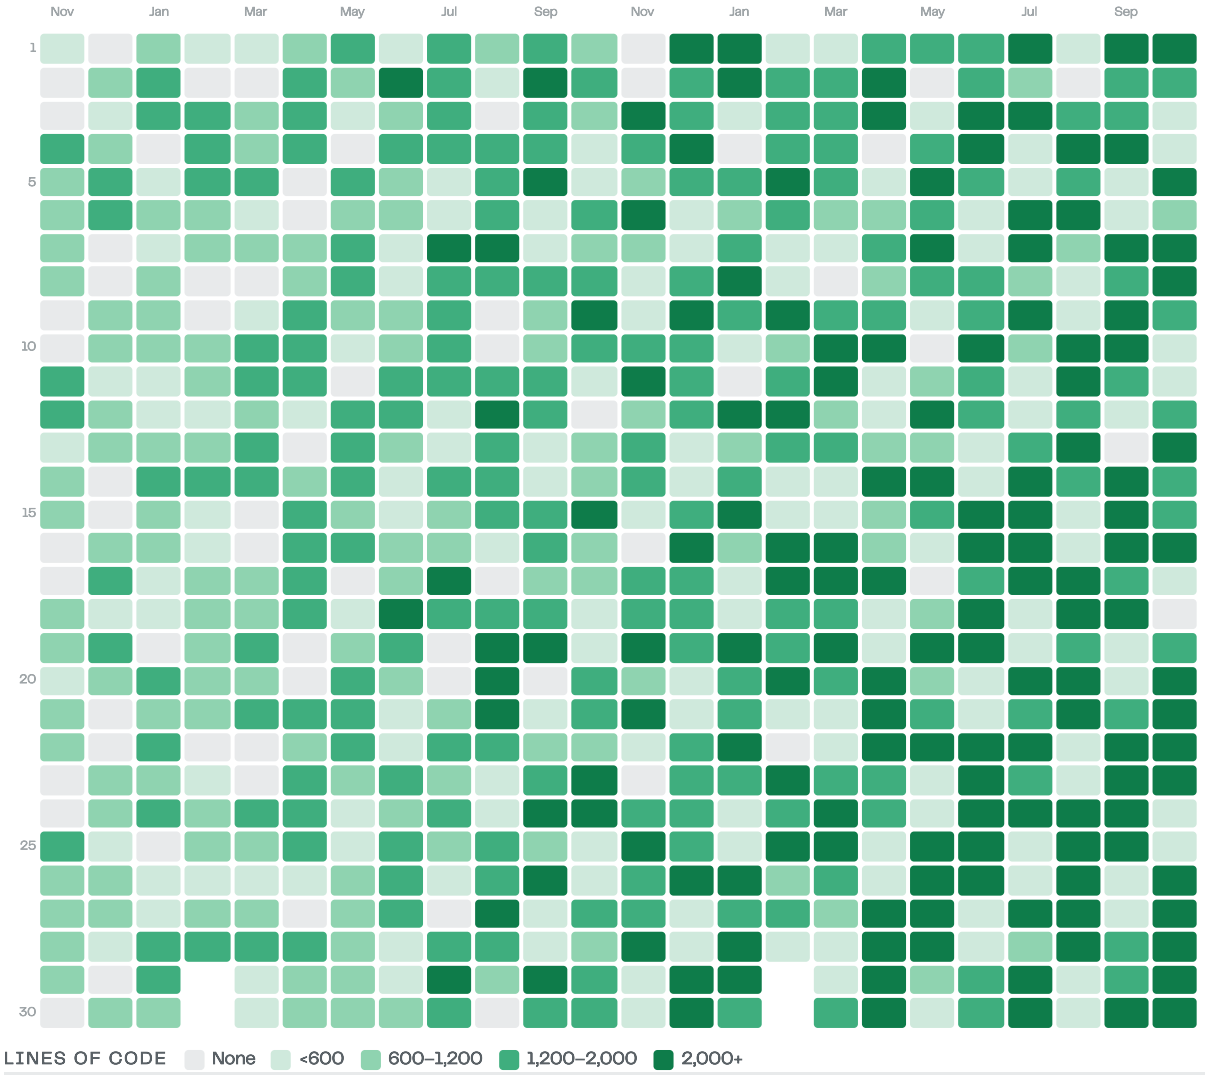

AI Code Intensity NOV 24 – OCT 26


Share of committed code written by AI.

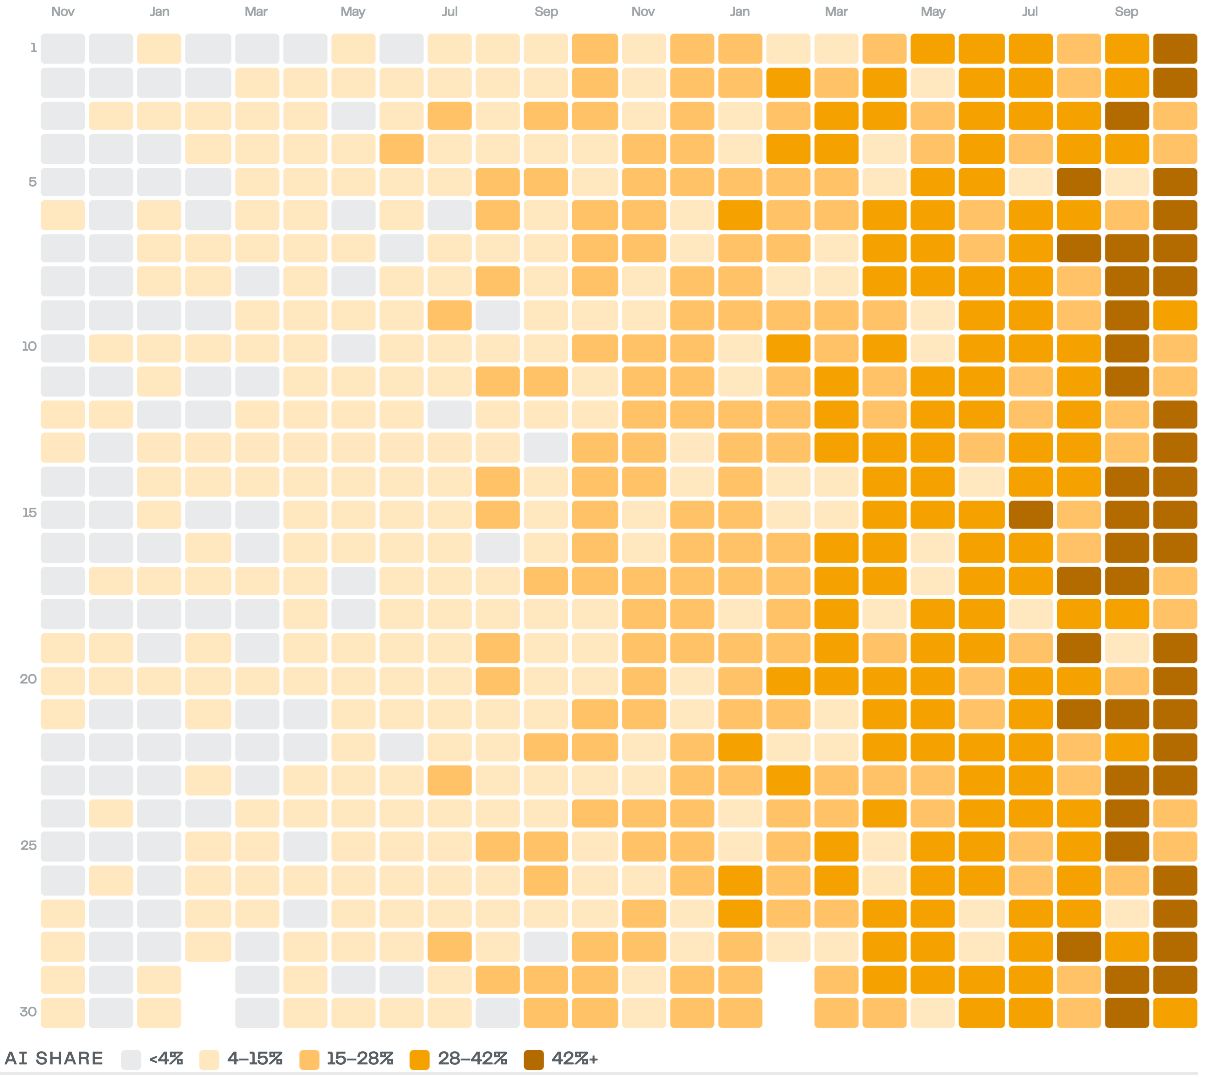

SECTION 1 OF 5

Cyber & Infra

2 teams reported

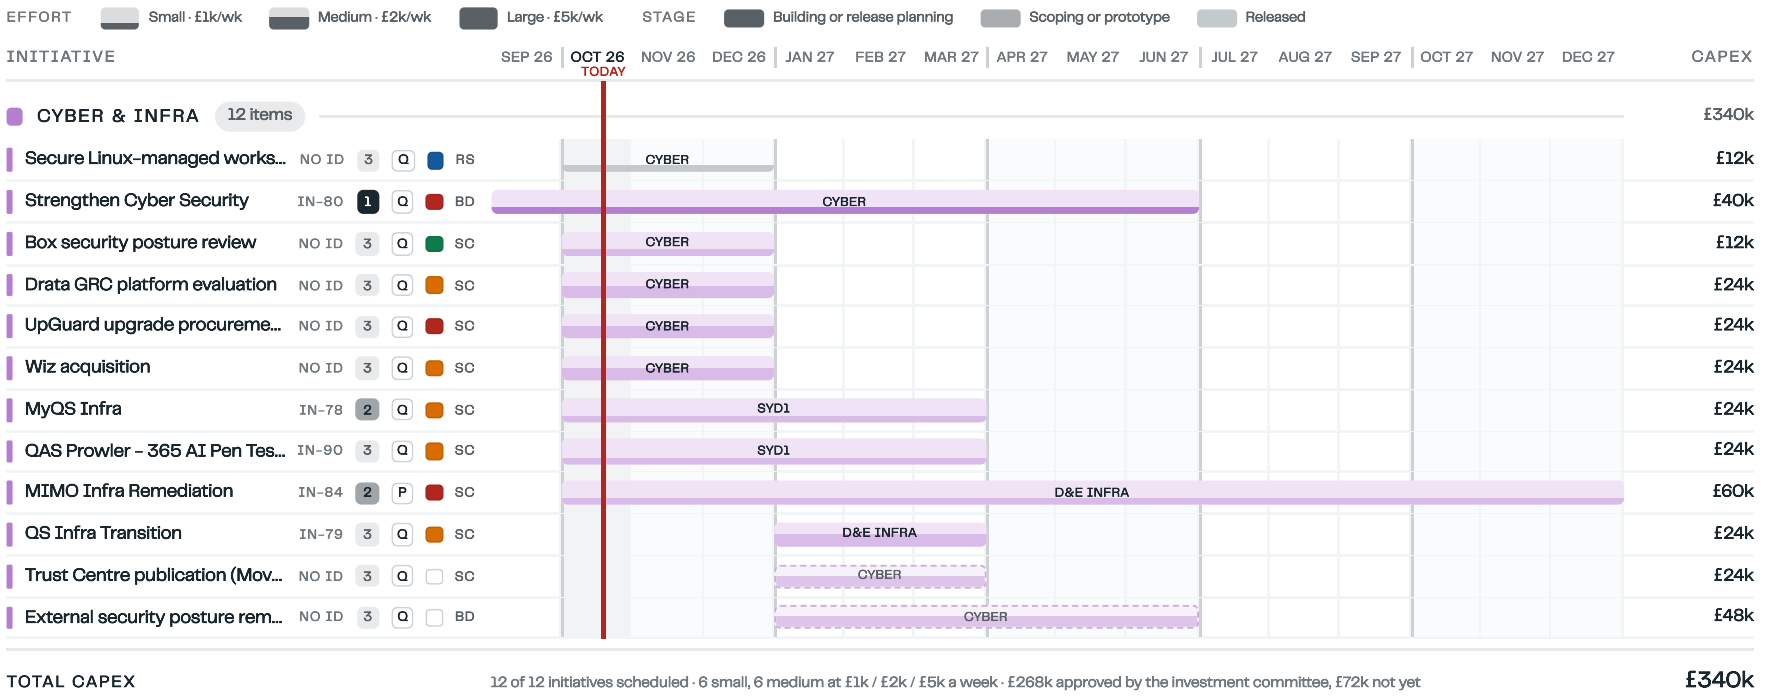

TOTAL CAPEX — 12 of 12 initiatives scheduled · 6 small, 6 medium at £1k / £2k / £5k a week · £268k approved by the investment committee, £72k not yet — £340k

Infrastructure

OTHER WORK · NOT LINKED TO AN INITIATIVE

MoveIN: Investigated Elasticsearch indexing and Memcached eviction issues, with configuration changes applied. MoveON: Applied August patches to the staging and demo environments. Resolved Jenkins pipeline and AP dev VM issues, and implemented SSL automation pipeline work on staging. Set up a new workflow for renewing SSL certificates; implementation for all SSL certificates across MoveON environments continues next week. TU and TM: Completed documentation for the Datadog monitoring updates in QSCHINA and reviewed Cloudflare metrics for TopUniversities. D&E: Updated the 'Auto Create Instance Check Alarms' Lambda for automatic deletion of old alarms.

Infrastructure

RISKS AND DECISIONS


Risks and decisions. MoveON downtime. Downtime was encountered owing to a disk failure on the MoveON Telemaxx hosting. VM migration to shared storage has been implemented and a RAID rebuild begun. D&E patching budget. Automox has been evaluated as a product for patching all D&E AWS account resources; awaiting budget approval from Patrick.

SECTION 2 OF 5

Core

5 initiatives reported

1 prototype
1 building
3 released

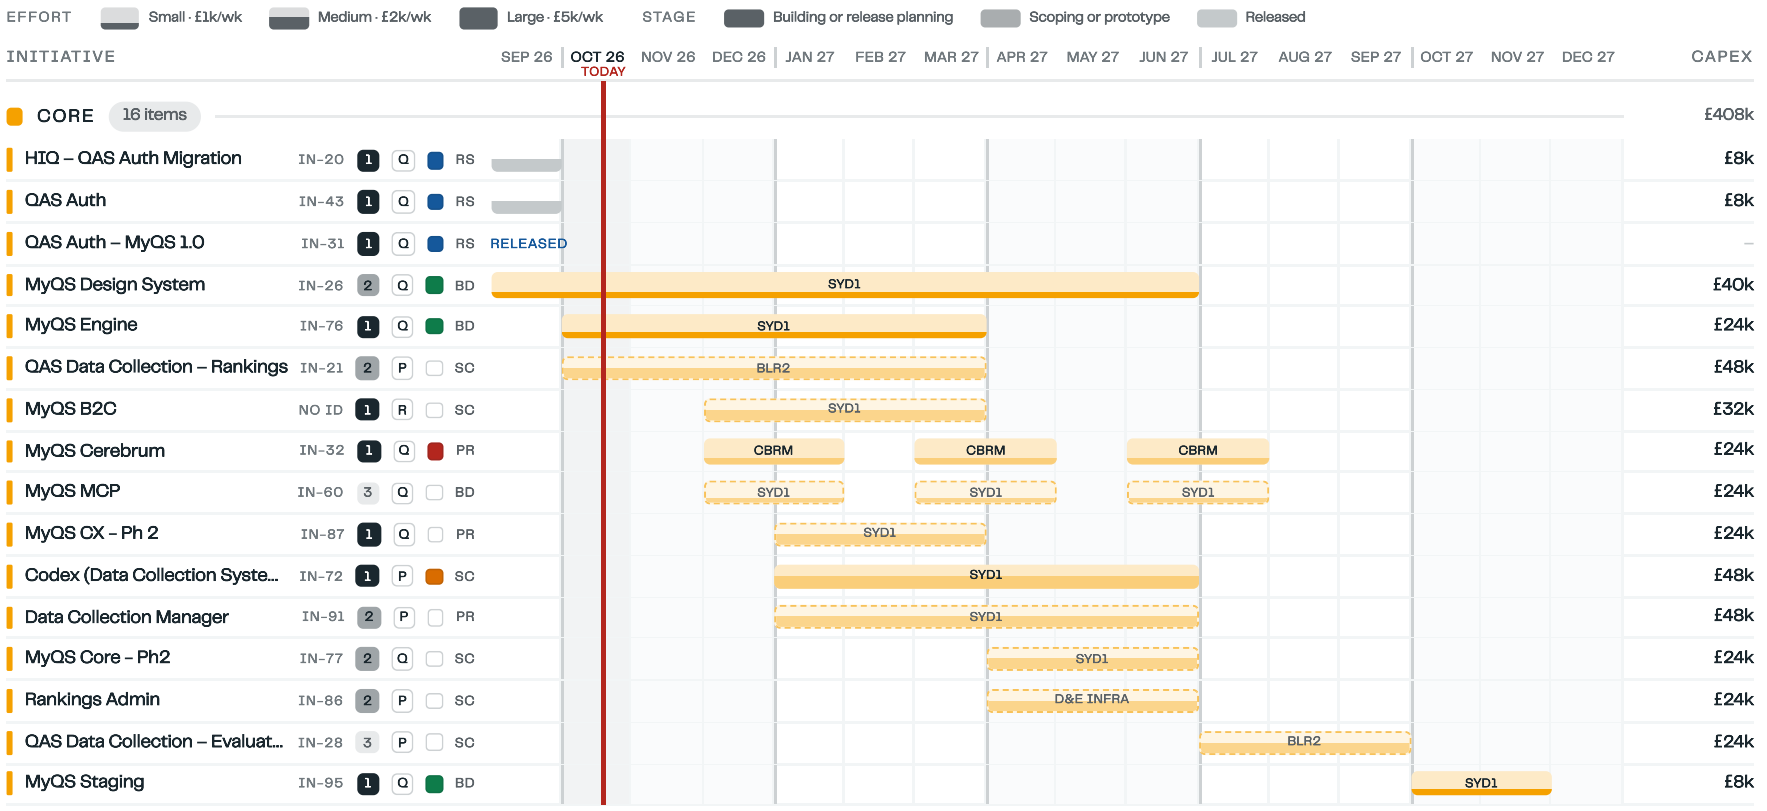

HIQ – QAS Auth Migration

IN-20 · SYD1 · CHARLIE LIU · SYD1 · RELEASED

Migration work is complete in dev. Behind: the production deployment is still outstanding.

Risks and decisions. HolonIQ to QAS migration. Finished in dev but not deployed to production.

MyQS Cerebrum

IN-32 · CEREBRUM · PROTOTYPE

Implemented the new QS_ID format QS_{ENTITY_TYPE}_{NANOID}{CHECK}, using Crockford Base32 with an appended check character for validation. Added an API endpoint for issuing QS_IDs, backed by a persistent ledger that guarantees each QS_ID is issued only once, and ENUM validation during data ingestion.

QAS Auth

IN-43 · SYD1 · CHARLIE LIU · SYD1 · RELEASED

Production Auth0 estate live on eu-west-2: auth.api.qs.com routes verified, SES sending from no-reply@my.qs.com, WebAuthn passkey and security-key factors enabled, and MFA enforcement moved to the QAS MFA Policy action. Auth-API now accepts QS platform-audience tokens and makes the current_account_id claim namespace deployment-configurable. Federation delivery stack parameterised over regions, with an eu-west-2 production target and per-region schema-release credential secrets; RFC 9068 client-credentials tokens accepted at the schema-release guard; qs.com origins allowed at the router; and the qas_application catalogue added and exposed in the auth subgraph, superseding product.subdomain.

Risks and decisions. the global profile-completion flow is not live. The compliance_log omit opens a front-end outage window that must be sequenced around the CX and MyQS releases.

QAS Auth – MyQS 1.0

IN-31 · BLR2 · RELEASED

Removed legacy ROLE references across the codebase to follow CX roles; integrated the QAS app launcher, replacing the custom implementation; and updated the header and sidebar UI to match the CX design.

MyQS Design System

IN-26 · SYD1 · CHARLIE LIU · BUILDING

2.0 landed, dropping Tailwind and Flowbite, then 2.0.2 to 2.0.14 shipped across the week: a configurable app-launcher base domain, a LegacyAppLauncher subpath entry, Auth0 audience and auth-API base URL made configurable, and atomic release pushes. With Caitlin: dropdown redesign, new table cell types, responsive grid and profile data, and the app visibility model. Adopted by MyQS, CX, RR, CBR and MyQS 1.0 Legacy.

QS Application System

OTHER WORK · NOT LINKED TO AN INITIATIVE

QS Auth · with Ming Shi: Production Auth0 estate live on eu-west-2: auth.api.qs.com routes verified, SES sending from no-reply@my.qs.com, WebAuthn passkey and security-key factors enabled, and MFA enforcement moved to the QAS MFA Policy action. Auth-API now accepts QS platform-audience tokens and makes the current_account_id claim namespace deployment-configurable. QS Supergraph · with Ming Shi: Federation delivery stack parameterised over regions, with an eu-west-2 production target and per-region schema-release credential secrets; RFC 9068 client-credentials tokens accepted at the schema-release guard; qs.com origins allowed at the router; and the qas_application catalogue added and exposed in the auth subgraph, superseding product.subdomain.

QS Application System

RISKS AND DECISIONS

Risks and decisions. compliance_log front-end outage. The supergraph omit is merged and Pulse's own plan records the outage window it opens; CX has already stripped ComplianceLog selections and rerun codegen. User onboarding is not ready. The global profile-completion flow is not live. UI tweaks still outstanding. Design feedback across the 2.0 surfaces is not closed out. HolonIQ to QAS migration. Finished in dev but not deployed to production.


Sector Intelligence 3 initiatives

SECTION 3 OF 5

Sector Intelligence

3 initiatives reported

1 scoping
1 building
1 release planning

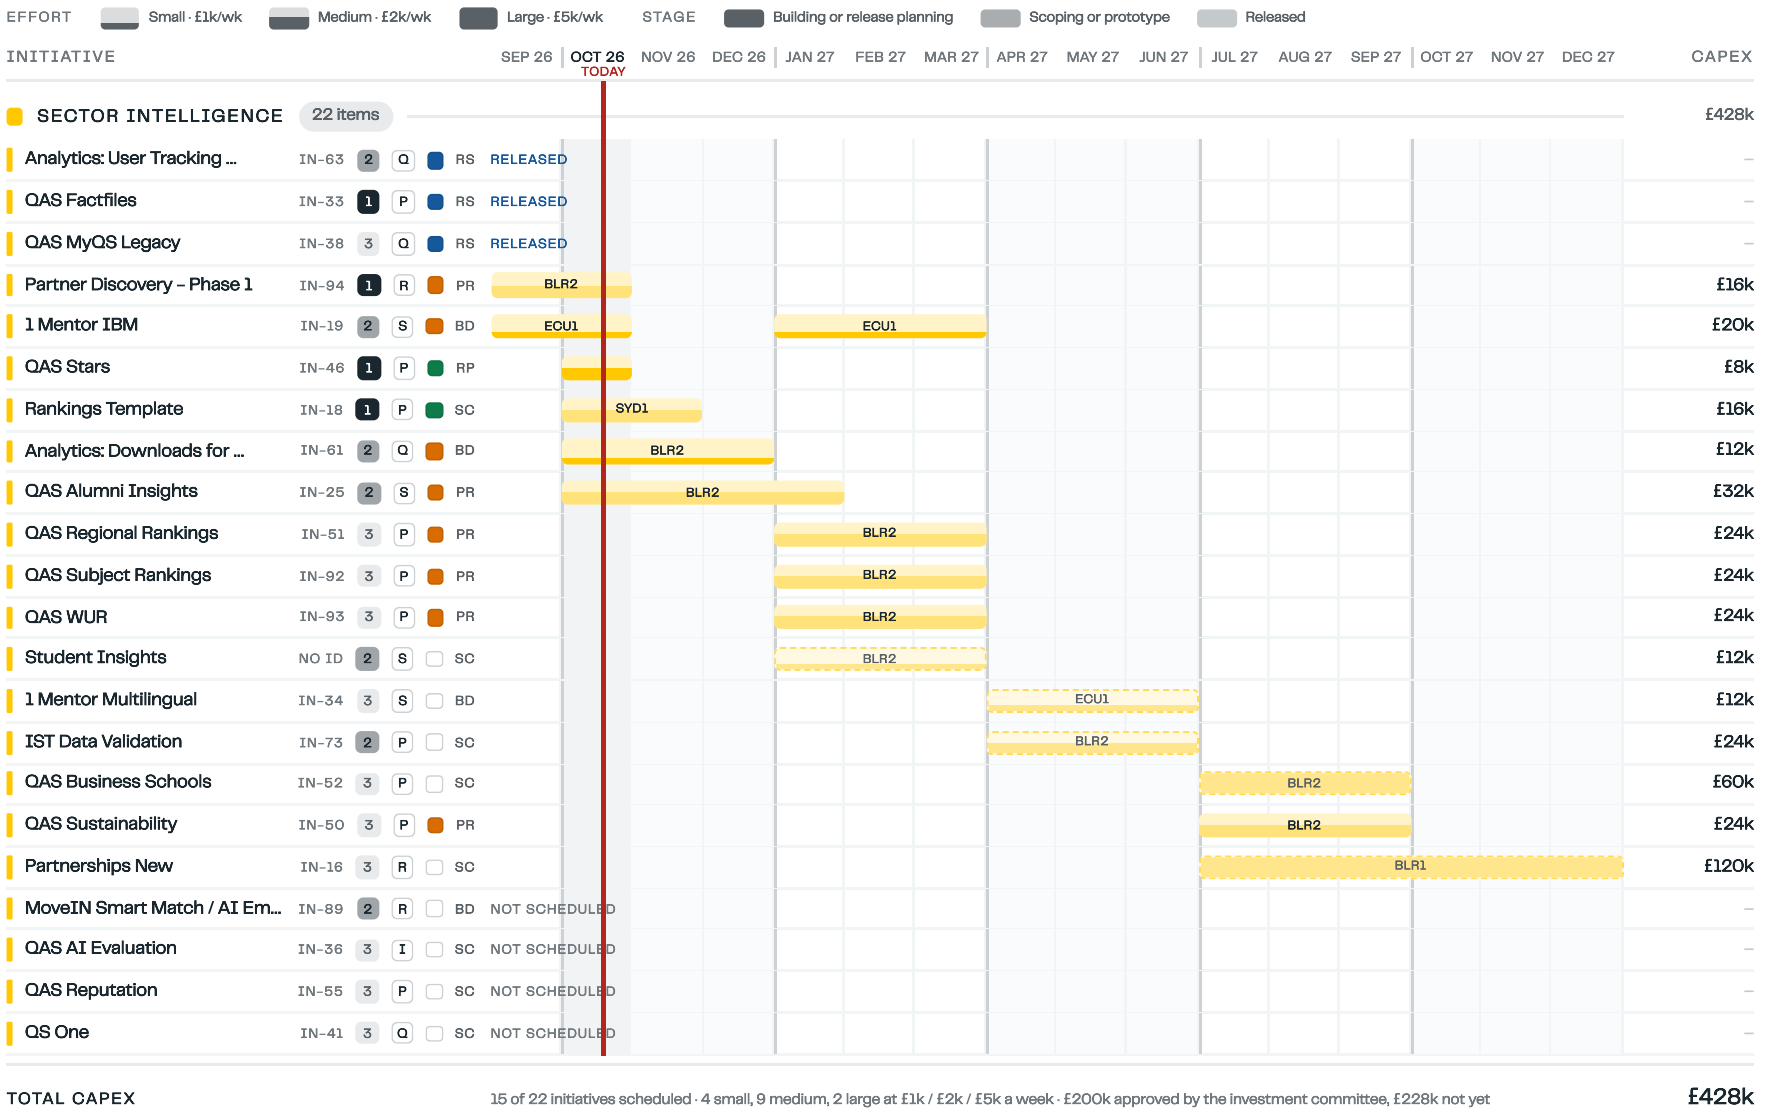

QAS Stars

IN-46 · BLR2 · RELEASE PLANNING

Shipped all P1/P2 text changes (IPS-2317, IPS-2332), the route rename (stars-new to stars), an accordion responsiveness fix and brand colour updates. The Stars dashboard is now production-ready.

Risks and decisions. some category tabs (Online Learning, Subject Ranking and others) show as 'Not validated' in Snowflake and are filtered out; the data team must confirm before QA sign-off. Decision needed on the still-public stars-legacy route: removal, redirect or a feature flag.

1 Mentor IBM

IN-19 · ECU1 · BUILDING

Risks and decisions. IBM SSO integration. The SSO integration and how to avoid duplicate Learner accounts remain unclear; a task is evaluating alternatives, which could even lead to development by IBM.

Partnerships New

IN-16 · BLR2 · BLR1 · SCOPING

Opportunity Management filters and status dots (IPS-2324) moved to QA. The docked chat UI (IPS-2350) has been built, targeting QA next week. Data modelling and APIs for messaging (IPS-2347) are in progress, with the polling approach confirmed. Planning to take on QPD tickets to support team capacity and help balance workload across the team.

BLR2

OTHER WORK · NOT LINKED TO AN INITIATIVE

MyQS Auth migration: Removed legacy ROLE references across the codebase to follow CX roles; integrated the QAS app launcher, replacing the custom implementation; and updated the header and sidebar UI to match the CX design. Stars: Shipped all P1/P2 text changes (IPS-2317, IPS-2332), the route rename (stars-new to stars), an accordion responsiveness fix and brand colour updates. Partner Discovery: Opportunity Management filters and status dots (IPS-2324) moved to QA. The docked chat UI (IPS-2350) has been built, targeting QA next week. Data modelling and APIs for messaging (IPS-2347) are in progress, with the polling approach confirmed. QA: Completed MyQS sprint regression testing. No live deployment this sprint owing to the new Auth implementation.

BLR1

OTHER WORK · NOT LINKED TO AN INITIATIVE

HUB 2 – Media Partners for Outreach · IPS-2220, IPS-2341: Completed analysis and aligned on a solution approach that reduces development effort and user impact. HUB 1 project setup: The team completed knowledge transfer, Git and Docker setup, and application onboarding; sample data population is in progress (cross-training from the one contractor developer to QS developers). MyQS QPD: Planning to take on QPD tickets to support team capacity and help balance workload across the team.

ECU1

OTHER WORK · NOT LINKED TO AN INITIATIVE

Refactor of legacy code: Reduced the number of lines of code in the 1M project to enable Sonar to perform quality, accessibility and security analysis more aligned with standards. Career Trends: Two CTAs will be added: additional locations on the Advisor platform will include the option to request new features for the sales team. Learning Path to academic programme matching: Allows a Learning Path to be assigned directly to the Learner based on their academic programmes, consistently recommending resources relevant to their goals.

ECU2

OTHER WORK · NOT LINKED TO AN INITIATIVE

Career recommendation accuracy: Significantly expanded the data behind Career Matcher, enabling more precise matches across a broader range of careers. Site navigation and footer: Fixed navigation and footer issues affecting overall site usability. Accessibility compliance: Completed accessibility improvements and added automated checks to help prevent future regressions. Site speed: Restructured page loading to improve performance, especially on the first visit. Hosting and deployment upgrade: Upgrading the tools used to build and deploy the site. Stability issues were encountered that required several same-day emergency fixes to keep deployments working.

BLR2

RISKS AND DECISIONS

Risks and decisions. Stars blocker. Some category tabs (Online Learning, Subject Ranking and others) show as 'Not validated' in Snowflake and are filtered out. If QA flags these, the root cause is data or configuration, not the front end. Confirmation is needed from the data team before QA sign-off. Decision needed. The Stars legacy route (stars-legacy) is still publicly accessible. A decision is needed on removal, redirect or a feature flag to avoid user confusion.

BLR1

RISKS AND DECISIONS

Risks and decisions. Dependency on Outreach API integration. Full end-to-end delivery of HUB 2 remains dependent on the Outreach team adopting the updated Media Partners APIs.

ECU1

RISKS AND DECISIONS

Risks and decisions. QA capacity for 1M certification. Certification of the 1M production environment was estimated at three days with three QAs; with only one QA now available, more days may be required. To mitigate this, the Cypress automation project will be used to detect more critical errors and reduce QA time. IBM SSO integration. The IBM project was discussed this week, but the SSO integration and how to avoid duplicate Learner accounts remain unclear.

ECU2

RISKS AND DECISIONS

Risks and decisions. Limited new feature work. The microsite is essentially feature complete. The team is waiting for the next priority, such as Alumni Insights, or for new feature and design requirements from Product; if another team needs support, they can also help there.


2027 Data and Engineering Delivery Plan

SECTION 4 OF 5

D&E

2 initiatives reported

2 released

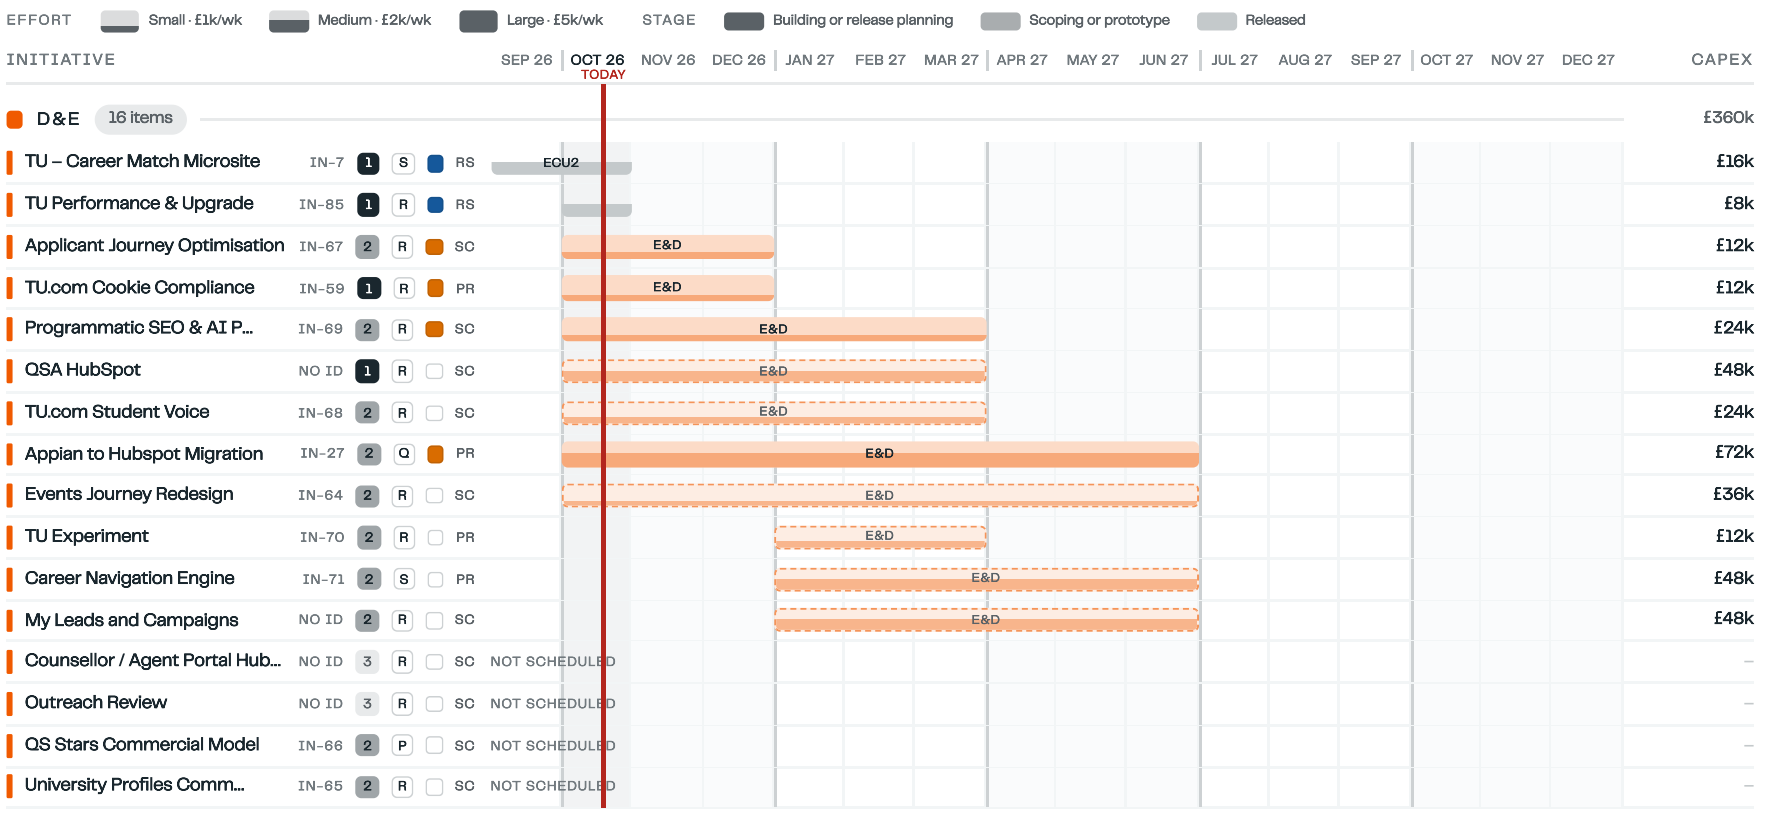

TOTAL CAPEX — 12 of 16 initiatives scheduled · 6 small, 6 medium at £1k / £2k / £5k a week · £144k approved by the investment committee, £216k not yet — £360k

TU – Career Match Microsite

IN-7 · ECU2 · DIGITAL AND EVENTS · RELEASED

Significantly expanded the data behind Career Matcher, enabling more precise matches across a broader range of careers. Fixed navigation and footer issues affecting overall site usability. Completed accessibility improvements and added automated checks to help prevent future regressions. Restructured page loading to improve performance, especially on the first visit. Upgrading the tools used to build and deploy the site. Stability issues were encountered that required several same-day emergency fixes to keep deployments working. Completed a batch of homepage and lead capture form content and layout updates. Backend work completed, including last sprint's requirement changes. Frontend work is ongoing as expected.

Risks and decisions. Limited new feature work. The microsite is essentially feature complete; the team is waiting for the next priority, such as Alumni Insights, or new requirements from Product.

TU Performance & Upgrade

IN-85 · DIGITAL AND EVENTS · RELEASED

In the testing stage of the upgrade, with bug fixing of issues reported.

Risks and decisions. Angular upgrade. A substantial change that needs a lot of testing, with the events season approaching; it should ideally be released before the season starts.

Digital and Events

OTHER WORK · NOT LINKED TO AN INITIATIVE

Career Matcher: Backend work completed, including last sprint's requirement changes. Frontend work is ongoing as expected. Quick Wins: Custom forms changes have been completed and are ready for next week's release. CMT module conversion from React to Drupal: In the testing stage of the conversion, fixing any issues reported during testing. QSA page and form: Reported data issues are fixed and breadcrumbs added as requested; ready for next week's release. Angular upgrade: In the testing stage of the upgrade, with bug fixing of issues reported. Agenda builder: Implementing the last requirements phase, with testing happening in parallel.

Digital and Events

RISKS AND DECISIONS


Risks and decisions. Angular upgrade. This is a substantial change that requires a lot of testing, and the events season is approaching. It should ideally be released before the season starts. Drupal upgrade. Major code development needs to be on hold while all developers upgrade their local environments and all issues are fixed. DevOps team availability will also be needed, so a plan is now being aligned with them to make sure the team is fully prepared.

SECTION 5 OF 5

University Services

1 initiative reported

1 building

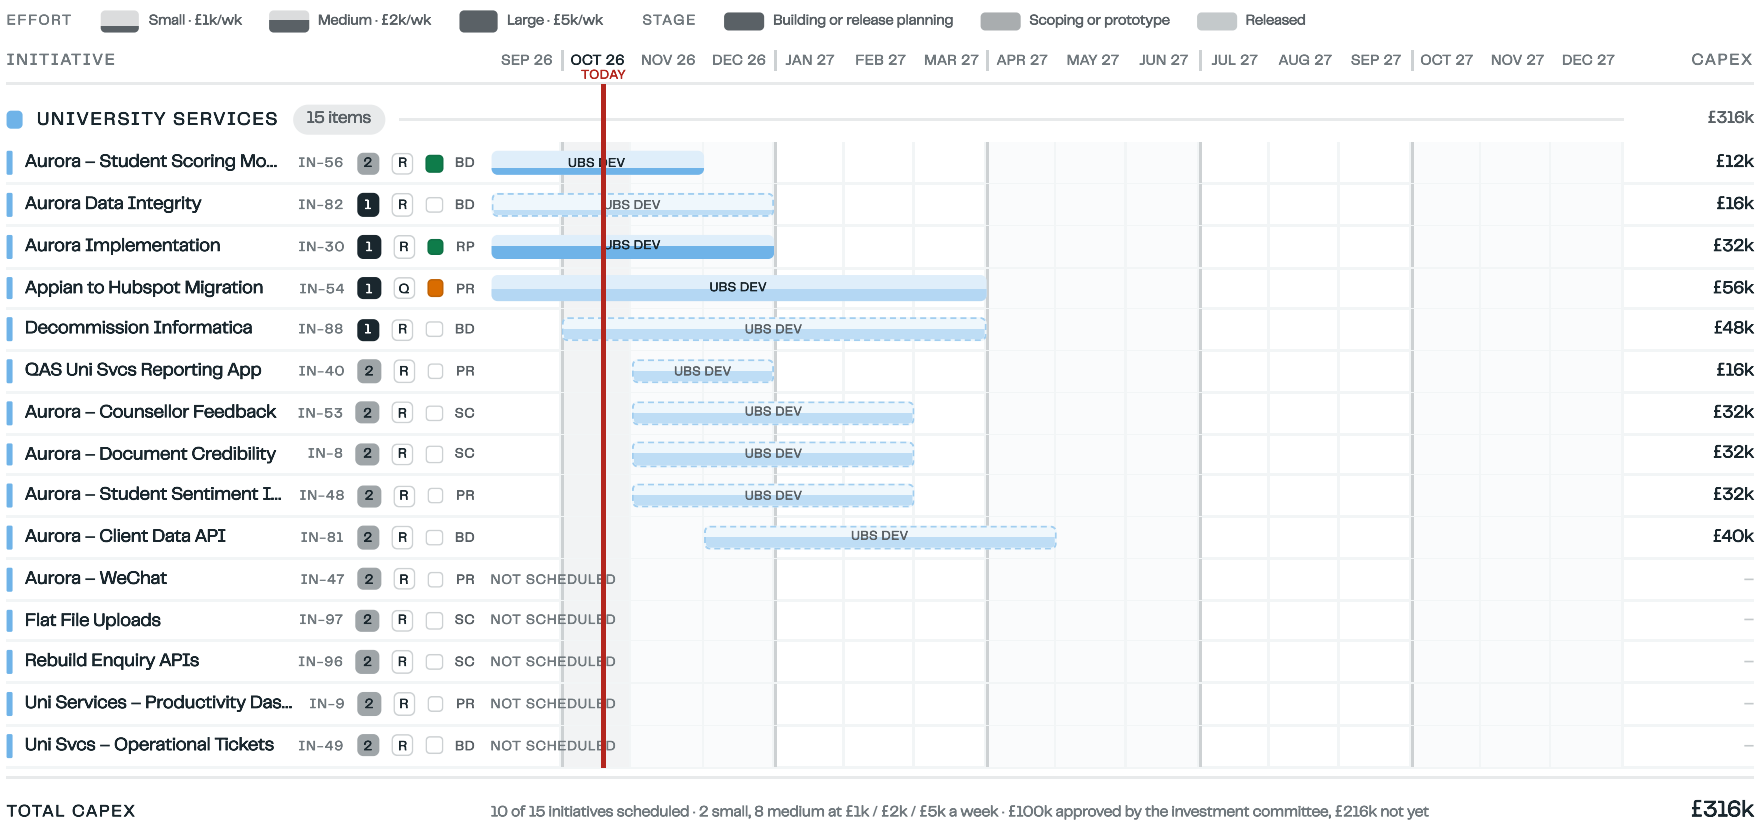

TOTAL CAPEX — 10 of 15 initiatives scheduled · 2 small, 8 medium at £1k / £2k / £5k a week · £100k approved by the investment committee, £216k not yet — £316k

Aurora Data Integrity

IN-82 · UNIVERSITY SERVICES · SIMON PENNINGTON · UNIVERSITY SERVICES · BUILDING

V2 fixes the issues inherent in the contact matching created by Huble. Throughput speed is massively enhanced and duplication issues are removed. This will now be rolled out to all portals.

Risks and decisions. Missing data from migration files. The BI team missed contacts and Course of Interest (COI) objects in their alpha and delta extracts; work is under way to find what is missing and update all portals.

University Services

OTHER WORK · NOT LINKED TO AN INITIATIVE

Data ingestion workflows: New workflows take raw data files, map the fields, rank the statuses and create contacts and COI objects automatically. This reduces the human checking needed to just records on review, and cuts around five hours from producing the required HubSpot objects. V2 contact matching: V2 fixes the issues inherent in the contact matching created by Huble. Throughput speed is massively enhanced and duplication issues are removed. This will now be rolled out to all portals. Marketing contact management: New workflows and rules have been created to manage the marketing contacts in HubSpot.

University Services

RISKS AND DECISIONS

Risks and decisions. Missing data from migration files. The BI team have found that they missed contacts and Course of Interest (COI) objects in their alpha and delta extracts. Work is under way to establish what is missing and get it updated in all portals.
