WEEK 35 · 24–30 AUGUST 2026

2027 Data and Engineering Delivery Plan

Week 35 Delivery Report

What moved this week, initiative by initiative, with the delivery schedule it sits in.

Cyber & Infra · Data · Core · Sector Intelligence · D&E · University Services

THE WEEK AT A GLANCE

Data 2 INITIATIVES

Outcomes. 2 initiatives moved, led by QAS Flows/ISS, QAS LMI Curriculum. Very early scoping; the HolonIQ-to-QAS moves follow one pattern. The analytics items were added since the August review; commentary to follow.

Risks & decisions. Nothing raised this week.

Core 9 INITIATIVES

Outcomes. 9 initiatives moved, led by HIQ – QAS Auth Migration, MyQS Cerebrum, QAS Auth. MyQS went live on my.qs.com.

Risks & decisions. QAS Auth: User load needs QA and sign-off. The identity load is applied with minor loose ends still to close; it needs a QA pass and formal sign-off before it can be called done. User load needs QA and sign-off. Dev Redshift retirement is queued as cleanup.

Sector Intelligence 16 INITIATIVES

Outcomes. 16 initiatives moved, led by QAS Factfiles, QAS Stars, Rankings Template. Shipped the new auth with subdomains to live, including role-based gating for Rankings Admin and CX institution syncing, securing access control across the portal.

Risks & decisions. Partnerships New: QPD admin module. Currently inaccessible owing to the deprecated Back Office. A decision is needed on where this will live now. MoveON. MoveIN. The RabbitMQ production OS upgrade remains pending development approval. TU.

D&E 11 INITIATIVES

Outcomes. 11 initiatives moved, led by TU – Career Match Microsite, TU.com Cookie Compliance, Appian to Hubspot Migration. Career Match accuracy: fixed a bug that could send students to the wrong subject's results, and tightened how matches are ranked and capped.

Risks & decisions. TU – Career Match Microsite: Exploratory phase. The team is working through what the microsite needs next; this week that surfaced crawler and bot protection as a new priority. Exploratory phase.

University Services 9 INITIATIVES

Outcomes. 9 initiatives moved, led by Appian to Hubspot Migration, Aurora Implementation, Aurora – Counsellor Feedback. WeChat plugged into Aurora and the HubSpot instances (Simon Pennington); the Appian move scoped by James Healy with Claire. Sunway University onboarding (Aircall, Sakari and HubSpot).


Risks & decisions. IVR changes. The IVR changes require extensive testing to ensure everything is working as expected. Sakari. QS Events Sakari and HubSpot credentials are needed.


Contents

Delivery schedule 3
Engineering activity 4
Data 5
Core 7
Sector Intelligence 11
D&E 15
University Services 19

2027 Data and Engineering Delivery Plan


Delivery schedule 109 initiatives

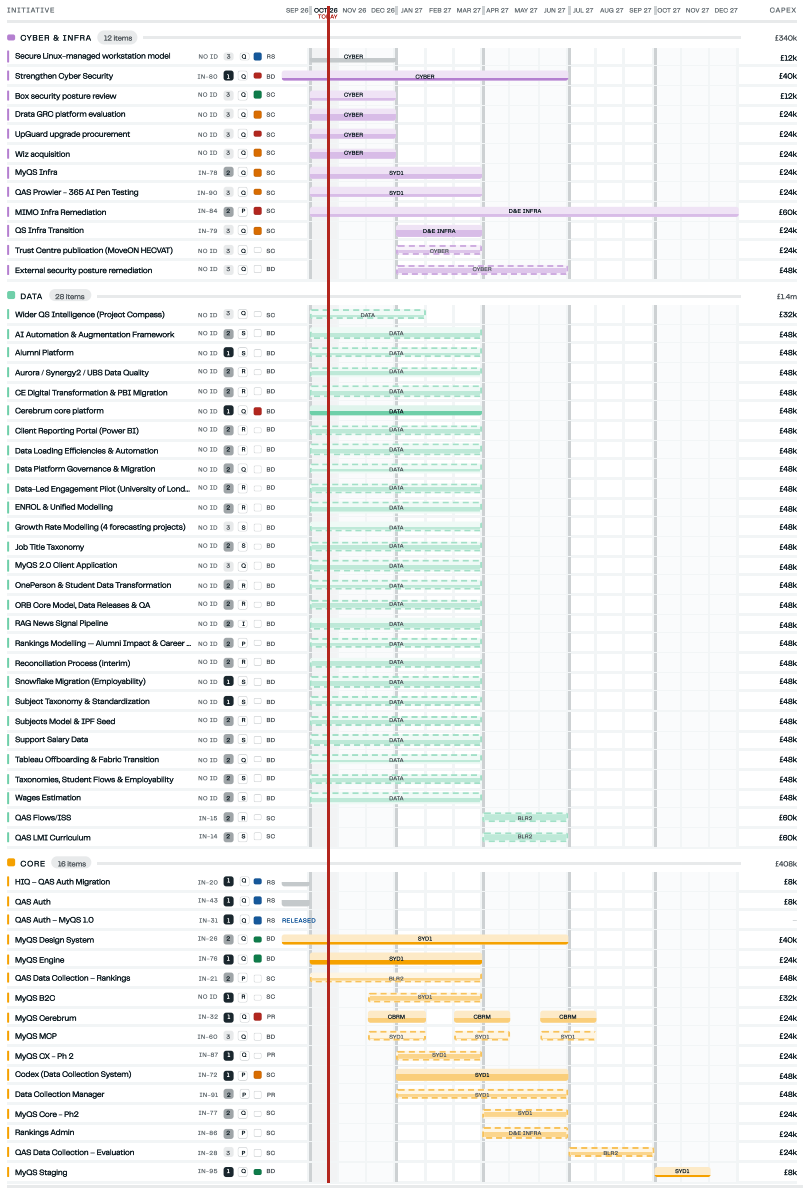

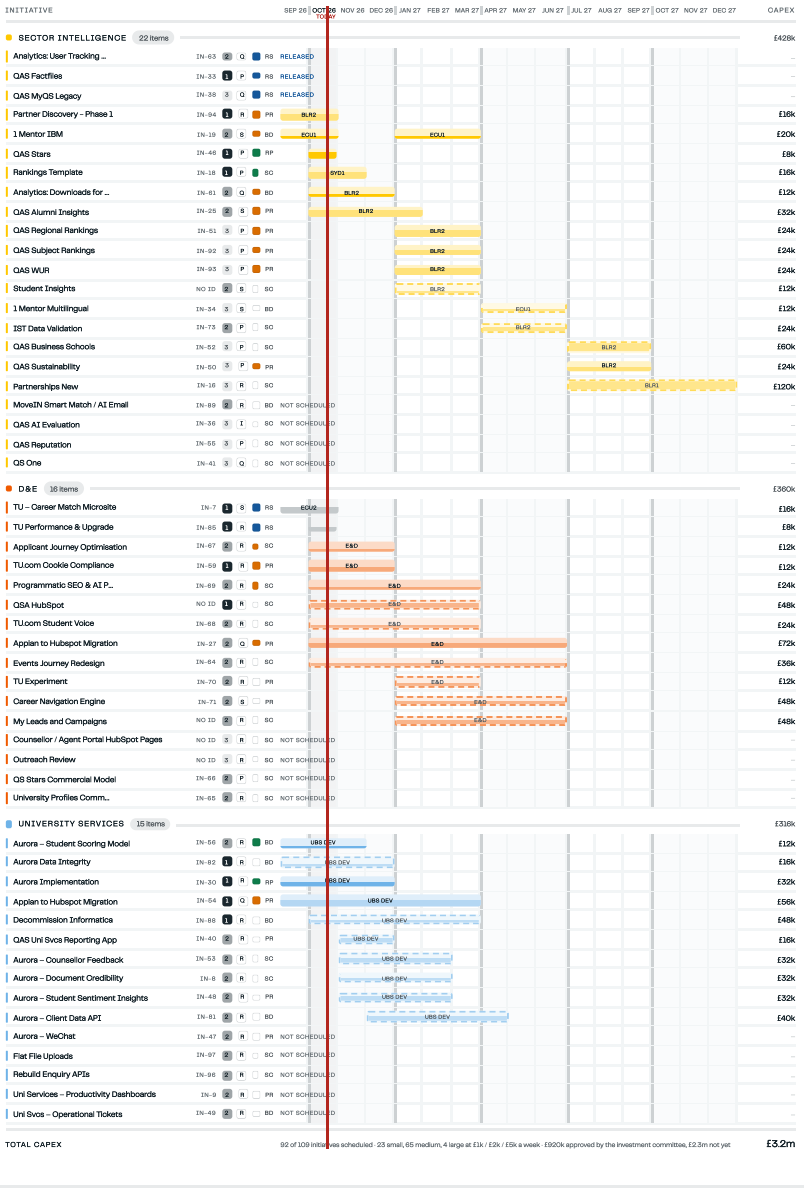


Productivity Heatmap NOV 24 – OCT 26

Lines of code committed a day.

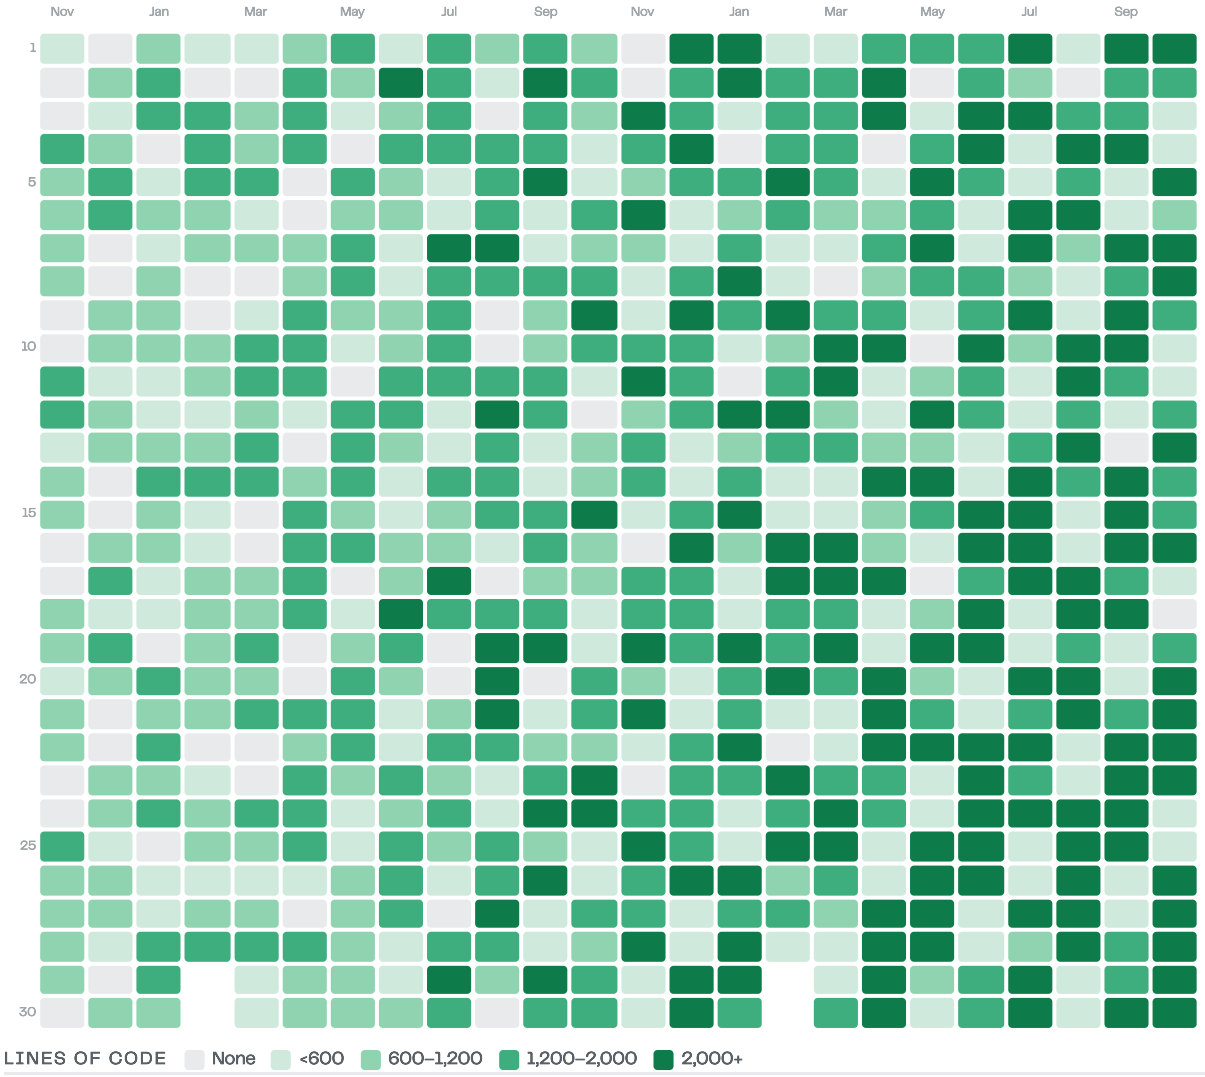

AI Code Intensity NOV 24 – OCT 26

Share of committed code written by AI.

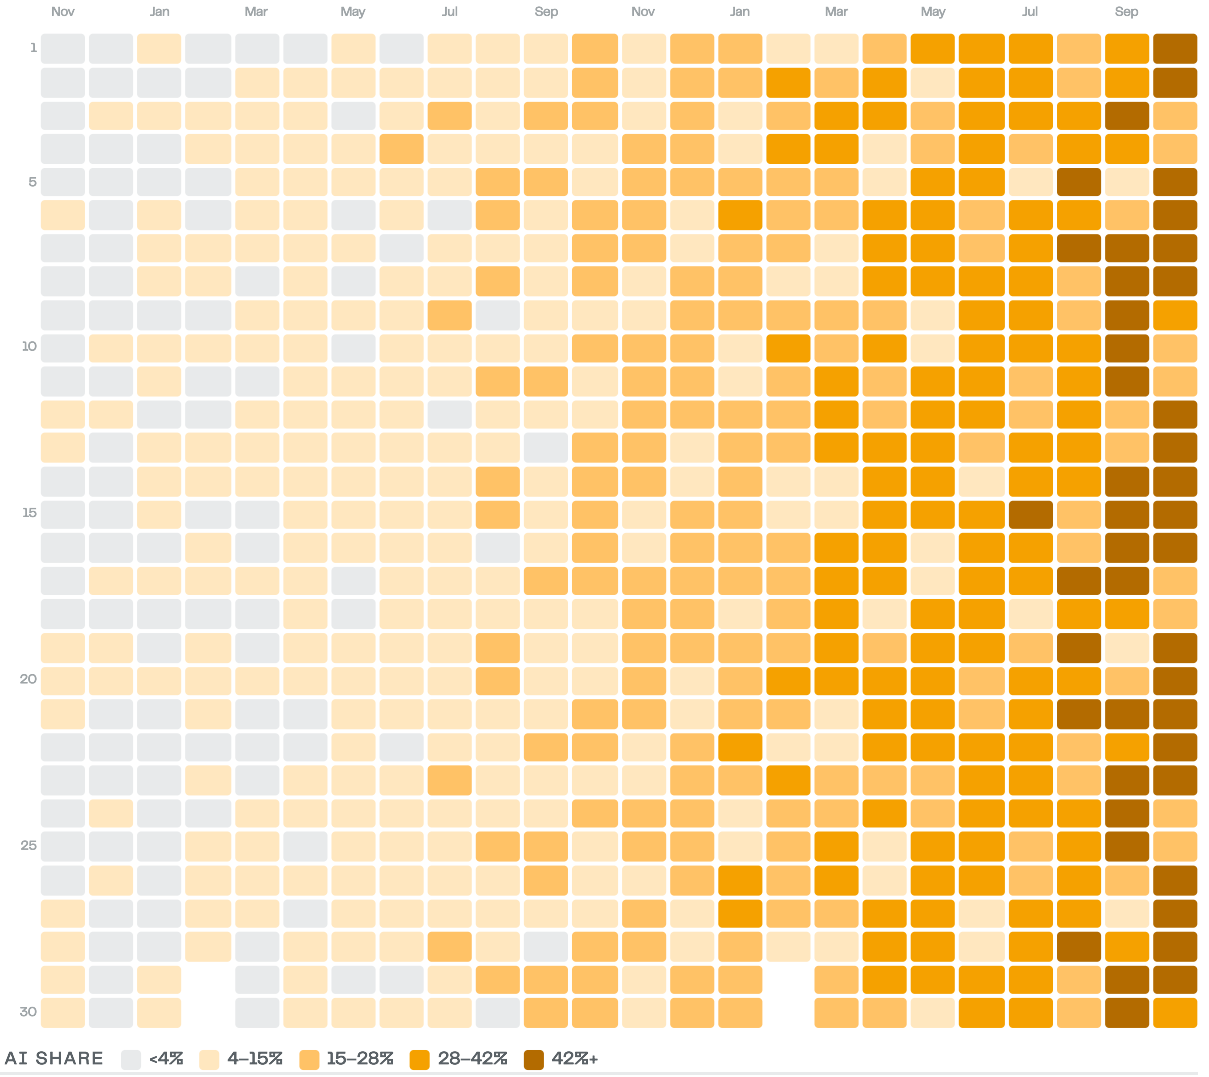

2027 Data and Engineering Delivery Plan

SECTION 1 OF 5


Data

2 initiatives reported

2 scoping

EFFORT Small · £1k/wk Medium · £2k/wk Large · £5k/wk STAGE Building or release planning Scoping or prototype Released

INITIATIVE						CAPEX
DATA	28 items					£1.4m
Wider QS Intelligence (Projec…	NO ID	3	Q		SC	£32k
AI Automation & Augmentati…	NO ID	2	S		BD	£48k
Alumni Platform	NO ID	1	S		BD	£48k
Aurora / Synergy2 / UBS Data …	NO ID	2	R		BD	£48k
CE Digital Transformation & P…	NO ID	2	R		BD	£48k
Cerebrum core platform	NO ID	1	Q	●	BD	£48k
Client Reporting Portal (Power…	NO ID	2	R		BD	£48k
Data Loading Efficiencies & A…	NO ID	2	R		BD	£48k
Data Platform Governance & …	NO ID	2	Q		BD	£48k
Data-Led Engagement Pilot (U…	NO ID	2	R		BD	£48k
ENROL & Unified Modelling	NO ID	2	R		BD	£48k
Growth Rate Modelling (4 fore…	NO ID	3	S		BD	£48k
Job Title Taxonomy	NO ID	2	S		BD	£48k
MyQS 2.0 Client Application	NO ID	3	Q		BD	£48k
OnePerson & Student Data Tr…	NO ID	2	R		BD	£48k
ORB Core Model, Data Release…	NO ID	2	R		BD	£48k
RAG News Signal Pipeline	NO ID	2	I		BD	£48k
Rankings Modelling — Alumni …	NO ID	2	P		BD	£48k
Reconciliation Process (Interi…	NO ID	2	R		BD	£48k
Snowflake Migration (Employ…	NO ID	1	S		BD	£48k
Subject Taxonomy & Standar…	NO ID	1	S		BD	£48k
Subjects Model & IPF Seed	NO ID	2	R		BD	£48k
Support Salary Data	NO ID	2	S		BD	£48k
Tableau Offboarding & Fabric …	NO ID	2	Q		BD	£48k
Taxonomies, Student Flows & …	NO ID	2	S		BD	£48k
Wages Estimation	NO ID	2	S		BD	£48k
QAS Flows/ISS	IN-15	2	R		SC	£60k
QAS LMI Curriculum	IN-14	2	S		SC	£60k

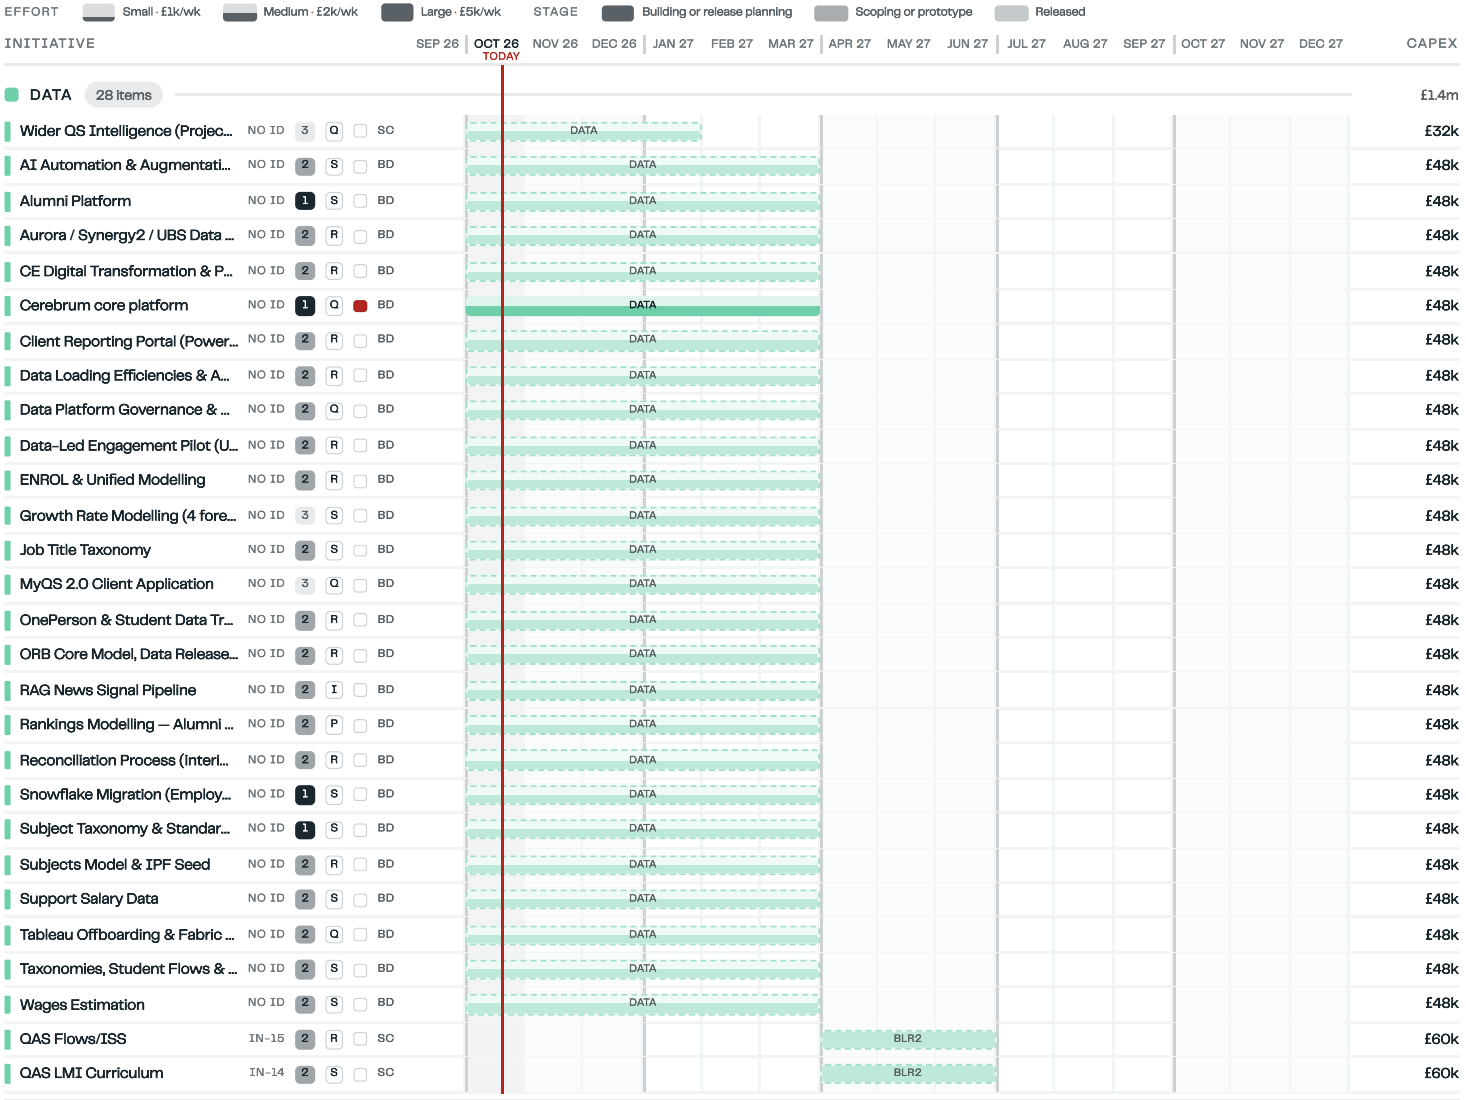

TOTAL CAPEX — 28 of 28 initiatives scheduled · 26 medium, 2 large at £1k / £2k / £5k a week · £48k approved by the investment committee, £1.3m not yet — £1.4m

QAS Flows/ISS

IN-15 · SCOPING

Very early scoping; the HolonIQ-to-QAS moves follow one pattern. The analytics items were added since the August review; commentary to follow.

QAS LMI Curriculum

IN-14 · SCOPING

Very early scoping; the HolonIQ-to-QAS moves follow one pattern. The analytics items were added since the August review; commentary to follow.


2027 Data and Engineering Delivery Plan

SECTION 2 OF 5

Core

9 initiatives reported

3 scoping
1 prototype
2 building
3 released

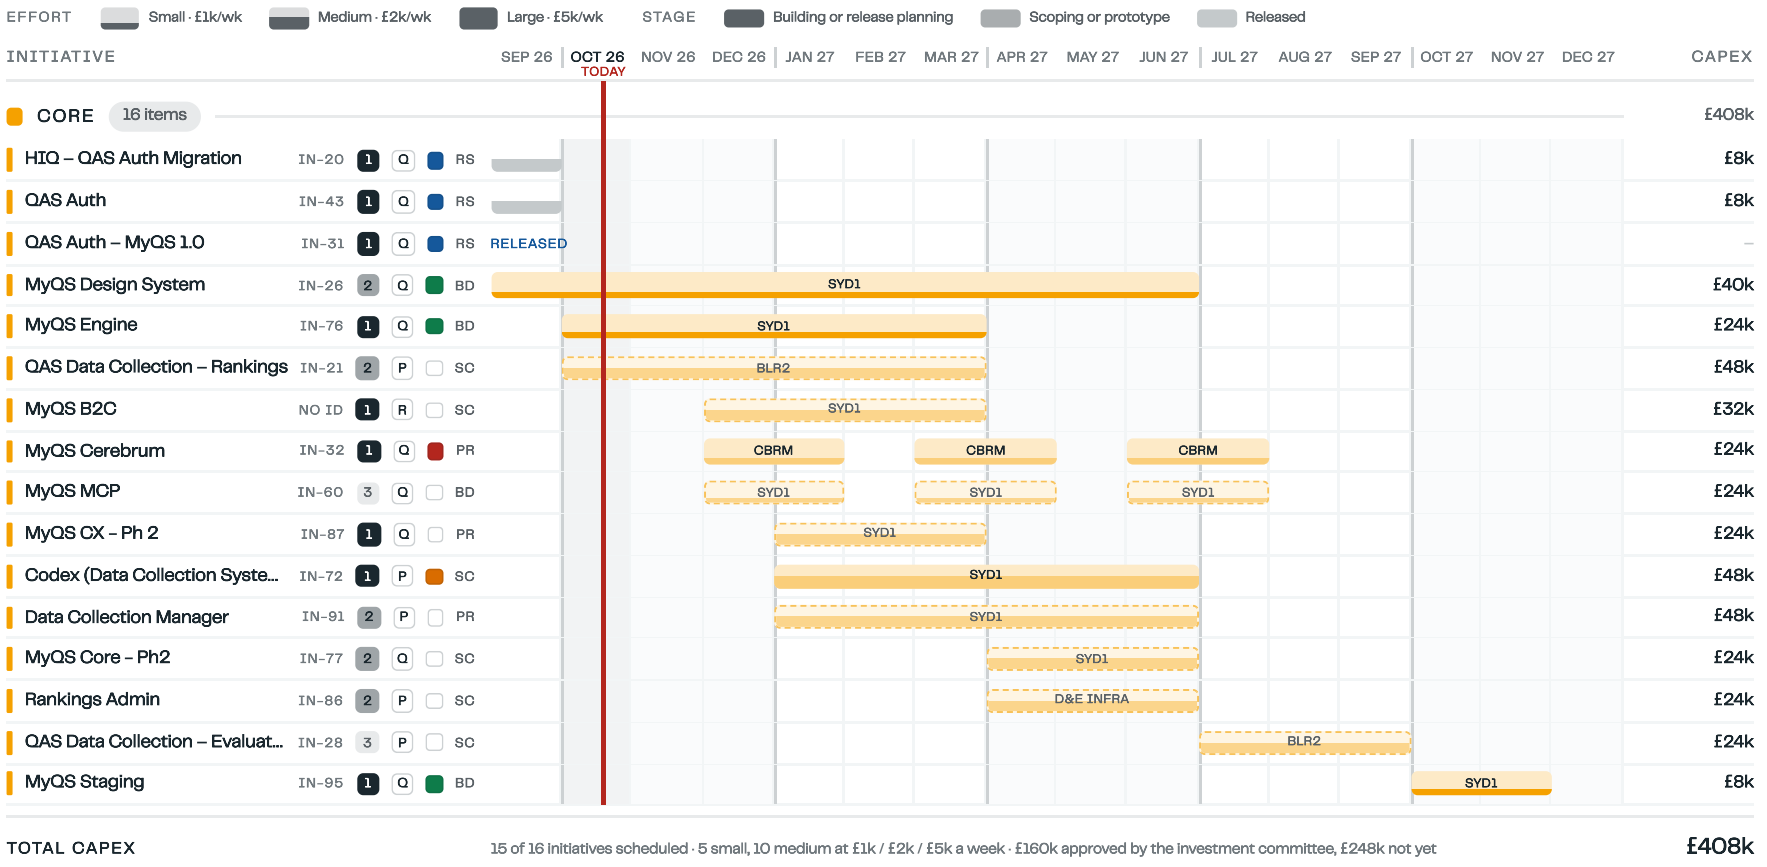

HIQ – QAS Auth Migration

IN-20 · SYD1 · SYD1 · CHARLIE LIU · QS APPLICATION SYSTEM · RELEASED

HolonIQ migration (my.holoniq.com to holoniq.qs.com). All HolonIQ logins moved onto QAS Auth alongside the main release. my.holoniq.com is now holoniq.qs.com. On the front end the launcher resolves the MyQS subdomain from an allowlisted key, qas-design was adopted up to 2.1.19, QS Pulse activity tracking was mounted behind PULSE_INGEST_URL, and each change was promoted from holoniq-qas to qas-prod. On the back end, org-link resolution was reworked over qs_core_id, ranking_item_id and hrit_id; the renamed QAS membership role vocabulary and the ranking_master account type are accepted in the consumer derivation; native and derived subscription rows are merged in account_view; and the DMS QAS sync was retired. 18 merged PRs and 39 commits across three HolonOS repositories.

MyQS Cerebrum

IN-32 · SYD1 · SYD1 · CHARLIE LIU · QS APPLICATION SYSTEM · PROTOTYPE

Cerebrum FE. QAS data exposed to AI agents, and the Cerebrum data asset brought into QAS, under the permissioning model. Experimental through 2026, subject to appetite for an MCP and to Cerebrum covering more data assets. Activity now reported to Pulse through the shell tracker, the agent session warmed before the user's first message, and qas-design taken to 2.1.19 with its estate defaults and theme plugin adopted.

QAS Auth

IN-43 · SYD1 · SYD1 · CHARLIE LIU · INFRASTRUCTURE · D&E · QS APPLICATION SYSTEM · INFRASTRUCTURE · RELEASED

MyQS production cutover; audit and compliance surface; QS Auth; product access and role vocabulary; identity data load; QS Supergraph; MyQS FE; CX FE. D&E infrastructure: my.qs.com DNS and deployment support. Single sign-in for all future QS platforms, delivered on the end-of-August target; migrating users reset their password and re-establish MFA. MyQS now serves from my.qs.com. The Auth0 tenants were cut over with a my2.qs.com transition window kept open, the design system followed, production invitation URLs were repointed, and the MyQS1 partner-discovery origin was synced from live prod.

Risks and decisions. User load needs QA and sign-off. The identity load is applied with minor loose ends still to close; it needs a QA pass and formal sign-off before it can be called done.

QAS Auth – MyQS 1.0

IN-31 · BLR2 · SECTOR INTELLIGENCE · RELEASED

MyQS (new auth with subdomains to live); QA (MyQS regression testing). MyQS 1.0 on QAS Auth; Factfiles migrated with its release issues resolved; dormant MyQS 1.0 technology kept available for reference. Shipped the new auth with subdomains to live. Added role-based access control for Rankings Admin via CX roles; fixed the institution switcher for Rankings and Stars; resolved an infinite redirect loop for users with no CX accounts and added expired CX session handling; built the Rankings Calendar API endpoint; replaced the access-restricted screen with a redirect to the request-demo page; and integrated the Legacy Pulse component for Stars users. Completed Chat Composer and Export testing, MyQS regression testing and QPD ticket estimations. Waiting for Products access to begin sanity testing.

MyQS Design System

IN-26 · SYD1 · SYD1 · CHARLIE LIU · QS APPLICATION SYSTEM · BUILDING

Design System 2.1.0 to 2.1.25. Phase One closes in August for the Brand review and publishes at a stable URL; Phase Two (September–November) delivers the application building blocks. 2.1.0 through 2.1.25: resizable and reorderable table columns, per-product role granting from the table, a Tile component, the PageMoved screen, LegacyPulse, and a reworked launcher catalogue: Factfiles renamed to Rankings Preview and moved to its own subdomain, QS Stars promoted to a product app, and Stars and Partner Discovery badged alpha.

QAS Data Collection – Rankings

IN-21 · SCOPING

Significant work to reach a clear prototype; a priority to work through with Lee.

Rankings Admin

IN-86 · INFRASTRUCTURE · D&E · SCOPING

Completed deployment and hosting setup for the rankings-admin, rankings-preview, stars and partnerdiscovery platforms using Docker, Nginx and AWS ALB.

MyQS MCP

IN-60 · SYD1 · SYD1 · CHARLIE LIU · QS APPLICATION SYSTEM · BUILDING

QS Agent and MCP (Claude Opus 5, warm-up, production skills registry). QAS data exposed to AI agents, and the Cerebrum data asset brought into QAS, under the permissioning model. Experimental through 2026, subject to appetite for an MCP and to Cerebrum covering more data assets. Claude Opus 5 is now the agent's main model; thinking and tool progress stream before the first answer token; an authenticated warm-up ping builds and parks the whole session so the first real message is fast; production skills are served from an eu-west-1 registry; and the Cerebrum registry tool runs in production behind a product gate.

QAS Data Collection – Evaluation

IN-28 · SCOPING

Remove the MIMO dependency for Stars and evaluation data collection, probably with an off-the-shelf solution; AI evaluation likely shares the technology.

QS Application System

OTHER WORK · NOT LINKED TO AN INITIATIVE

Pulse activity tracking: The shell tracker now reports activity from CX and Cerebrum; LegacyPulse gives legacy pages a zero-config tracker with full-URL page views behind the qs.com consent record; the HubSpot embed is consent-gated; and page-path resolution moved into the normaliser, with PAGE_PATH promoted to a first-class product-lane field.

QS Application System

RISKS AND DECISIONS

Risks and decisions. User load needs QA and sign-off. The identity load is applied with minor loose ends still to close; it needs a QA pass and formal sign-off before it can be called done. Dev Redshift retirement is queued as cleanup. QAS-Pulse #18 stays a draft until there is capacity for it.

Infrastructure

RISKS AND DECISIONS

Risks and decisions. TU. The QS Apply form submission investigation through Cloudflare Security Analytics remains ongoing. QSCHINA. The content team's CSV import upload issue in QS RMS remains under investigation. Automox. Approval from the Legal and DPO teams is required before D&E Linux OS patch management adoption. Bitdefender. Deployment remains pending the required approvals and licensing confirmation.

Sector Intelligence

RISKS AND DECISIONS

Risks and decisions. QPD admin module. Currently inaccessible owing to the deprecated Back Office. A decision is needed on where this will live now.

Sector Intelligence 16 initiatives

SECTION 3 OF 5

Sector Intelligence

16 initiatives reported

6 scoping
3 prototype
3 building
1 release planning
3 released

EFFORT Small · £1k/wk | Medium · £2k/wk | Large · £5k/wk
STAGE Building or release planning | Scoping or prototype | Released

INITIATIVE						SEP 26	OCT 26 TODAY	NOV 26	DEC 26	JAN 27	FEB 27	MAR 27	APR 27	MAY 27	JUN 27	JUL 27	AUG 27	SEP 27	OCT 27	NOV 27	DEC 27	CAPEX
SECTOR INTELLIGENCE	22 items																					£428k
Analytics: User Tracking …	IN-63	2	Q	RS	RELEASED																	–
QAS Factfiles	IN-33	1	P	RS	RELEASED																	–
QAS MyQS Legacy	IN-38	3	Q	RS	RELEASED																	–
Partner Discovery – Phase 1	IN-94	1	R	PR		BLR2																£16k
1 Mentor IBM	IN-19	2	S	BD		ECU1				ECU1												£20k
QAS Stars	IN-46	1	P	RP																		£8k
Rankings Template	IN-18	1	P	SC			SYD1															£16k
Analytics: Downloads for …	IN-61	2	Q	BD			BLR2															£12k
QAS Alumni Insights	IN-25	2	S	PR			BLR2															£32k
QAS Regional Rankings	IN-51	3	P	PR						BLR2												£24k
QAS Subject Rankings	IN-92	3	P	PR						BLR2												£24k
QAS WUR	IN-93	3	P	PR						BLR2												£24k
Student Insights	NO ID	2	S	SC						BLR2												£12k
1 Mentor Multilingual	IN-34	3	S	BD									ECU1									£12k
IST Data Validation	IN-73	2	P	SC									BLR2									£24k
QAS Business Schools	IN-52	3	P	SC												BLR2						£60k
QAS Sustainability	IN-50	3	P	PR												BLR2						£24k
Partnerships New	IN-16	3	R	SC												BLR1						£120k
MoveIN Smart Match / AI Em…	IN-89	2	R	BD	NOT SCHEDULED																	–
QAS AI Evaluation	IN-36	3	I	SC	NOT SCHEDULED																	–
QAS Reputation	IN-55	3	P	SC	NOT SCHEDULED																	–
QS One	IN-41	3	Q	SC	NOT SCHEDULED																	–

TOTAL CAPEX — 15 of 22 initiatives scheduled · 4 small, 9 medium, 2 large at £1k / £2k / £5k a week · £200k approved by the investment committee, £228k not yet — £428k

QAS Factfiles

IN-33 · D&E INFRASTRUCTURE · INFRASTRUCTURE · D&E · INFRASTRUCTURE · RELEASED

rankings-preview.qs.com hosting (Factfiles, renamed Rankings Preview). MyQS 1.0 on QAS Auth; Factfiles migrated with its release issues resolved; dormant MyQS 1.0 technology kept available for reference. Completed deployment and hosting setup for the rankings-admin, rankings-preview, stars and partnerdiscovery platforms using Docker, Nginx and AWS ALB.

QAS Stars

IN-46 · BLR2 · INFRASTRUCTURE · D&E · SECTOR INTELLIGENCE · RELEASE PLANNING

Stars. D&E infrastructure: stars.qs.com hosting. Largely built and being refined; launch expected early September. Completed deployment and hosting setup for the rankings-admin, rankings-preview, stars and partnerdiscovery platforms using Docker, Nginx and AWS ALB. Renamed 'Overall Summary' to 'Summary' across the header and sidebar, and applied visual polish to the summary cards and modal (typography, icon alignment and spacing).

Rankings Template

IN-18 · SCOPING

First standalone QAS version of HolonIQ rankings, WUR first; through Build Ready and wired into QAS before launch. Likely to displace the Factfiles rankings preview.

1 Mentor IBM

IN-19 · ECU1 · SECTOR INTELLIGENCE · BUILDING

IBM instance adjustments; next release with the IBM-requested changes. 1 Mentor enhanced to the functionality sold in the signed IBM contract; multilingual support for Central Asian customers. Worked on several adjustments requested for the IBM instance.

Analytics: Downloads for ...

IN-61 · BUILDING

Very early scoping; the HolonIQ-to-QAS moves follow one pattern. The analytics items were added since the August review; commentary to follow.

Analytics: User Tracking ...

IN-63 · RELEASED

Very early scoping; the HolonIQ-to-QAS moves follow one pattern. The analytics items were added since the August review; commentary to follow.

QAS Alumni Insights

IN-25 · PROTOTYPE

More prototype work before the next Build Ready milestone, expected within weeks.

1 Mentor Multilingual

IN-34 · BUILDING

1 Mentor enhanced to the functionality sold in the signed IBM contract; multilingual support for Central Asian customers.

Partnerships New

IN-16 · BLR2 · INFRASTRUCTURE · D&E · BLR1 · SECTOR INTELLIGENCE · SCOPING

Partner Discovery; QA (Chat Composer and Export testing, QPD estimations). BLR1: QPD enhancements. D&E infrastructure: partnerdiscovery.qs.com hosting. Latest enhancements pass Build Ready again; the next release makes it a full QAS application (permissioning and authentication) before any customer release. Completed deployment and hosting setup for the rankings-admin, rankings-preview, stars and partnerdiscovery platforms using Docker, Nginx and AWS ALB. Reworked incoming-interest read state to sync across the dashboard, lists and notifications in one action; tightened access control on interest read actions; added a verified badge on staff and faculty profiles; and refreshed the Smart Match promo panel.

Risks and decisions. QPD admin module. Currently inaccessible owing to the deprecated Back Office. A decision is needed on where this will live now.

QAS AI Evaluation

IN-36 · SCOPING

Remove the MIMO dependency for Stars and evaluation data collection, probably with an off-the-shelf solution; AI evaluation likely shares the technology.

QAS Business Schools

IN-52 · SCOPING

Identified as an important priority at the last Tech Week.

QAS MyQS Legacy

IN-38 · RELEASED

MyQS 1.0 on QAS Auth; Factfiles migrated with its release issues resolved; dormant MyQS 1.0 technology kept available for reference.

QAS Regional Rankings

IN-51 · PROTOTYPE

Very early scoping; the HolonIQ-to-QAS moves follow one pattern. The analytics items were added since the August review; commentary to follow.

QAS Reputation

IN-55 · SCOPING

Very early scoping; the HolonIQ-to-QAS moves follow one pattern. The analytics items were added since the August review; commentary to follow.

QAS Sustainability

IN-50 · PROTOTYPE

Very early scoping; the HolonIQ-to-QAS moves follow one pattern. The analytics items were added since the August review; commentary to follow.

QS One

IN-41 · SCOPING

QAS permissions will track QS One membership for embargoed rankings access; what QS One is and is not still needs scoping.

Infrastructure

OTHER WORK · NOT LINKED TO AN INITIATIVE

MoveON: Completed migration of the AWS London PlatformPHP servers to Ubuntu 24.04 and validated functionality. MoveIN: Resolved Elasticsearch performance and indexing issues through infrastructure optimisation.

Sector Intelligence

OTHER WORK · NOT LINKED TO AN INITIATIVE

HUB2: Initiated development of Media Partner authentication enhancements, including login redirection and password recovery workflows. HUB1: Began implementation of ranking form enhancements to improve handling of pre-populated data, source tracking and data update workflows. Mixpanel coverage: Increased Mixpanel coverage across three 1M features (Ikigai, Saved courses and Learning paths); awaiting final approval. Visual and accessibility improvements: Delivered visual and accessibility improvements to the advisor and learner platforms. QA: Successfully validated all tasks planned for the current sprint.

Infrastructure

RISKS AND DECISIONS

Risks and decisions. MoveON. France patching remains pending and is a dependency for the planned Uyuni server upgrade; the France MySQL 8.4.7 migration remains pending; PlatformPHP migration activities continue to require environment-specific validation and remediation; and the review and restriction of sensitive AP files and URLs is still being validated before production rollout. MoveIN. The RabbitMQ production OS upgrade remains pending development approval. TU.

Sector Intelligence

RISKS AND DECISIONS

Risks and decisions. QPD admin module. Currently inaccessible owing to the deprecated Back Office. A decision is needed on where this will live now. HUB2 timing. Minor timing risk on future HUB2 enhancements if pending requirements are received later in the sprint, reducing the available implementation and testing window.


2027 Data and Engineering Delivery Plan

SECTION 4 OF 5

D&E

11 initiatives reported

6 scoping
4 prototype
1 released

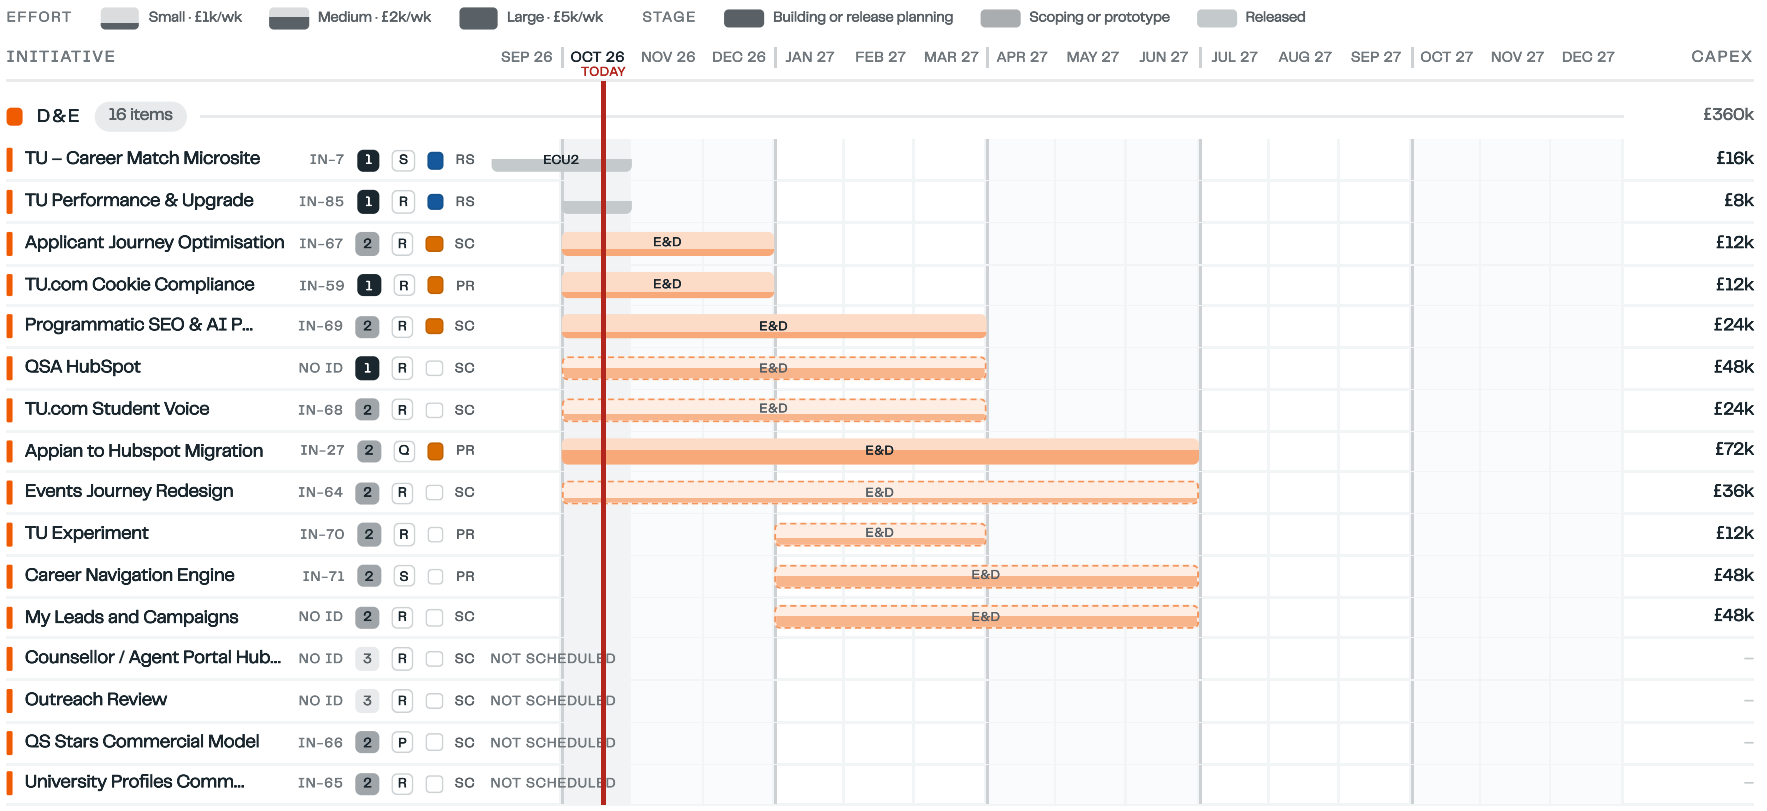

TOTAL CAPEX — 12 of 16 initiatives scheduled · 6 small, 6 medium at £1k / £2k / £5k a week · £144k approved by the investment committee, £216k not yet — £360k

TU – Career Match Microsite

IN-7 · ECU2 · DIGITAL AND EVENTS · SECTOR INTELLIGENCE · RELEASED

career recommendation accuracy; Career Match analytics; TopUniversities integration; site stabilisation; content and style fixes. Events and Drupal: Career Matcher post-release changes. The first epic of the TU career application has shipped; Phase 2 is being scoped in Tech Week Three. Fixed a bug sending students to unrelated subject results, and capped and prioritised matches so the strongest ones surface first. Fully instrumented the Career Match journey in Mixpanel, giving pathway-level funnel visibility for the first time. Career Match results now link directly to the matching subject page on topuniversities.com instead of a generic link. Removed unused code and consolidated duplicated styling logic to keep the codebase easy to maintain. Minor content correction and header spacing polish.

Risks and decisions. Exploratory phase. The team is working through what the microsite needs next; this week that surfaced crawler and bot protection as a new priority.

TU.com Cookie Compliance

IN-59 · NEWLY ADDED D&E ITEMS · PROTOTYPE

Events Journey Redesign, TU.com Cookie Compliance, University Profiles and QS Stars Commercial Models, Applicant Journey Optimisation, TU.com Student Voice and Programmatic SEO & AEO (scoping), plus TU Experiment (prototype). Status commentary to follow.

Appian to Hubspot Migration

IN-27 · PROTOTYPE

The candidate engagement and digital events side of the Appian to HubSpot move; James Healy leads the scoping.

Applicant Journey Optimisation

IN-67 · NEWLY ADDED D&E ITEMS · SCOPING

Events Journey Redesign, TU.com Cookie Compliance, University Profiles and QS Stars Commercial Models, Applicant Journey Optimisation, TU.com Student Voice and Programmatic SEO & AEO (scoping), plus TU Experiment (prototype). Status commentary to follow.

Career Navigation Engine

IN-71 · PROTOTYPE

The first epic of the TU career application has shipped; Phase 2 is being scoped in Tech Week Three.

Events Journey Redesign

IN-64 · NEWLY ADDED D&E ITEMS · SCOPING

Events Journey Redesign, TU.com Cookie Compliance, University Profiles and QS Stars Commercial Models, Applicant Journey Optimisation, TU.com Student Voice and Programmatic SEO & AEO (scoping), plus TU Experiment (prototype). Status commentary to follow.

Programmatic SEO & AI P…

IN-69 · NEWLY ADDED D&E ITEMS · SCOPING

Events Journey Redesign, TU.com Cookie Compliance, University Profiles and QS Stars Commercial Models, Applicant Journey Optimisation, TU.com Student Voice and Programmatic SEO & AEO (scoping), plus TU Experiment (prototype). Status commentary to follow.

QS Stars Commercial Model

IN-66 · NEWLY ADDED D&E ITEMS · SCOPING

Events Journey Redesign, TU.com Cookie Compliance, University Profiles and QS Stars Commercial Models, Applicant Journey Optimisation, TU.com Student Voice and Programmatic SEO & AEO (scoping), plus TU Experiment (prototype). Status commentary to follow.

TU Experiment

IN-70 · NEWLY ADDED D&E ITEMS · PROTOTYPE

Events Journey Redesign, TU.com Cookie Compliance, University Profiles and QS Stars Commercial Models, Applicant Journey Optimisation, TU.com Student Voice and Programmatic SEO & AEO (scoping), plus TU Experiment (prototype). Status commentary to follow.

TU.com Student Voice

IN-68 · NEWLY ADDED D&E ITEMS · SCOPING

Events Journey Redesign, TU.com Cookie Compliance, University Profiles and QS Stars Commercial Models, Applicant Journey Optimisation, TU.com Student Voice and Programmatic SEO & AEO (scoping), plus TU Experiment (prototype). Status commentary to follow.

University Profiles Comm…

IN-65 · NEWLY ADDED D&E ITEMS · SCOPING

Events Journey Redesign, TU.com Cookie Compliance, University Profiles and QS Stars Commercial Models, Applicant Journey Optimisation, TU.com Student Voice and Programmatic SEO & AEO (scoping), plus TU Experiment (prototype). Status commentary to follow.

Infrastructure

OTHER WORK · NOT LINKED TO AN INITIATIVE

Resolved SSL hostname mismatch issues for outreach.qs.com and qs-enrollments.qs.com. Completed the Outreach pre-production setup using AWS CDK and Ansible automation. Continued development of modular AWS CDK templates and provisioned TU/TM and Apache Solr pre-production environments. Whitelisted new IP ranges across the bastion hosts for the new code-ingestion process. Completed Solr upgrades across all QSCHINA non-production environments. Automated Solr VM provisioning and installation for the TU/TM environments. Implemented CDN cache optimisation with one-year expiry policies for WOFF/WOFF2 assets in QSCHINA live. Implemented CloudWatch monitoring optimisation and cleanup activities.

Digital and Events

OTHER WORK · NOT LINKED TO AN INITIATIVE

CMT module conversion from React to Drupal: Testing is complete and the conversion is ready for release. Agenda builder: The last phase of testing is taking place, with some code refactoring owing to merge issues. Client App: The new app version is ready and approved by the business, to be released in the stores once the approval process is complete. New servers: The new servers are set up and testing is starting.

Sector Intelligence

RISKS AND DECISIONS

Risks and decisions. Exploratory phase. The team is working through what the microsite actually needs next; this week that surfaced crawler and bot protection (see next week). Identification and scoping will continue alongside any new Product requirements or opportunities to support another team.

Digital and Events

RISKS AND DECISIONS


Risks and decisions. Angular upgrade. Testing on the new servers has started. Drupal upgrade. All code has been merged again to resolve the conflicts that appeared from the last three sprints' code.

SECTION 5 OF 5

University Services

9 initiatives reported

2 scoping
5 prototype
1 building
1 release planning

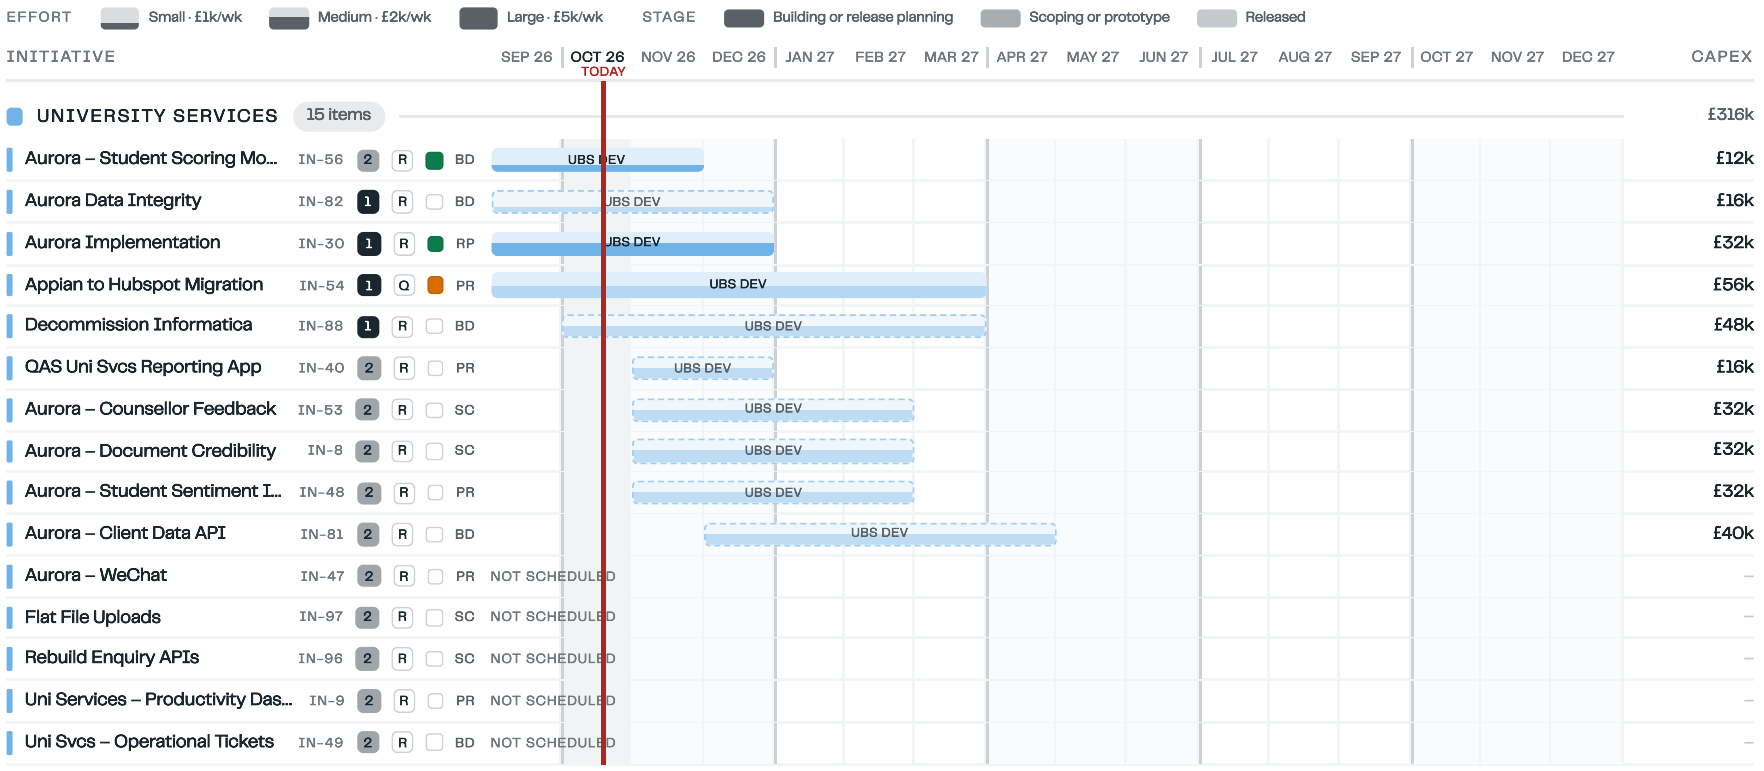

TOTAL CAPEX — 10 of 15 initiatives scheduled · 2 small, 8 medium at £1k / £2k / £5k a week · £100k approved by the investment committee, £216k not yet — £316k

Appian to Hubspot Migration

IN-54 · PROTOTYPE

WeChat plugged into Aurora and the HubSpot instances (Simon Pennington); the Appian move scoped by James Healy with Claire.

Aurora Implementation

IN-30 · CX SYSTEMS · UNIVERSITY SERVICES · RELEASE PLANNING

Sunway University onboarding (Aircall, Sakari and HubSpot). All campuses launched; issues, gaps and technical debt accumulated through the rollout still to close out. Onboarding onto Sakari and integration with the HubSpot portal; flow testing and amendments; voicemail set up.

Aurora – Counsellor Feedback

IN-53 · SCOPING

Call-transcript insight depends on call-data extraction led by Adam; the partner reporting app depends on University Services data reaching Cerebrum.

Aurora – Document Credibility

IN-8 · SCOPING

One Jira ticketing system across regions; document credibility scoring off the shelf; Power BI over HubSpot data rather than a QAS app.

Aurora – Student Scoring Model

IN-56 · BUILDING

Lead scoring through HubSpot's built-in model (Simon Pennington); data science also exploring the student model.

Aurora – Student Sentiment Insights

IN-48 · PROTOTYPE

Call-transcript insight depends on call-data extraction led by Adam; the partner reporting app depends on University Services data reaching Cerebrum.

Aurora – WeChat

IN-47 · PROTOTYPE

WeChat plugged into Aurora and the HubSpot instances (Simon Pennington); the Appian move scoped by James Healy with Claire.

QAS Uni Svcs Reporting App

IN-40 · PROTOTYPE

Call-transcript insight depends on call-data extraction led by Adam; the partner reporting app depends on University Services data reaching Cerebrum.

Uni Services – Productivity Dashboards

IN-9 · PROTOTYPE

One Jira ticketing system across regions; document credibility scoring off the shelf; Power BI over HubSpot data rather than a QAS app.

University Services

OTHER WORK · NOT LINKED TO AN INITIATIVE

Aircall: onboarded new users; followed up with Sean to obtain the caller IDs Aircall requires for further investigation of the Derby call-drop issue; assisted Patrick with Aircall calling data and granted Jess access to the Aircall API and dashboard. IVR: continued IVR upgrades for the remaining universities; added a call-back request option to the Derby IVR and changed the Nottingham IVR; recreated IVRs for universities following the split of teams into two groups. Sakari: set up the alphanumeric sender ID in the UTSC environment for testing; conducted testing on QS Staging for the main markets and communicated with the Sakari account manager.

University Services

RISKS AND DECISIONS

Risks and decisions. IVR changes. The IVR changes require extensive testing to ensure everything is working as expected. Sakari. QS Events Sakari and HubSpot credentials are needed.
