WEEK 40 · 28 SEPTEMBER – 2 OCTOBER 2026

2027 Data and Engineering Delivery Plan

Week 40 Delivery Report

What moved this week, initiative by initiative, with the delivery schedule it sits in.

Cyber & Infra · Data · Core · Sector Intelligence · D&E · University Services

THE WEEK AT A GLANCE

Cyber & Infra 2 INITIATIVES

Outcomes. 2 initiatives moved, led by Strengthen Cyber Security, MIMO Infra Remediation. Every QS front end now ships from one reviewed pipeline.

Risks & decisions. Box platform constraints and stakeholder impacts. Discovery activities continue to show that Box is... well... an issue and there is resistance to change beginning to emerge. Additional stakeholder engagement is required before recommendations can be finalised.

Data 26 INITIATIVES

Outcomes. 26 initiatives moved, led by Alumni Platform, Cerebrum core platform, Snowflake Migration (Employability). Cerebrum reached its most significant structural milestone to date: institution identity now reads from the platform registry rather than local bookkeeping.

Risks & decisions. Aurora / Synergy2 / UBS Data Quality (D&A) — AT RISK: a cross-functional task force is now in place, but persistent UBS defects across course-of-interest records, engagements and dates remain — the priority is finding where bad data originates, not just repairing history.

Core 3 INITIATIVES

Outcomes. 3 initiatives moved, led by MyQS CX – Ph 2, MyQS Staging, MyQS Design System. Every QS front end now ships from one reviewed pipeline.

Risks & decisions. Nothing raised this week.

Sector Intelligence 7 INITIATIVES

Outcomes. 7 initiatives moved, led by Partner Discovery – Phase 1, QAS Stars, Rankings Template. Every QS front end now ships from one reviewed pipeline.

Risks & decisions. No blockers, outstanding decisions, or major risks flagged this week. No risks or decisions required at the moment. The new sprint starts this Wednesday. Infrastructure upgrade demo timing.

D&E 2 INITIATIVES

Outcomes. 2 initiatives moved, led by TU Performance & Upgrade, Appian to Hubspot Migration. South America Rankings were released on 1 October. TU performance changes awaiting release; Drupal 11.4.8 in testing. Infrastructure: PHP 8.4 and Drupal 11.4.8 across TU and TM non-production.

Risks & decisions. Drupal sprint release. It was agreed with product that this would be delayed, since Drupal needs to be upgraded first. Redesign of QSA page. Waiting for clear requirements and form changes. GenAI workaround.

University Services 2 INITIATIVES

Outcomes. 2 initiatives moved, led by Appian to Hubspot Migration, Decommission Informatica. The team continues to focus on Appian production support and enhancements, while progressing with Appian Migration documentation and review activities.


Risks & decisions. Contact Matching in Sandbox. Still not able to fully test Contact Matching in Sandbox due to issues promoting data from production to sandbox, caused by missing data objects. Testing will proceed in Sandbox without Contact Matching. UoL licensing.


Contents

Delivery schedule 3
Engineering activity 4
Cyber & Infra 5
Data 8
Core 14
Sector Intelligence 16
D&E 20
University Services 23

2027 Data and Engineering Delivery Plan


Delivery schedule 109 initiatives

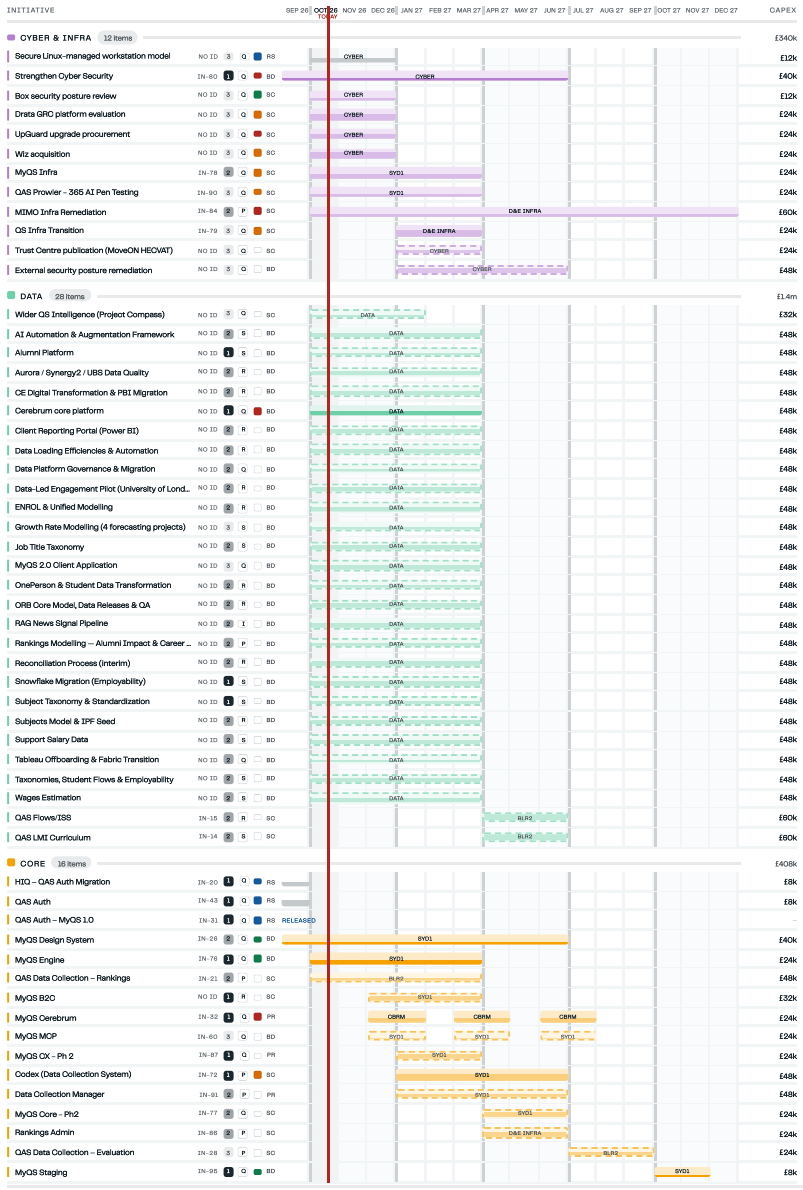

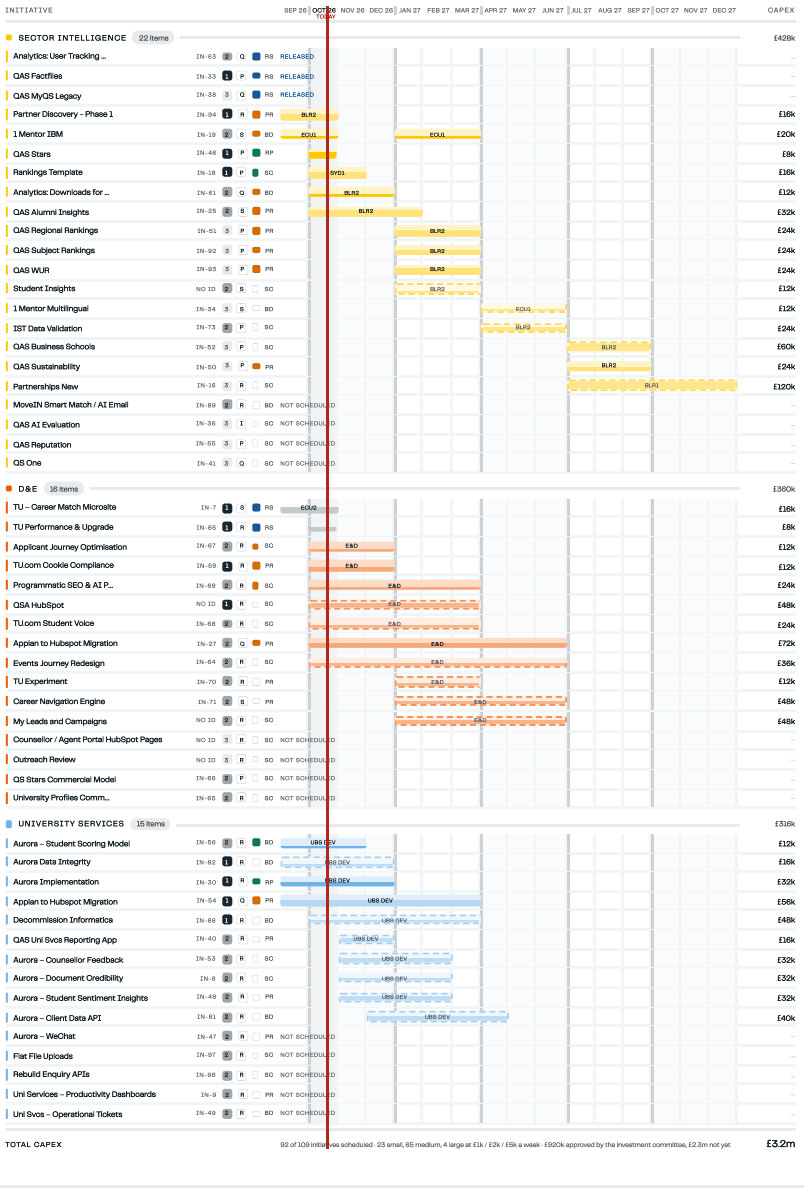

Productivity Heatmap NOV 24 – OCT 26


Lines of code committed a day.

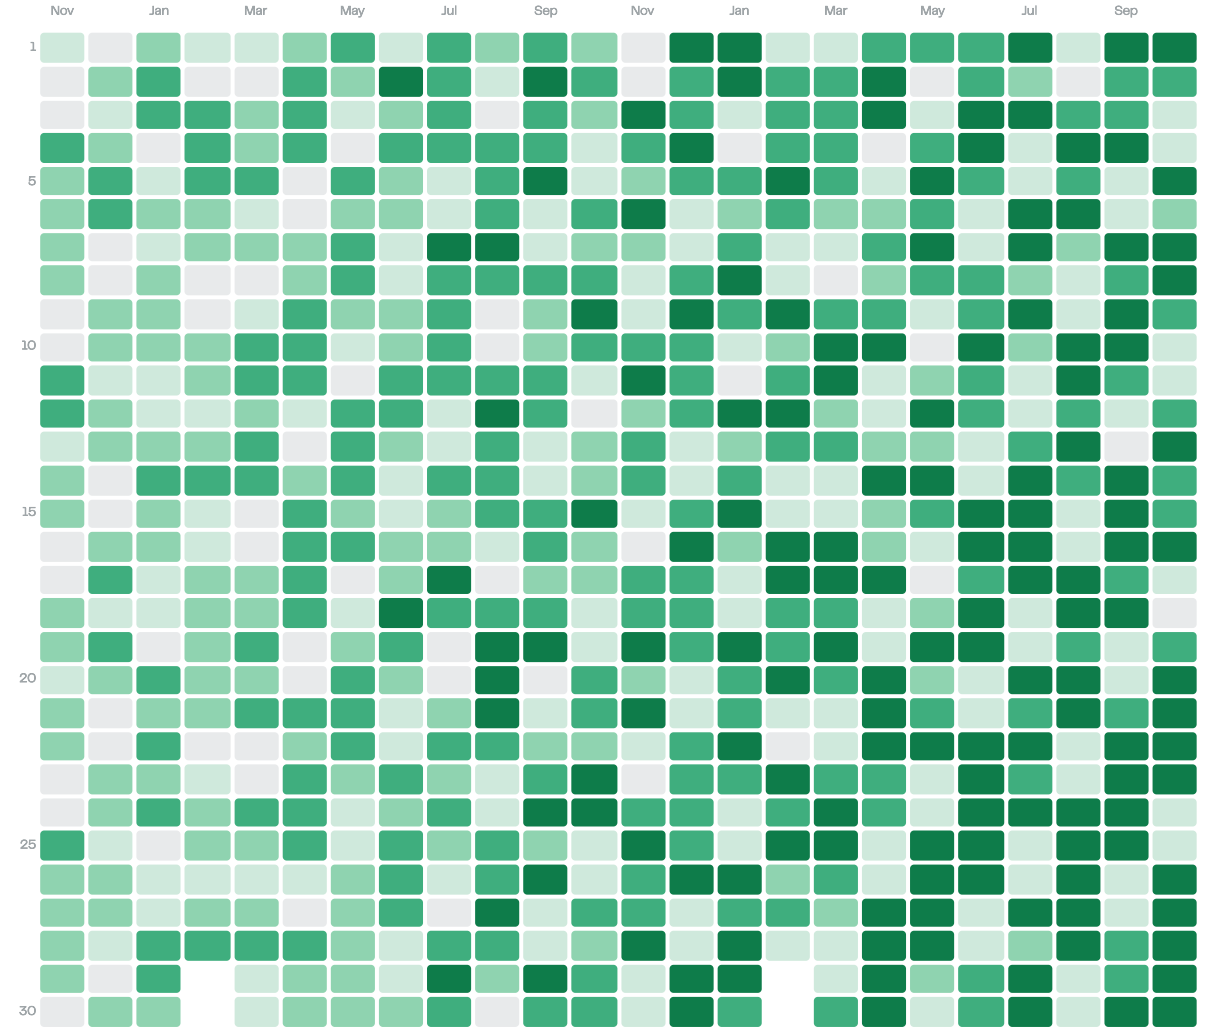

LINES OF CODE None <600 600–1,200 1,200–2,000 2,000+

AI Code Intensity NOV 24 – OCT 26

Share of committed code written by AI.

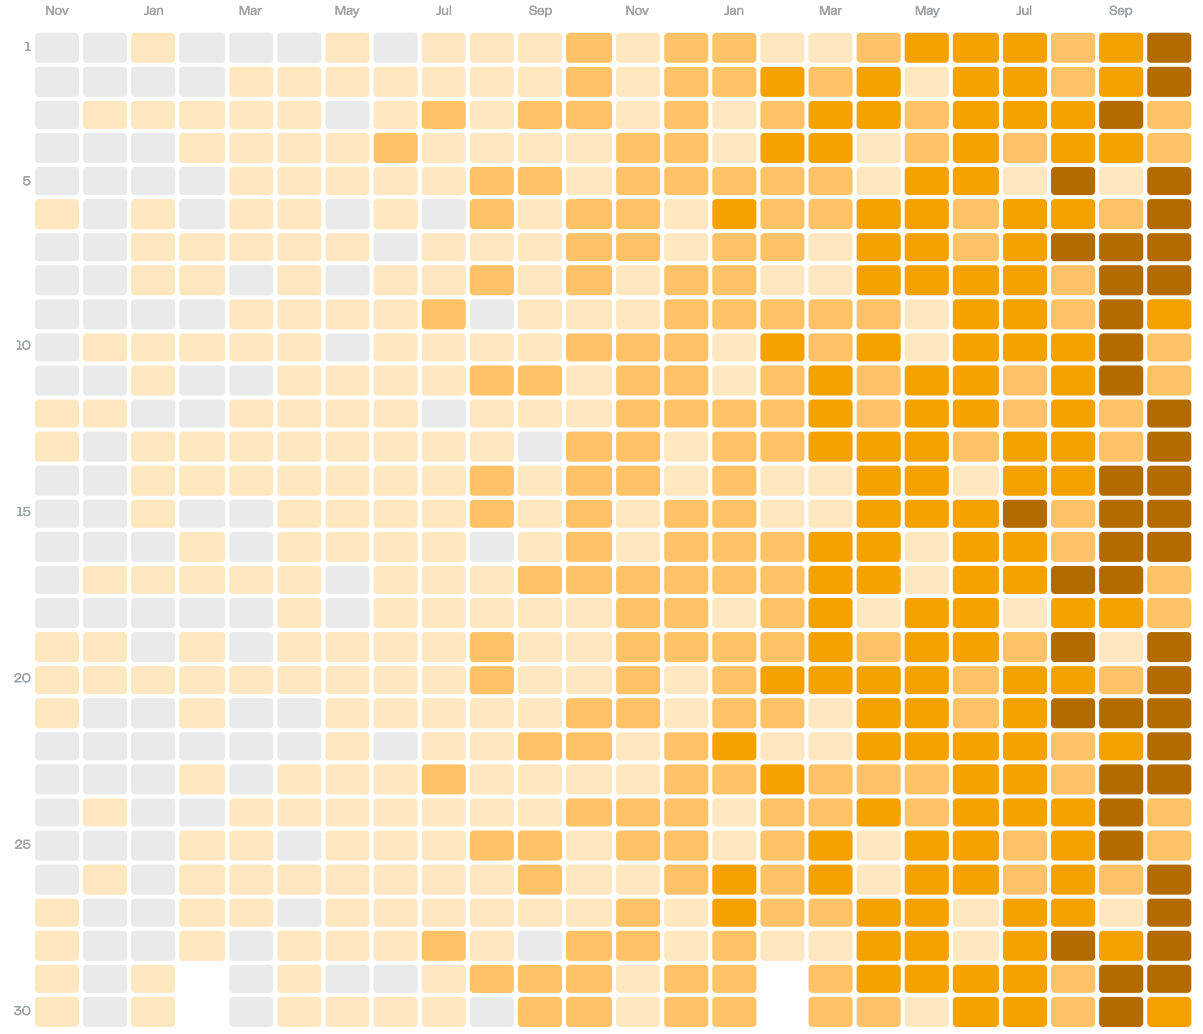


AI SHARE <4% 4–15% 15–28% 28–42% 42%+

SECTION 1 OF 6

Cyber & Infra

2 initiatives reported

1 scoping
1 building

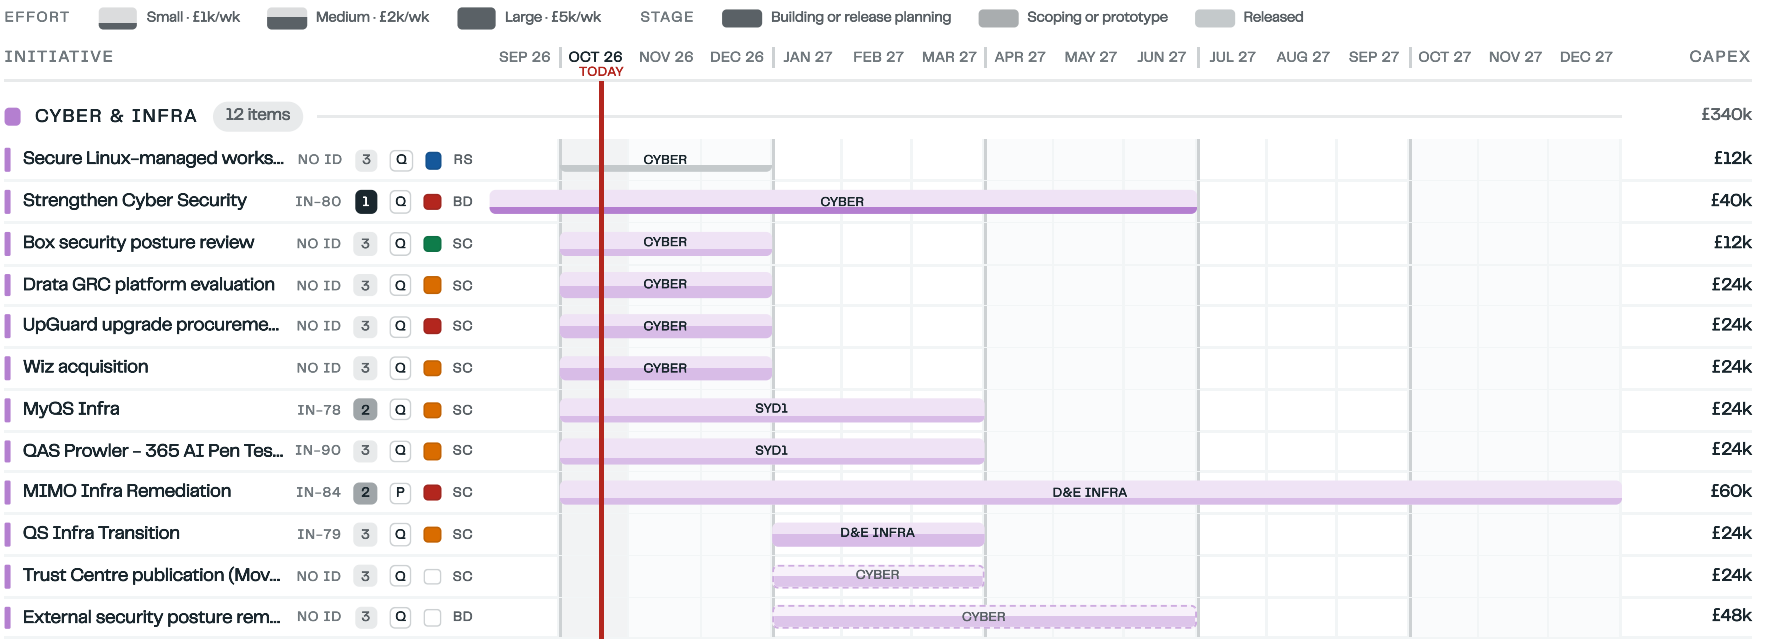

TOTAL CAPEX — 12 of 12 initiatives scheduled · 6 small, 6 medium at £1k / £2k / £5k a week · £268k approved by the investment committee, £72k not yet — £340k

Strengthen Cyber Security

IN-80 · CYBER · SYD1 · BUILDING

Box posture review, GRC platform selection, third-party risk management, endpoint vulnerability reduction. SYD1: tamper-evident admin action record and compliance feed. QS now keeps one tamper-evident record of every administrative action across its cloud estate, and feature-switch changes and HolonIQ exports flow into the compliance feed. Completed a further round of Box stakeholder discovery sessions. Initial findings have identified additional business stakeholders and use cases requiring consultation before recommendations can be finalised. The programme is also managing its first business challenge arising from previously implemented changes, highlighting the sensitivity and complexity of reducing risk in a heavily embedded platform.

MIMO Infra Remediation

IN-84 · INFRASTRUCTURE · MIMO · SCOPING

MoveON MySQL 8.4 cluster and Telemaxx migrations, Redis/Memcached containerisation, SSL automation; MoveIN Elasticsearch test environment and client SSO. Migrated Advanced Publisher staging from standalone MySQL to the new cluster and addressed the AWS NFS bottleneck. Migrated 30 Telemaxx instances to MySQL 8.4.7; remaining migrations are planned over the weekend with scheduled downtime. Completed Redis/Memcached container migration in France and Telemaxx, including application integration and monitoring. Deployed containerised SMTP across Demo, AWS London, AWS Lite and AWS Canada. Successfully tested and enabled scheduled SSL renewal in staging. Merged reusable provisioning prerequisites and implemented locally tested certificate bootstrap for replacement servers.

Cyber

OTHER WORK · NOT LINKED TO AN INITIATIVE

Cyber Awareness Month preparations: Commenced development of cybersecurity awareness content for publication through Inside QS in support of Cyber Awareness Month activities during October. Identity security incidents: Multiple identity-related security incidents were investigated during the last two weeks. Impacted users were notified and appropriate response activities undertaken in accordance with established security processes. Budget and strategy planning: Facilitated a budget planning and strategy workshop with the wider Data Security & Compliance team to support prioritisation, investment planning and alignment of future security initiatives.

Cyber

RISKS AND DECISIONS

Risks and decisions. Box platform constraints and stakeholder impacts. Discovery activities continue to show that Box is... well... an issue and there is resistance to change beginning to emerge. Additional stakeholder engagement is required before recommendations can be finalised. External security rating decline. The introduction of multiple public-facing staging and test assets running end-of-life software, combined with issues associated with future17.org, has negatively impacted QS's external security rating.

MIMO

RISKS AND DECISIONS

Risks and decisions. Service availability. Recurring France service disruption and Telemaxx Advanced Publisher timeouts remain service-availability risks; corrective work and monitoring continue. Repository credentials. Repository credential cleanup remains outstanding, leaving a security risk until remediation is completed.


2027 Data and Engineering Delivery Plan

SECTION 2 OF 6

Data

26 initiatives reported

1 scoping
25 building

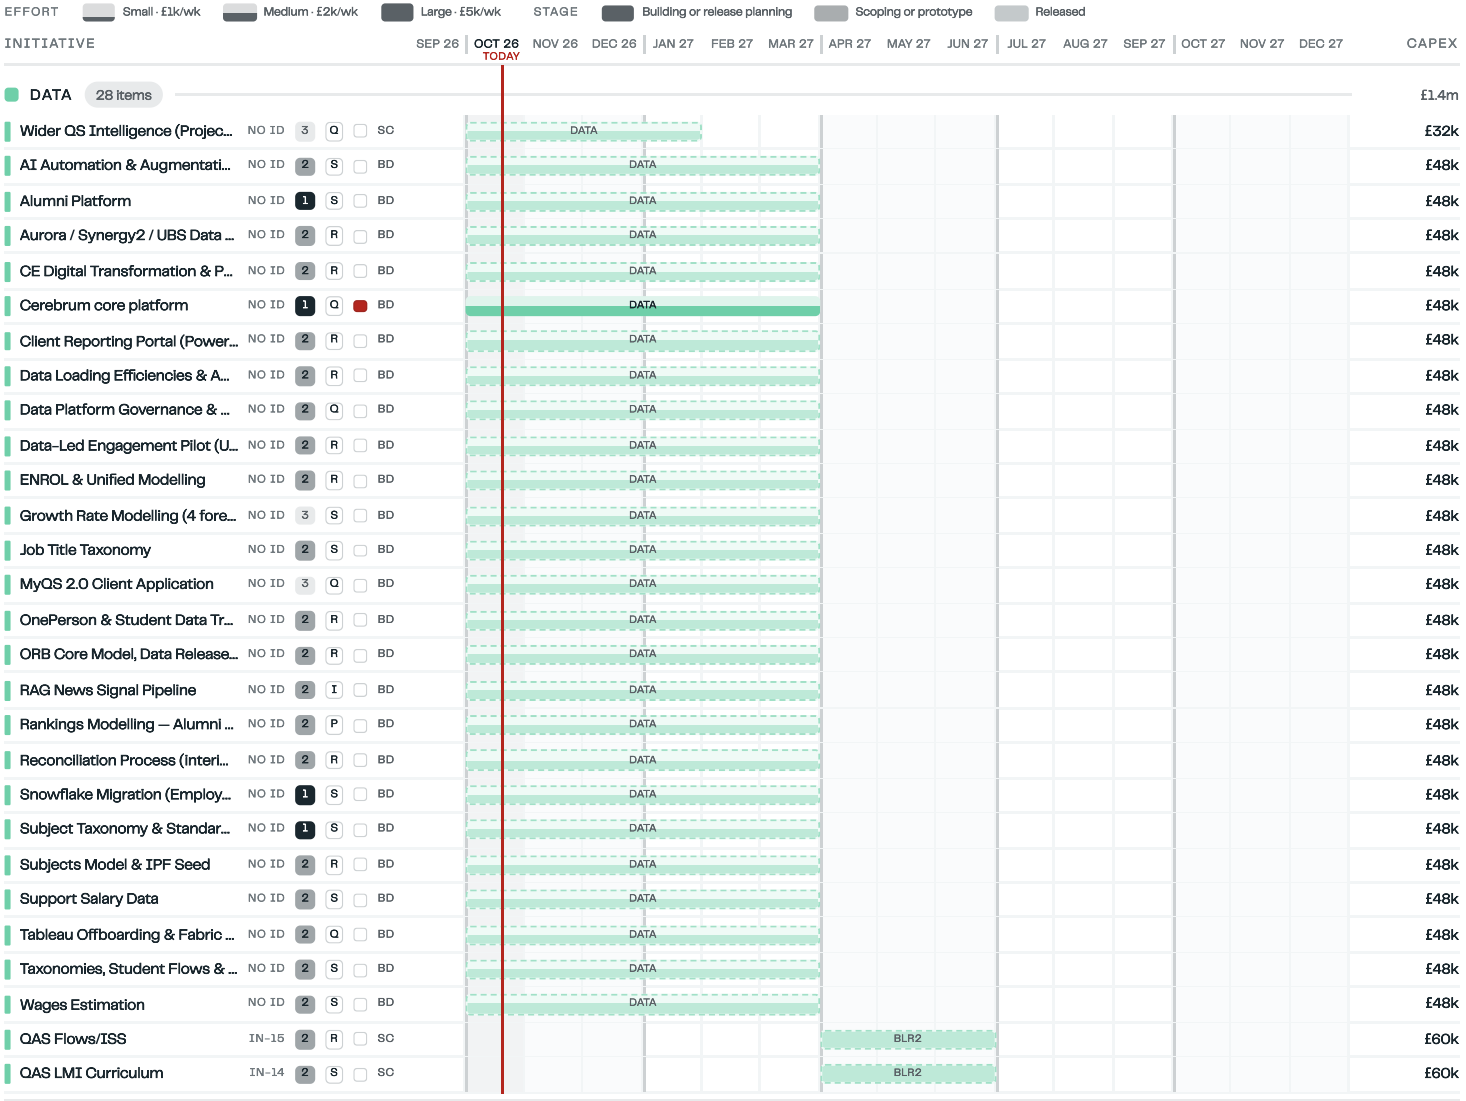

Alumni Platform

NO INITIATIVE NUMBER · DATA TEAM · EMPLOYABILITY & SKILLS · BUILDING

Migrated Snowflake profile datasets handed to Charlie; analytics being restructured to serve consulting and platform needs. Blocker: Awaiting clarity on whether infrastructure/datasets are managed in-house.

Cerebrum core platform

NO INITIATIVE NUMBER · DATA TEAM · DATA & ANALYTICS · BUILDING

Institution identity now read from platform registry; false merge-reviews cut from 2,037 to 633 genuine cases + 51 contradictions. Rankings producer reached first bundle. Blocker: Genuine review queues need steward decisions; supersession can be read but not yet recorded.

Snowflake Migration (Employability)

NO INITIATIVE NUMBER · DATA TEAM · EMPLOYABILITY & SKILLS · BUILDING

Raw/processed GCP pipeline finalised for profile datasets; same approach being extended to job postings. No material blocker this week.

Subject Taxonomy & Standardization

NO INITIATIVE NUMBER · DATA TEAM · EMPLOYABILITY & SKILLS · BUILDING

v2.1 shared for sign-off; Studyportals and UBS mappings finalised and sent for review; service moving into GitHub. Blocker: v3 still needs to close parent-child mapping gaps.

AI Automation & Augmentation Framework

NO INITIATIVE NUMBER · DATA TEAM · LMI · BUILDING

Layer 1 baseline scores complete; Layer 2 v1 implemented but found six structural problems in testing; v2 occupation-specific redesign planned. Blocker: v2 needs real AI-usage data to calibrate adjustments and test against independent adoption evidence.

Aurora / Synergy2 / UBS Data Quality

NO INITIATIVE NUMBER · DATA TEAM · DATA & ANALYTICS · BUILDING

Synergy2 TEST environment live for BI; Deferred/Declined journeys backfilled; comms-direction fixes shipped. Blocker: Persistent UBS defects (course-of-interest, engagements, dates); root cause vs. repair still unclear.

CE Digital Transformation & PBI Migration

NO INITIATIVE NUMBER · DATA TEAM · BUSINESS INTELLIGENCE · BUILDING

Supporting lead-scoring model and B2B/B2C funnel work with Natalie's team. Blocker: Remaining Tableau→Power BI migration tied to the 22 Jan 2027 deadline.

Client Reporting Portal (Power BI)

NO INITIATIVE NUMBER · DATA TEAM · BUSINESS INTELLIGENCE · BUILDING

Greenlight session booked 7 Oct ahead of 16 Oct access target; Sean Coffey's MVP review positive. Blocker: Client user list from AM/CD still outstanding — needed for IT whitelisting and RLS encoding.

Data Loading Efficiencies & Automation

NO INITIATIVE NUMBER · DATA TEAM · BUSINESS INTELLIGENCE · BUILDING

Contact Matching v2 running across all clients; historical source-tag migration nearly complete. Blocker: KCL transformation workflow missed its 30 Sep go-live and still depends on Simon — no revised date committed.

Data Platform Governance & Migration

NO INITIATIVE NUMBER · DATA TEAM · DATA & ANALYTICS · BUILDING

Most Data Science repos moved GitLab→GitHub; Prefect IaC documentation and replica ENROL stack under way. Blocker: Several dbt projects still rely on personal credentials in CI pending service-account access.

Data-Led Engagement Pilot (University of London)

NO INITIATIVE NUMBER · DATA TEAM · DATA & ANALYTICS · BUILDING

Campaign build complete; Stirling lined up as the next campaign. Blocker: reduced delivery cover during the week — 5 Oct launch likely slips a few days.

ENROL & Unified Modelling

NO INITIATIVE NUMBER · DATA TEAM · DATA & ANALYTICS · BUILDING

First model sign-off reporting workflow delivered; course-of-interest models next. Blocker: Jiun left this week after handover — reduced continuity on modelling; UBS data quality remains a dependency.

Job Title Taxonomy

NO INITIATIVE NUMBER · DATA TEAM · EMPLOYABILITY & SKILLS · BUILDING

QSIDs now in hand for the migration. Blocker: Migration delayed until the current mining run concludes — no revised date yet.

OnePerson & Student Data Transformation

NO INITIATIVE NUMBER · DATA TEAM · DATA & ANALYTICS · BUILDING

QS Apply and Appian added as sources; People Data Labs scoping under way; linked to Cerebrum direction. Blocker: PDL field/version choice and Appian–QS Apply–HubSpot overlap still unresolved.

ORB Core Model, Data Releases & QA

NO INITIATIVE NUMBER · DATA TEAM · GLOBAL STUDENT FLOWS · BUILDING

New gap-filling methods tested; test run complete with revised global totals; India 2023–24 updated, Eurostat/Europe update started; tier 1 QA checks defined. Blocker: A bug reducing 2024 country totals for several European countries needs fixing; India 2025 remains an estimate pending official data.

RAG News Signal Pipeline

NO INITIATIVE NUMBER · DATA TEAM · GLOBAL STUDENT FLOWS · BUILDING

Country-sources pipeline rebuilt to match the international design; 21 country-level news sources now parsed alongside GDELT. Blocker: Source quality/licensing and noise from low-quality stories still need clear signal-acceptance rules.

Rankings Modelling — Alumni Impact & Career Alignment

NO INITIATIVE NUMBER · DATA TEAM · EMPLOYABILITY & SKILLS · BUILDING

Restructured to Sam's new spec; subject standardisation, seniority and skill-complexity modelling complete; full indicator modelling begins next sprint. Blocker: Still confirming the primary data source for each Alumni Impact list.

Reconciliation Process (interim)

NO INITIATIVE NUMBER · DATA TEAM · BUSINESS INTELLIGENCE · BUILDING

VW_RECON_RESULT built in Synergy2; Griffith interim list due 7 Oct. Blocker: Huble has stepped back (contract ends 14 Oct) after QS declined 12 extra hours — no vendor fallback; recon scrutiny tied to the GBP 2m budget gap.

Subjects Model & IPF Seed

NO INITIATIVE NUMBER · DATA TEAM · GLOBAL STUDENT FLOWS · BUILDING

university-by-subject data collected for 26 countries (2.5m students), matched to 2,200 of 3,789 QS-ranked universities. Blocker: Relies on Diego's programme mapper; South Asia/India coverage under 20% will lean on modelling, not real data. Major milestone: university-by-subject data collected for 26 countries (2.5m students), matched to 2,200 of 3,789 QS-ranked universities.

Support Salary Data

NO INITIATIVE NUMBER · DATA TEAM · EMPLOYABILITY & SKILLS · BUILDING

Passed PDL's refreshed inferred salary field (with min/max ranges) to LMI; reviewed current LMI wage data against job titles. Blocker: Next steps for the project are pending direction.

Tableau Offboarding & Fabric Transition

NO INITIATIVE NUMBER · DATA TEAM · BUSINESS INTELLIGENCE · BUILDING

Non-renewal notice issued 28 Sep; scoping sent to Consulting/Insights/infra (responses due 16 Oct). Blocker: Consulting's early ask (~50 licences + Server) exceeds the desktop-only notice scope — needs a decision.

Taxonomies, Student Flows & Employability

NO INITIATIVE NUMBER · DATA TEAM · DATA & ANALYTICS · BUILDING

Programme-to-subject mapper deployed to AWS Lambda/Bedrock; Job Posting ingestion moved into active work. Blocker: Subject-level national mappings need explicit crosswalks into the QS taxonomy.

Wages Estimation

NO INITIATIVE NUMBER · DATA TEAM · LMI · BUILDING

2025 median wage estimates complete for 22 of 24 countries; occupational tag rebuild under way. Blocker: US 2025 revalidation awaiting latest BLS data; Canada and Spain estimates still in progress.

Growth Rate Modelling (4 forecasting projects)

NO INITIATIVE NUMBER · DATA TEAM · LMI · BUILDING

24 country workbooks rebuilt on the new CAGR methodology (review under way); ECA/SSA regional bounds built and being tested. Blocker: CAGR validation checks and penetration scoring are still early-stage, with several cross-project dependencies.

MyQS 2.0 Client Application

NO INITIATIVE NUMBER · DATA TEAM · BUSINESS INTELLIGENCE · BUILDING

Stirling prototype expected mid-Nov–early Dec. Blocker: Full build/launch now estimated ~Q2 2027 (pending prototype review).

Wider QS Intelligence (Project Compass)

NO INITIATIVE NUMBER · DATA TEAM · BUSINESS INTELLIGENCE · SCOPING

Groundwork complete (ISS, Rankings, GSF walkthroughs); concept previewed to the business. Blocker: Paused for capacity (client access, end of cycle, HubSpot); no restart date yet.

Business Intelligence

OTHER WORK · NOT LINKED TO AN INITIATIVE

HubSpot Data Quality, Reruns & Backfilling: 57 audit tickets now triaged by business impact under an interim decision group. Blocker: No dedicated data model owner yet; workflows can still fail silently. Data Acquisition QA & Load Reporting: Week 39: 89 loads, 31,844 records, 0 failures, 100% QA pass rate; Macquarie load pulled forward to 1 Oct. Blocker: RCA and KCL data still delayed; Royal College of Art has sent no data since 17 Aug. Other reporting & enablement (stable): No material change or new blockers this week. Internal Reporting Suite: new YoY/MoM pages live; departmental sessions starting. Quality Assurance Team Planning (future state): Future QA tiering and the operating approach are agreed; sequencing set.

Employability & Skills

OTHER WORK · NOT LINKED TO AN INITIATIVE

Mining Run: Final mining run of the year begins 5 Oct, introducing agent-based feedback loops alongside the usual occupation-level run. Blocker: Job-title layer output on hold pending the Job Title Taxonomy migration. 1Mentor / Consulting / Mining Process Improvements: Cyber Essentials review and IBM requirements for 1Mentor; Bath alumni matching; new LLM-based skill-extraction reference under build. No material blocker this week.

Data & Analytics

RISKS AND DECISIONS

Risks and decisions. Aurora / Synergy2 / UBS Data Quality (D&A) — AT RISK: a cross-functional task force is now in place, but persistent UBS defects across course-of-interest records, engagements and dates remain — the priority is finding where bad data originates, not just repairing history. Data-Led Engagement Pilot, University of London (D&A) — AT RISK: the 5 Oct launch is likely to slip a few days on reduced delivery cover; Stirling is next once readiness is restored.

Business Intelligence

RISKS AND DECISIONS

Risks and decisions. Reconciliation Process (BI) — AT RISK: Huble has exited (contract ends 14 Oct) with nothing usable delivered; BI's own interim build is now the likely permanent process, and — given the GBP 2m gap to budget — its coverage and exclusions will be closely scrutinised. Data Loading Efficiencies & Automation (BI) — OFF TRACK: the KCL transformation workflow missed its 30 Sep go-live and still depends on Simon with no revised date; RCA remains the only client live on the new workflow.

Employability & Skills

RISKS AND DECISIONS

Risks and decisions. Support Salary Data (Employability) — AT RISK: PDL's refreshed inferred salary field has been passed to LMI, but how the project evolves next is waiting on direction from Bledi. Job Title Taxonomy (Employability) — AT RISK: QSIDs are in hand, but migration to the new job title layer can't start until the current mining run concludes — no date yet.

Global Student Flows

RISKS AND DECISIONS

Risks and decisions. Relies on Diego's programme mapper; South Asia/India coverage under 20% will lean on modelling, not real data. A bug reducing 2024 country totals for several European countries needs fixing; India 2025 remains an estimate pending official data. Source quality/licensing and noise from low-quality stories still need clear signal-acceptance rules.

LMI

RISKS AND DECISIONS

Risks and decisions. v2 needs real AI-usage data to calibrate adjustments and test against independent adoption evidence. CAGR validation checks and penetration scoring are still early-stage, with several cross-project dependencies. US 2025 revalidation awaiting latest BLS data; Canada and Spain estimates still in progress.


2027 Data and Engineering Delivery Plan

SECTION 3 OF 6

Core

3 initiatives reported

1 prototype
2 building

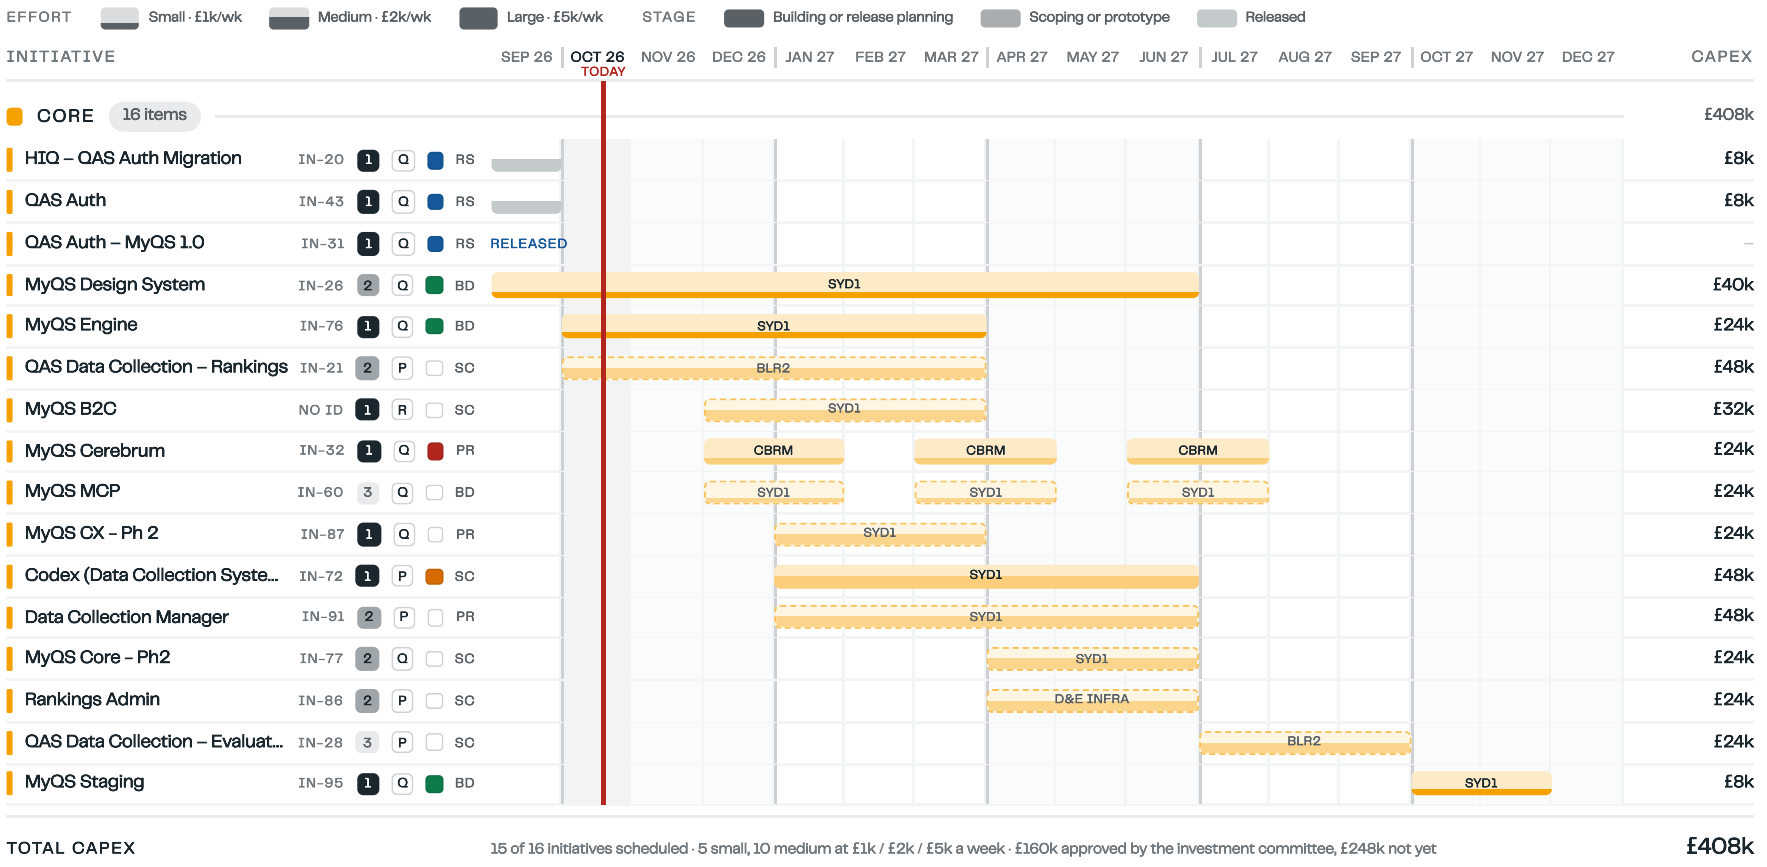

TOTAL CAPEX — 15 of 16 initiatives scheduled · 5 small, 10 medium at £1k / £2k / £5k a week · £160k approved by the investment committee, £248k not yet — £408k

MyQS CX – Ph 2

IN-87 · SYD1 · PROTOTYPE

CX bulk user import in production, HolonIQ export activity in the access feed, embargo-dates page live behind its switch. CX admins can bulk-import users in production, see HolonIQ export activity in the access feed, and the embargo-dates page is live behind its switch.

MyQS Staging

IN-95 · SYD1 · BUILDING

single reviewed release pipeline for every front end; six production apps moved to code-managed; first release flags live in production. Features can be switched on or off for staff and customers without a new release; every switch is audited, a revert was rehearsed in staging before the first production change, and the first two switches are live in production. Every QS front end ships from one reviewed pipeline: builds are identical wherever they run, each release records exactly what was tested, old tabs refresh themselves, and six production apps moved from hand-managed to code-managed with a written release and rollback procedure.

MyQS Design System

IN-26 · SYD1 · BUILDING

instant account switching, Ranking Master accounts labelled Primary, rankings board insights in production, two design releases. Switching accounts in any QS app is now instant and shows which products each account opens; Ranking Master accounts are labelled Primary; after accepting an invitation the new account appears at once and administration menus follow the shell's access rules; rankings board insights and the template's overview readings reached production; two design releases rolled out to every app.

SYD1

OTHER WORK · NOT LINKED TO AN INITIATIVE

QS Auth: Staging sign-in is limited to QS staff addresses, and apps learn which products an account holds the moment it signs in.

SECTION 4 OF 6

Sector Intelligence

7 initiatives reported

1 scoping
3 prototype
2 building
1 release planning

EFFORT Small · £1k/wk Medium · £2k/wk Large · £5k/wk STAGE Building or release planning Scoping or prototype Released

INITIATIVE						SEP 26	OCT 26 TODAY	NOV 26	DEC 26	JAN 27	FEB 27	MAR 27	APR 27	MAY 27	JUN 27	JUL 27	AUG 27	SEP 27	OCT 27	NOV 27	DEC 27	CAPEX
SECTOR INTELLIGENCE	22 items																					£428k
Analytics: User Tracking …	IN-63	2	Q	RS	RELEASED																	–
QAS Factfiles	IN-33	1	P	RS	RELEASED																	–
QAS MyQS Legacy	IN-38	3	Q	RS	RELEASED																	–
Partner Discovery – Phase 1	IN-94	1	R	PR		BLR2																£16k
1 Mentor IBM	IN-19	2	S	BD		ECU1				ECU1												£20k
QAS Stars	IN-46	1	P	RP																		£8k
Rankings Template	IN-18	1	P	SC			SYD1															£16k
Analytics: Downloads for …	IN-61	2	Q	BD			BLR2															£12k
QAS Alumni Insights	IN-25	2	S	PR			BLR2															£32k
QAS Regional Rankings	IN-51	3	P	PR						BLR2												£24k
QAS Subject Rankings	IN-92	3	P	PR						BLR2												£24k
QAS WUR	IN-93	3	P	PR						BLR2												£24k
Student Insights	NO ID	2	S	SC						BLR2												£12k
1 Mentor Multilingual	IN-34	3	S	BD									ECU1									£12k
IST Data Validation	IN-73	2	P	SC									BLR2									£24k
QAS Business Schools	IN-52	3	P	SC												BLR2						£60k
QAS Sustainability	IN-50	3	P	PR												BLR2						£24k
Partnerships New	IN-16	3	R	SC												BLR1						£120k
MoveIN Smart Match / AI Em…	IN-89	2	R	BD	NOT SCHEDULED																	–
QAS AI Evaluation	IN-36	3	I	SC	NOT SCHEDULED																	–
QAS Reputation	IN-55	3	P	SC	NOT SCHEDULED																	–
QS One	IN-41	3	Q	SC	NOT SCHEDULED																	–

TOTAL CAPEX — 15 of 22 initiatives scheduled · 4 small, 9 medium, 2 large at £1k / £2k / £5k a week · £200k approved by the investment committee, £228k not yet — £428k

Partner Discovery – Phase 1

IN-94 · BLR2 · PROTOTYPE

video tutorials, more accurate profile analytics, unified interest dashboard, contributor permissions, Plan & Usage refresh; QA in progress. Added a Video Tutorials library inside Partner Discovery so institutions can learn how to use the module without leaving the page. Made profile analytics meaningfully more accurate: visits from an institution's own staff no longer inflate the numbers, visits to shared public profile pages are now counted, shared links are clearly labelled as shared visits with the sender's search details stripped out, and each visit source has a clearer explanation on the dashboard. Simplified the analytics dashboard by removing low-use tiles and ranked lists. Added expired partnerships to the partnership map and activity view so institutions can see their full partnership history.

QAS Stars

IN-46 · BLR2 · RELEASE PLANNING

MyQS Stars shows the latest audit by subscription date; AI Insights panel hidden while being finalised. Fixed data correctness across MyQS Stars so every institution now sees the most recent audit, including the right indicator-level data based on their subscription history — closing a gap where some renewed or re-audited institutions were still being shown older audit data. Hid the in-progress AI Insights panel in the Stars Category Deep Dive so users only see finished, reviewed content while that feature is being finalised.

Rankings Template

IN-18 · SYD1 · SCOPING

data graph can rank entities other than institutions; safer table-scoped data moves between environments. Rankings in the data graph can now rank entities other than institutions, and moving data between environments is safer: table-scoped, locked against concurrent writers, and rehearsed on a clone before production.

1 Mentor IBM

IN-19 · ECU1/ECU2 · ECU1 AND ECU2 · BUILDING

release 74.27.7 (IBM login page text and legal disclaimer); job title recommendation fix with QA. getJobTitleRecommendationByMajorIds without limited occupations (IBM). Bug: getJobTitleRecommendationByMajorIds without limited occupations (IBM).

MoveIN Smart Match / AI Email

IN-89 · MOVEIN · BUILDING

AI brand detection and template tools, email brand compliance, AI usage reporting, feature prompts, guided contact matching. new AI capabilities automatically detect an institution's brand style from its website and speed up email campaign creation, helping teams produce on-brand communications with less manual work. outgoing emails now maintain consistent, professional branding automatically, reducing manual formatting corrections. administrators can now see clear, easy-to-read reports of AI usage, supporting better oversight and planning. new in-app prompts introduce first-time users to the AI email tools, encouraging adoption. a new step-by-step walkthrough helps users complete automated contact matching more easily, which should reduce support requests.

QAS Alumni Insights

IN-25 · SYD1 · PROTOTYPE

pre-computed aggregates in the governed serving layer; first staging-to-production promotion. Answers every question from pre-computed aggregates instead of crunching in the browser, and its data sits in the governed serving layer alongside rankings; the first staging-to-production promotion went through.

QAS WUR

IN-93 · SYD1 · PROTOTYPE

HolonIQ hardened and monitored; WUR Highlights shows nomination sources. HolonIQ on the QS estate is hardened and monitored — secure-by-default connections, alarms on every environment, slow queries capped in production; WUR Highlights shows where academic and employer nominations come from; HolonIQ exports now appear in QS's compliance feed; the legacy regional export is kept off production.

BLR1

OTHER WORK · NOT LINKED TO AN INITIATIVE

HUB2: All newly added sprint work is development complete and currently with QA before deployment: Added a rich-text scholarship description field to support profile-specific content. QPD / MyQS: Completed the development-side institution reconciliation and provided a report identifying missing records and gaps between HUB2 and QPD. Accord: Generated the Accord leads report covering 1 January 2024 to date, with PII removed and replaced by indicators showing whether each data field is present or missing. HUB1: No active work was assigned during this sprint.

ECU1 and ECU2

OTHER WORK · NOT LINKED TO AN INITIATIVE

The "View More" button in the mobile skill modal was not working. PLAR tasks: configurable login page text and contact info; add experience source tag; hide skill suggestions and set resume upload as the default empty state; configurable confirmation page; route to confirmation page after the wizard and end the journey.

MoveIN

OTHER WORK · NOT LINKED TO AN INITIATIVE

Faster Record Reconciliation: improved tracking and bulk actions let teams review and reconcile university records more quickly. Simplified Data Imports: a clearer import process reduces errors when teams upload new contact data. Easier Bulk Updates: marketing and admissions teams can now update contact records in bulk using just an email address, cutting manual data entry. Expanded Chinese Language Support: the platform now supports Chinese across more areas, improving accessibility for users in that region. Interface Polish: minor display and formatting issues were fixed, improving overall consistency of the user experience.

BLR2

RISKS AND DECISIONS

Risks and decisions. No blockers, outstanding decisions, or major risks flagged this week.

ECU1 and ECU2

RISKS AND DECISIONS

Risks and decisions. No risks or decisions required at the moment. The new sprint starts this Wednesday. ECU1 and ECU2 are currently fully focused on 1 Mentor, so if either team is considered for another project, advance notice would help the teams assess the impact on their deliverables.

MoveIN

RISKS AND DECISIONS

Risks and decisions. Infrastructure upgrade demo timing. Timing for an infrastructure version upgrade demo has not been finalised and depends on upcoming quality-assurance feedback.


2027 Data and Engineering Delivery Plan

SECTION 5 OF 6

D&E

2 initiatives reported

1 prototype
1 released

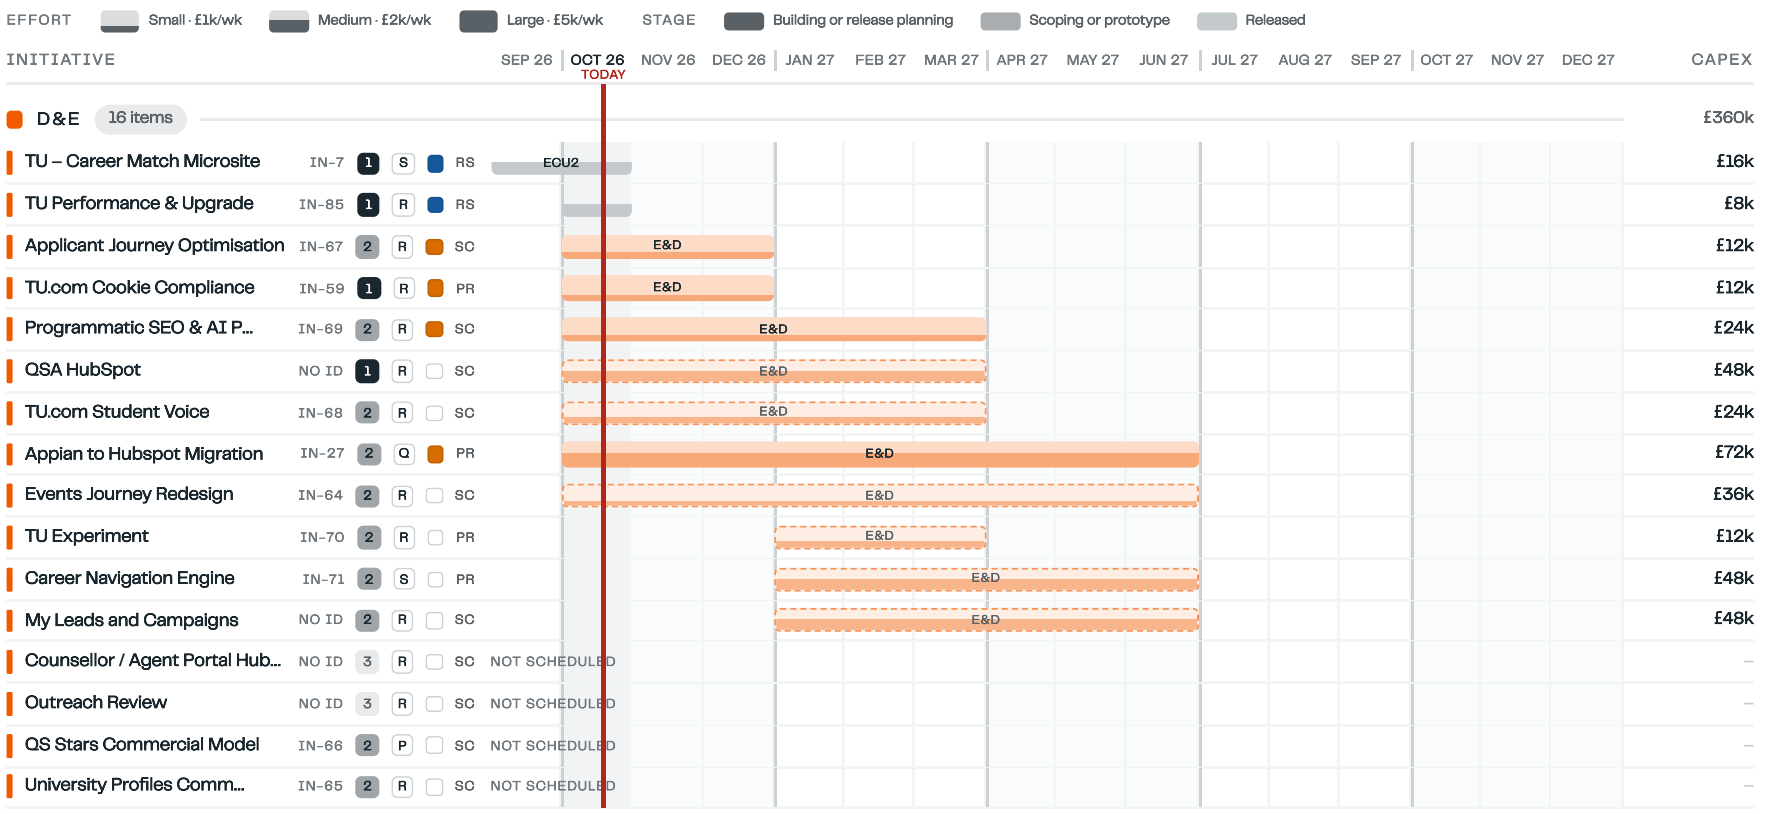

TOTAL CAPEX — 12 of 16 initiatives scheduled · 6 small, 6 medium at £1k / £2k / £5k a week · £144k approved by the investment committee, £216k not yet — £360k

TU Performance & Upgrade

IN-85 · DIGITAL AND EVENTS · RELEASED

TU performance changes awaiting release; Drupal 11.4.8 in testing. Infrastructure: PHP 8.4 and Drupal 11.4.8 across TU and TM non-production. Last batch of changes is waiting release. A decision has been made to upgrade to a higher version, so instead of 11.3.16 the plan is now to upgrade to Drupal 11.4.8. All non-prod environments have been upgraded and testing is under way.

Appian to Hubspot Migration

IN-27 · QS APPLY · QS APPLY (APPIAN) · PROTOTYPE

Appian migration documentation review and consolidation. The team continues to review and consolidate the migration documentation, based on the findings and information gathered during the discovery phase.

Digital and Events

OTHER WORK · NOT LINKED TO AN INITIATIVE

Drupal clean-up: Last batch of changes is waiting release. Convert CMT module from React to Drupal: Waiting release. Agenda builder: This is still waiting business validation.

QS Apply (Appian)

OTHER WORK · NOT LINKED TO AN INITIATIVE

Multi-Factor Authentication (MFA): implemented MFA functionality in the TEST environment in preparation for the mandatory MFA rollout in Production by 1 December 2026. Referral Partner Visibility: added Referral Partner names to the Agent Partner dropdown in the Applicant Dashboard to improve partner identification and selection. Referral Partner Username Update: investigated and resolved an error encountered while updating the username for a referral partner.

D&E

OTHER WORK · NOT LINKED TO AN INITIATIVE

Completed HUB1 production server switchover and temporarily stopped two unused development/staging servers to reduce unnecessary resource consumption. Progressed HUB1 repository migration from Beanstalk to GitHub and tested GitHub Actions deployment pipelines in development. Advanced DMARC analysis and enforcement preparation, including correcting MoveON Germany's email-domain authentication and supporting DNS records. Restored GenAI bot functionality through a temporary API-key rollback while investigating Enterprise migration and runner issues and replicating the workflow in the team's account. Resolved HUB2 client-tracking URL upload issues through a targeted Cloudflare WAF exception while retaining existing protection.

Digital and Events

RISKS AND DECISIONS

Risks and decisions. Drupal sprint release. It was agreed with product that this would be delayed, since Drupal needs to be upgraded first. Early next week the team will decide whether all conditions are in place to do the upgrade, depending on testing and on when the sprint code can be released. Redesign of QSA page. Waiting for clear requirements and form changes.

D&E

RISKS AND DECISIONS

Risks and decisions. GenAI workaround. GenAI functionality currently relies on a temporary workaround; the permanent Enterprise configuration remains unresolved.

SECTION 6 OF 6

University Services

2 initiatives reported

1 prototype
1 building

EFFORT Small · £1k/wk Medium · £2k/wk Large · £5k/wk STAGE Building or release planning Scoping or prototype Released

INITIATIVE					SEP 26	OCT 26 TODAY	NOV 26	DEC 26	JAN 27	FEB 27	MAR 27	APR 27	MAY 27	JUN 27	JUL 27	AUG 27	SEP 27	OCT 27	NOV 27	DEC 27	CAPEX
UNIVERSITY SERVICES 15 items																					£316k
Aurora – Student Scoring Mo…	IN-56	2	R	BD		UBS DEV															£12k
Aurora Data Integrity	IN-82	1	R	BD		UBS DEV															£16k
Aurora Implementation	IN-30	1	R	RP		UBS DEV															£32k
Appian to Hubspot Migration	IN-54	1	Q	PR		UBS DEV															£56k
Decommission Informatica	IN-88	1	R	BD		UBS DEV															£48k
QAS Uni Svcs Reporting App	IN-40	2	R	PR			UBS DEV														£16k
Aurora – Counsellor Feedback	IN-53	2	R	SC			UBS DEV														£32k
Aurora – Document Credibility	IN-8	2	R	SC			UBS DEV														£32k
Aurora – Student Sentiment I…	IN-48	2	R	PR			UBS DEV														£32k
Aurora – Client Data API	IN-81	2	R	BD				UBS DEV													£40k
Aurora – WeChat	IN-47	2	R	PR	NOT SCHEDULED																–
Flat File Uploads	IN-97	2	R	SC	NOT SCHEDULED																–
Rebuild Enquiry APIs	IN-96	2	R	SC	NOT SCHEDULED																–
Uni Services – Productivity Das…	IN-9	2	R	PR	NOT SCHEDULED																–
Uni Svcs – Operational Tickets	IN-49	2	R	BD	NOT SCHEDULED																–

TOTAL CAPEX — 10 of 15 initiatives scheduled · 2 small, 8 medium at £1k / £2k / £5k a week · £100k approved by the investment committee, £216k not yet — £316k

Appian to Hubspot Migration

IN-54 · UBS DEVELOPMENT · QS APPLY (APPIAN) · PROTOTYPE

enquiry-form and ESI replacements (Keele, RCA, Griffith, ACU, Stirling). QS Apply: migration documentation. The team continues to review and consolidate the migration documentation, based on the findings and information gathered during the discovery phase. Replacements for Keele and RCA are ready for testing. Griffith and ACU are undergoing changes for auto ticket creation. Stirling development work is still under way, as the data mapping discussion is ongoing with CDM.

Decommission Informatica

IN-88 · UBS DEVELOPMENT · BUILDING

Informatica replacements via S3 flat file (Griffith, ECU, Brighton, Stirling), Keystone (RCA, ECU) and York. RCA and ECU have been fixed in the sandbox environment following testing and are now ready for validation. Continued working on the Informatica York Integration to pull data from Dynamics after adding the deposit status column. Griffith's replacement is awaiting deployment, pending the API replacement.

UBS Development

OTHER WORK · NOT LINKED TO AN INITIATIVE

AI Chatbot functionality in HubSpot: Performed a test run for chatbot test automation.

CX Systems

OTHER WORK · NOT LINKED TO AN INITIATIVE

QS Events: conducted the SMS Sakari demo and training. QS Events: troubleshot the SMS workflow and reported the Helpdesk authentication issue to Sakari. HubSpot: troubleshot the Helpdesk connection issue in the B2C HubSpot portal. Stirling: extracted and provided the requested call logs from Twilio. Lincoln: implemented IVR changes. Aircall: communicated the double-window calling bug to Aircall and provided supporting evidence. Aircall: reviewed the outage and broadcast the relevant information to the team. Aircall: onboarded new users. Number porting: re-initiated the process of porting Twilio numbers to Aircall. SIP: followed up on SIP implementation. Callbacks: started initial work on Sakari and Vira automations for callbacks.

UBS

OTHER WORK · NOT LINKED TO AN INITIATIVE

Provisioned S3 access for four clients and resolved an S3 access issue. Configured Snowflake accounts, roles, grants and keys, and established GCP storage integration. Conducted EMEA CRMS Oracle database recovery testing and disabled an EMEA client in Synergy.

UBS Development

RISKS AND DECISIONS

Risks and decisions. Contact Matching in Sandbox. Still not able to fully test Contact Matching in Sandbox due to issues promoting data from production to sandbox, caused by missing data objects. Testing will proceed in Sandbox without Contact Matching. UoL licensing. One institution's test environment (UoL) is missing required licensing to proceed with development. Simon is arranging access. HubSpot x HubSpot data model. Clare is awaiting the Data Model from Daniel before development on the HubSpot x HubSpot integration can begin.

CX Systems

RISKS AND DECISIONS

Risks and decisions. Sunway AI Chatbot. Work is delayed because the required data source has not yet been provided.
