WEEK 41 · 5–9 OCTOBER 2026

2027 Data and Engineering Delivery Plan

Week 41 Delivery Report

What moved this week, initiative by initiative, with the delivery schedule it sits in.

Cyber & Infra · Data · Core · Sector Intelligence · D&E · University Services

THE WEEK AT A GLANCE

Cyber & Infra 9 INITIATIVES

Outcomes. 9 initiatives moved, led by Strengthen Cyber Security, MIMO Infra Remediation, Box security posture review.

Risks & decisions. UpGuard procurement timeline risk. There is budget for this purchase and extended delays may see QS miss the opportunity to capitalise before the budget is reallocated. MySQL 8.4 issues.

Data 9 INITIATIVES

Outcomes. 9 initiatives moved, led by Snowflake Migration (Employability), Subject Taxonomy & Standardization, Data Platform Governance & Migration.

Risks & decisions. Nothing raised this week.

Core 4 INITIATIVES

Outcomes. 4 initiatives moved, led by MyQS Cerebrum, MyQS CX – Ph 2, MyQS Staging. QS Supergraph welcomes its newest member: the institution registry. Cerebrum institutions — geography, subjects and occupations — now answer inside the data graph on both staging and production.

Risks & decisions. Confirm the remediation owner and expected route for the University of London course and intake defect before London inference is reconsidered.

Sector Intelligence 4 INITIATIVES

Outcomes. 4 initiatives moved, led by Partner Discovery – Phase 1, Rankings Template, MoveIN Smart Match / AI Email. QS Supergraph welcomes its newest member: the institution registry.

Risks & decisions. Limited historical records. Limited availability of historical change logs or legacy records may constrain the depth of analysis for ongoing investigations. Hackathon timing managed. Last week, the hackathon was considered a risk due to the tight timeline.

D&E 2 INITIATIVES

Outcomes. 2 initiatives moved, led by TU Performance & Upgrade, Appian to Hubspot Migration. The Agenda builder management system in Outreach has been released.

Risks & decisions. Drupal sprint release. Because of the new rankings release in the upcoming week and the hackathon, it was decided to postpone this to 19 October. Redesign of QS Apply page. Waiting for clear requirements and form changes — still pending.

University Services 3 INITIATIVES

Outcomes. 3 initiatives moved, led by Appian to Hubspot Migration, Aurora Data Integrity, Decommission Informatica. The Appian dev team has commenced work on developing integration replacements for enquiry forms within HubSpot.


Risks & decisions. UoL licensing. One institution's test environment (UoL) is missing required licensing to proceed with development. Simon Pennington is arranging access. HubSpot x HubSpot data model.


Contents

Delivery schedule 3
Engineering activity 4
Cyber & Infra 5
Data 8
Core 11
Sector Intelligence 14
D&E 18
University Services 21

2027 Data and Engineering Delivery Plan


Delivery schedule 109 initiatives

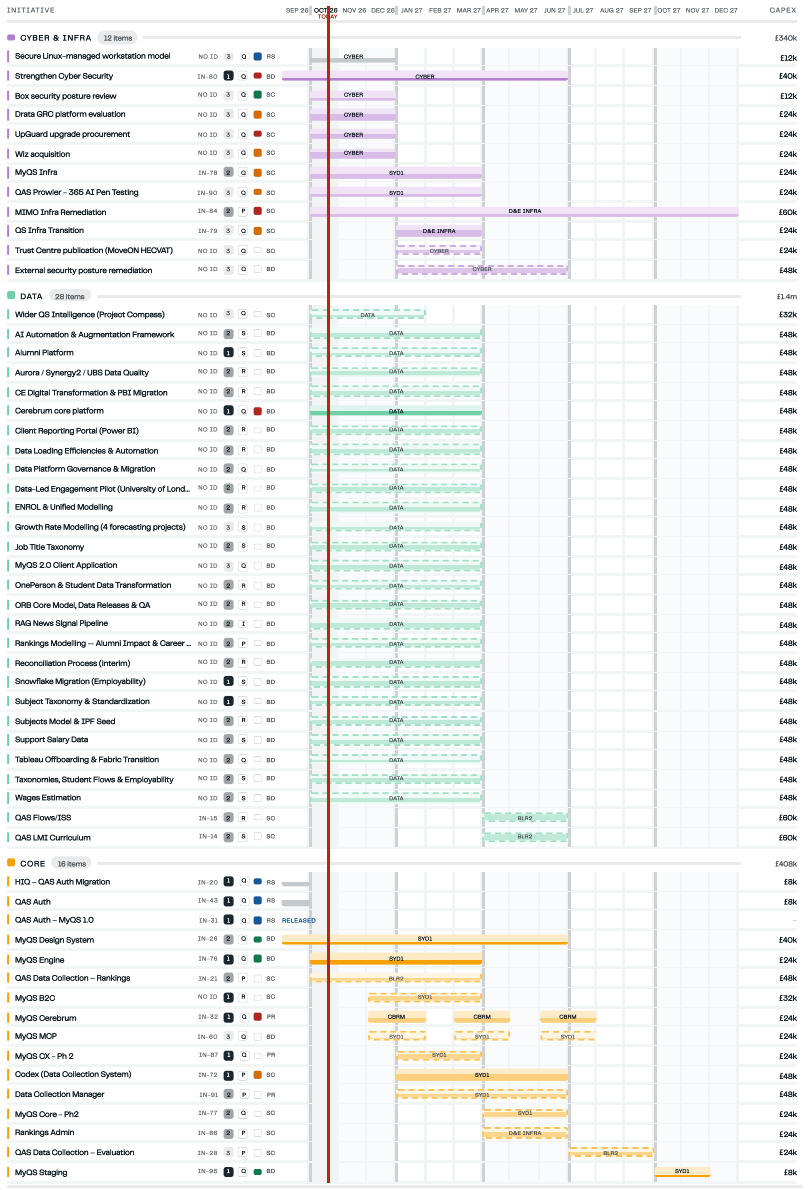

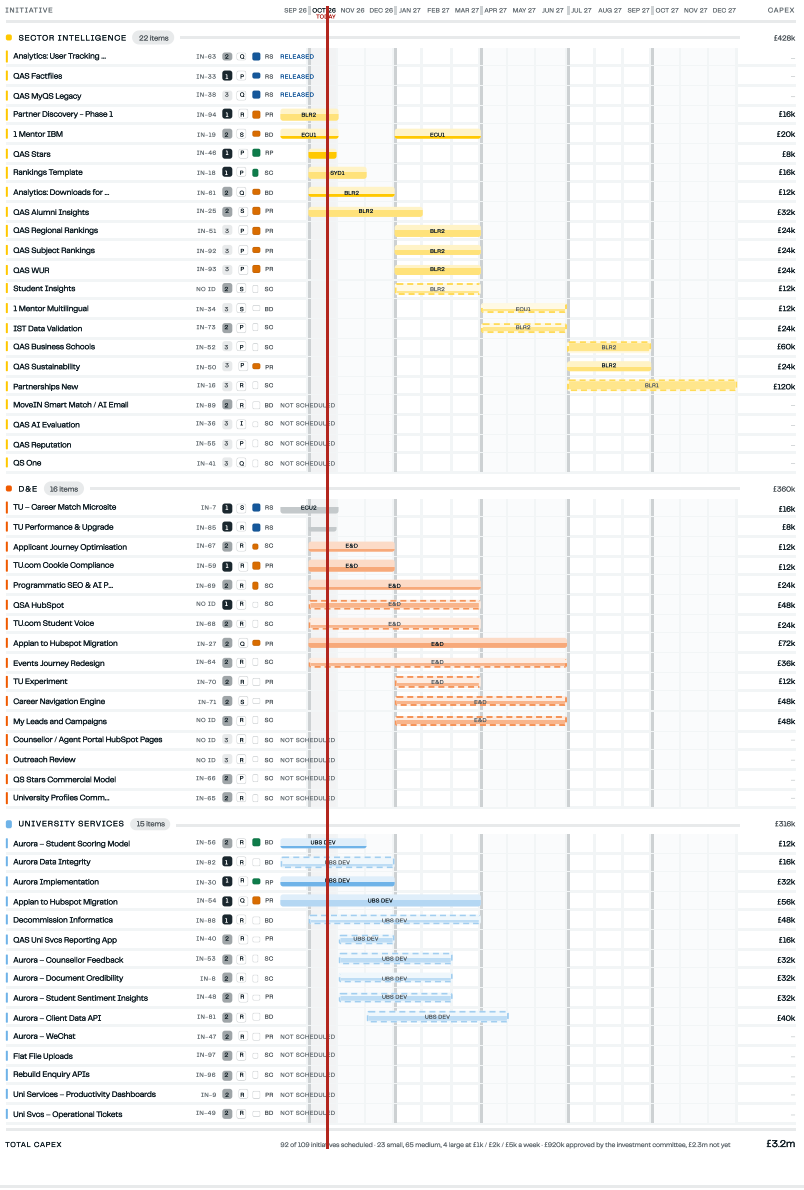


Productivity Heatmap NOV 24 – OCT 26

Lines of code committed a day.

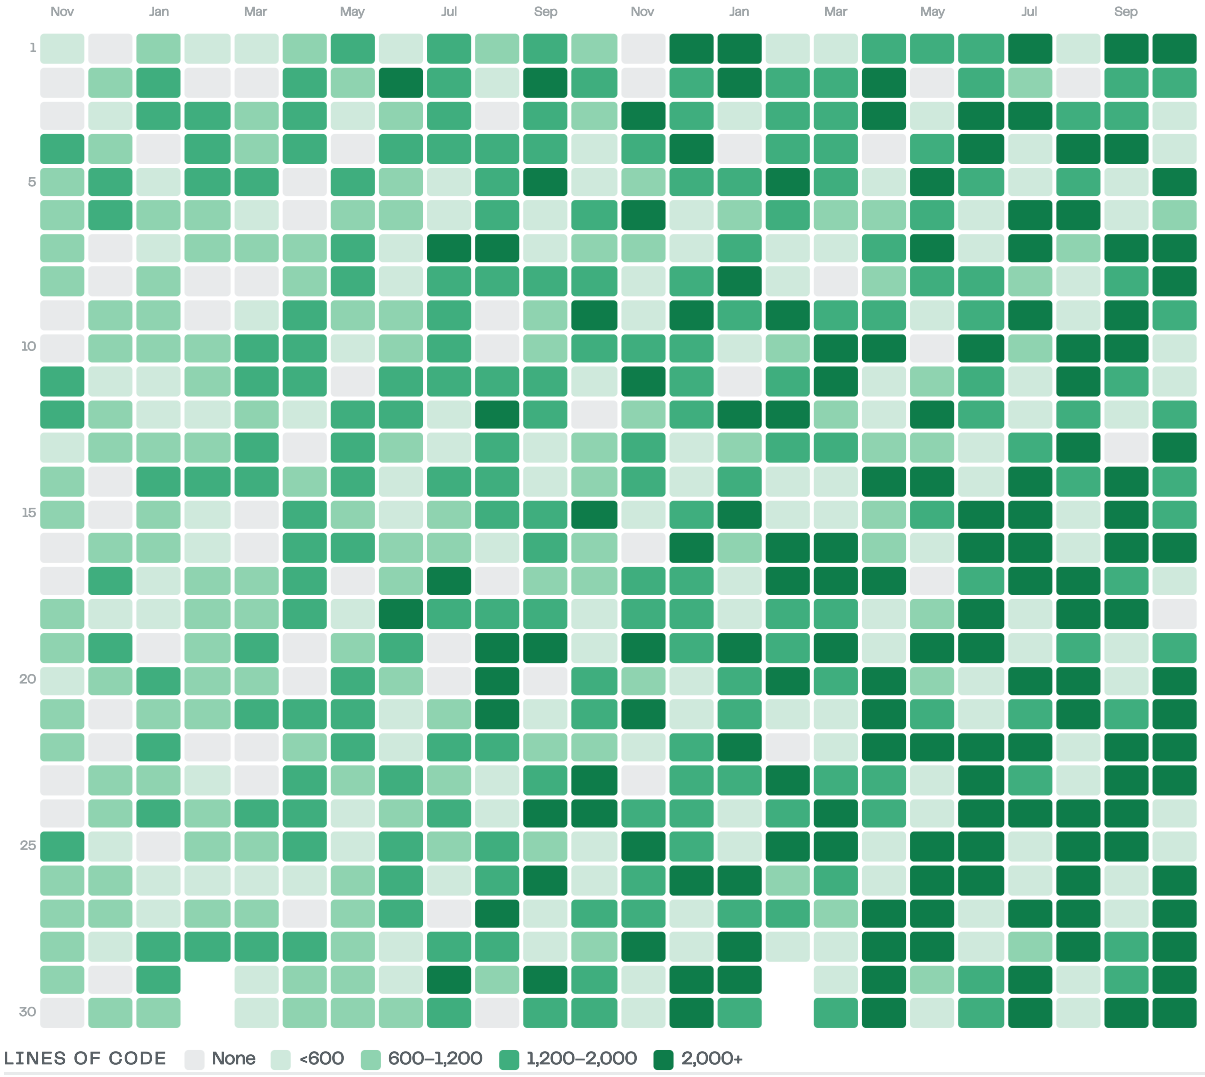

AI Code Intensity NOV 24 – OCT 26

Share of committed code written by AI.

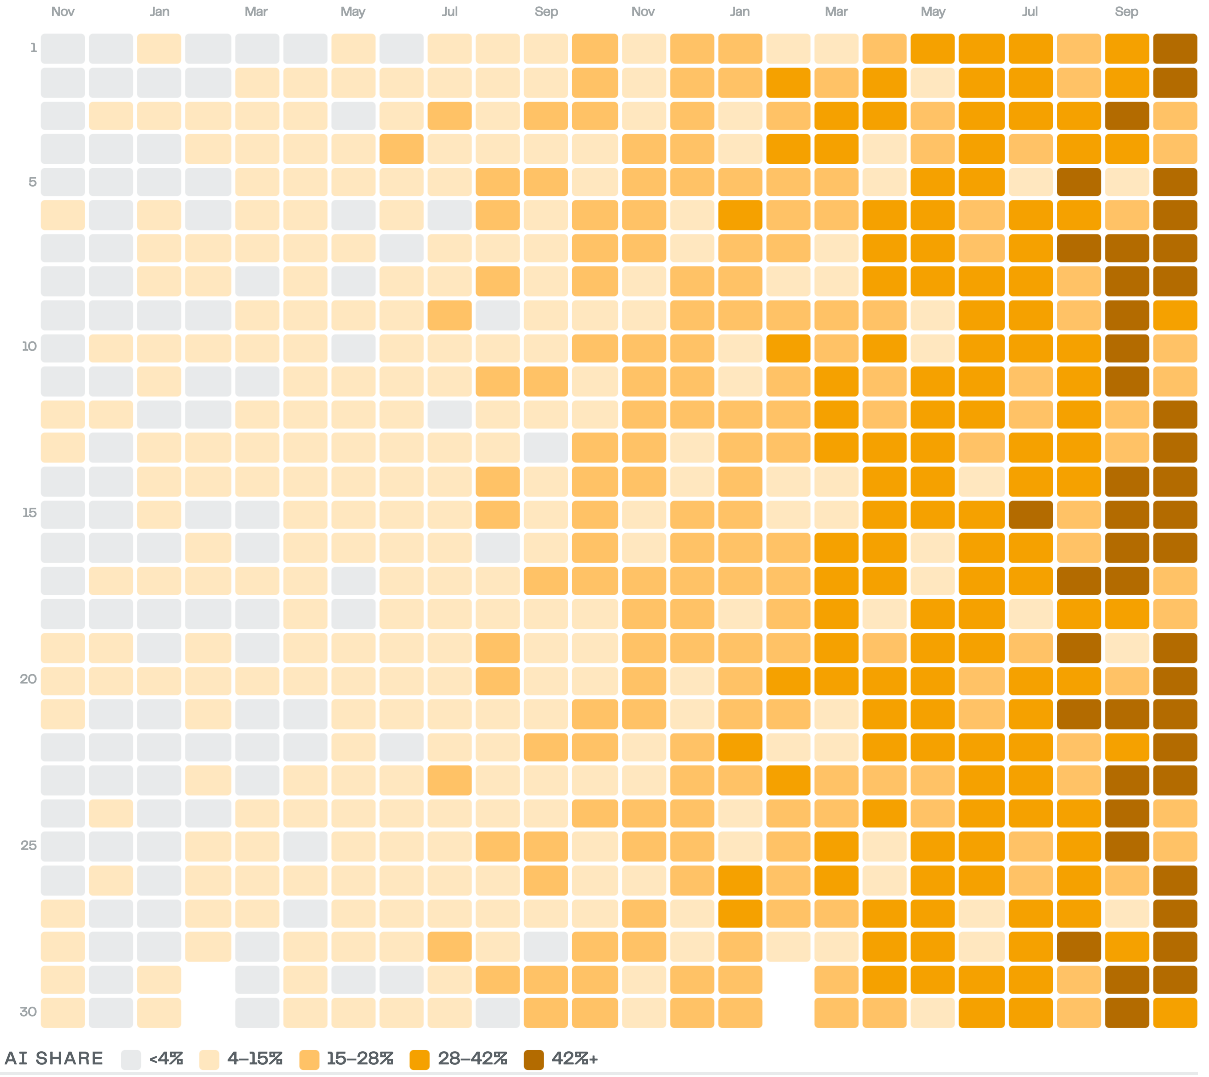


SECTION 1 OF 6

Cyber & Infra

9 initiatives reported

6 scoping
2 building
1 released

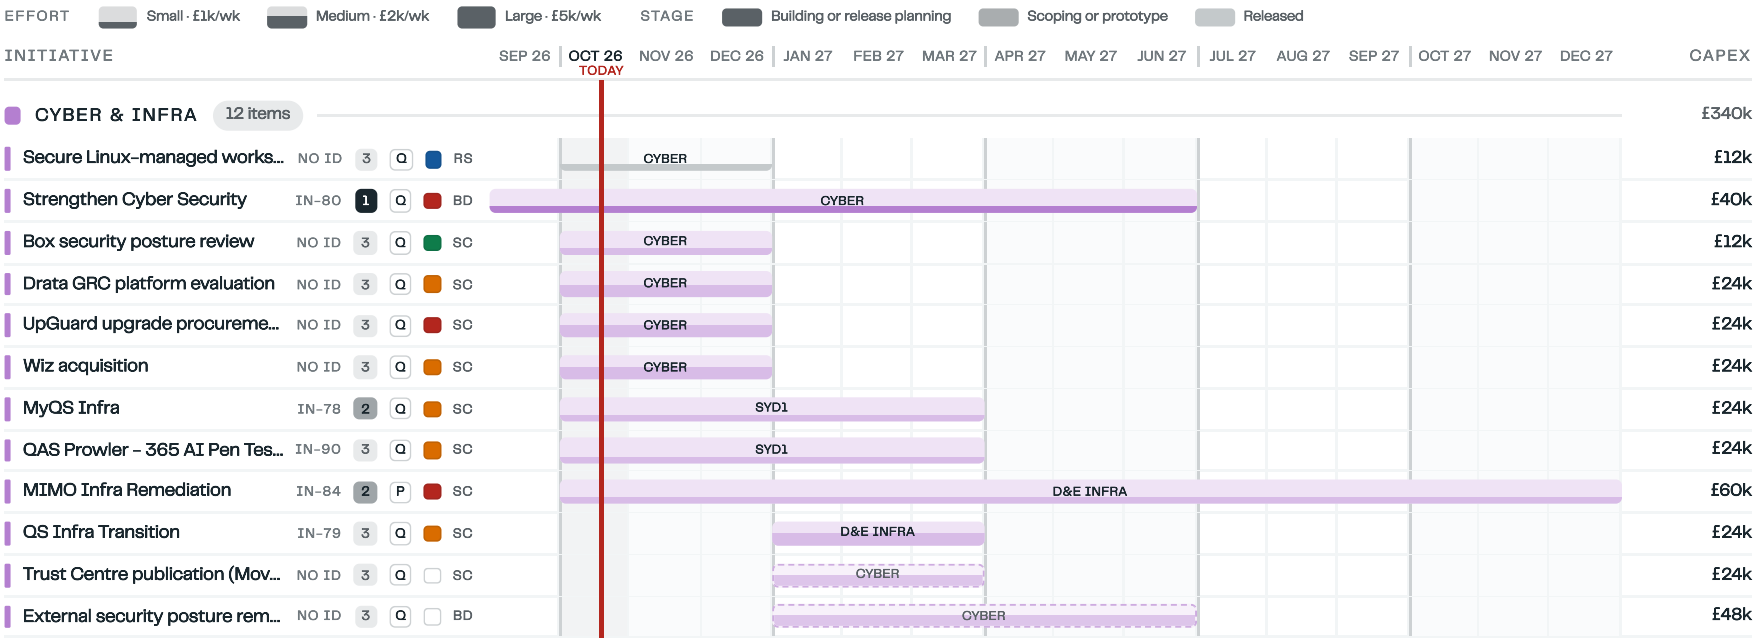

TOTAL CAPEX — 12 of 12 initiatives scheduled · 6 small, 6 medium at £1k / £2k / £5k a week · £268k approved by the investment committee, £72k not yet — £340k

Strengthen Cyber Security

IN-80 · CYBER · BUILDING

UpGuard and Wiz procurement, Drata evaluation, Box posture review, external posture remediation (A-tier regained), MoveON HECVAT for the Trust Centre. Procurement continued progressing both the UpGuard upgrade and Wiz acquisition activities. These investments remain key enablers for maturing QS's third-party risk management and cloud security capabilities. It is dragging on a bit here with only incremental updates; Rowan has requested that Senthil push this along. Discussions regarding Drata were delayed due to stakeholder availability constraints. The project remains active and will resume once key participants are available.

MIMO Infra Remediation

IN-84 · INFRASTRUCTURE · MIMO (MOVEON AND MOVEIN) · SCOPING

MoveON and MoveIN DR environments ahead of the BCP/DR exercises; Telemaxx MySQL 8.4 cluster migration; Jasper container in staging; container image retention. Progressed DR environment recreation through Terraform and reusable Ansible automation for infrastructure, databases and application services. Initial testing identified improvements ahead of the scheduled exercise. Completed the Telemaxx MySQL cluster migration, including additional-node provisioning and storage configuration. Deployed the Jasper container in staging, enabled monitoring and automatic restart, and stopped the legacy VM. Wider integration and application validation continue. Reviewed credential protection and retention of approved container images to support consistent deployment and recovery.

Box security posture review

NO INITIATIVE NUMBER · CYBER · SCOPING

Additional discovery sessions were held with the Marketing and Creative teams to understand business processes, content-sharing requirements and the impact of potential security changes, with recommendations to be refined for the CISO.

Drata GRC platform evaluation

NO INITIATIVE NUMBER · CYBER · SCOPING

Discussions regarding Drata were delayed due to stakeholder availability constraints, but the project remains active and will resume once key participants are available.

External security posture remediation

NO INITIATIVE NUMBER · CYBER · BUILDING

Work with multiple teams on externally visible security issues and vulnerabilities contributed to QS regaining its A-tier rating with external cybersecurity risk-scoring providers.

Secure Linux-managed workstation model

NO INITIATIVE NUMBER · CYBER · RELEASED

Rebuilding Rowan's laptop with Ubuntu 26 LTS, Secure Boot, TPM-backed encryption and Entra ID authentication (AuthD + MS Broker) proved a secure Linux-managed workstation model that may be valuable for Corporate IT, and the approach will be documented and shared.

Trust Centre publication (MoveON HECVAT)

NO INITIATIVE NUMBER · CYBER · SCOPING

Outstanding items in the MoveON HECVAT questionnaire continued to be reviewed and documented as part of preparing to publish the Trust Centre internally.

UpGuard upgrade procurement

NO INITIATIVE NUMBER · CYBER · SCOPING

Procurement of the UpGuard upgrade continued with only incremental updates, and there is budget for the purchase that may be reallocated if delays extend.

Wiz acquisition

NO INITIATIVE NUMBER · CYBER · SCOPING

Procurement activity for acquiring Wiz continued alongside UpGuard as a key enabler for QS's cloud security capability.

Cyber

OTHER WORK · NOT LINKED TO AN INITIATIVE

CyberCon 2026 preparation: Finalised attendance planning for CyberCon Melbourne, including building a targeted conference agenda and scheduling networking discussions with industry contacts and security vendors to maximise time at the event. Cyber Awareness content creation: Developed content for publication on the Inside QS and SharePoint platforms to support Cyber Awareness Month activities and promote stronger security awareness across the business.

Cyber

RISKS AND DECISIONS

Risks and decisions. UpGuard procurement timeline risk. There is budget for this purchase and extended delays may see QS miss the opportunity to capitalise before the budget is reallocated.

MIMO (MoveON and MoveIN)

RISKS AND DECISIONS

Risks and decisions. MySQL 8.4 issues. MySQL 8.4–related issues in France and Telemaxx, including issues observed following hotfixes, remain under investigation. Telemaxx queue failures also present a service-stability risk. Repository credential clean-up. Repository credential clean-up remains outstanding, with sensitive material still requiring removal from repository history.


2027 Data and Engineering Delivery Plan

SECTION 2 OF 6

Data

9 initiatives reported

2 scoping
7 building

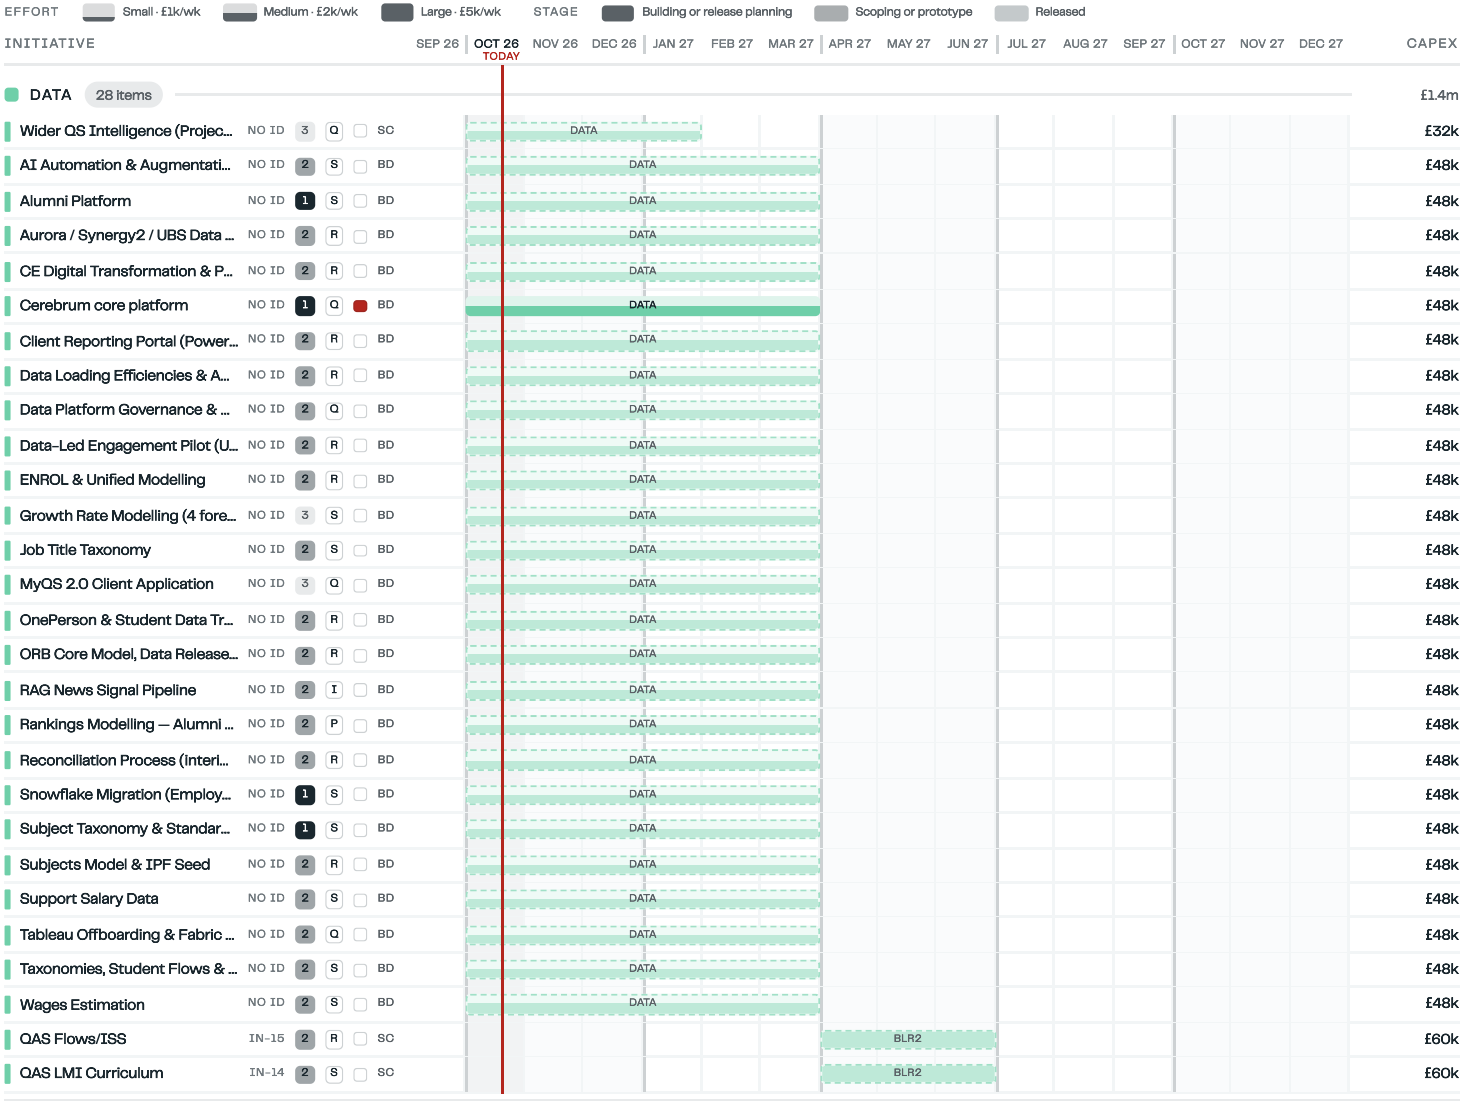

Snowflake Migration (Employability)

NO INITIATIVE NUMBER · EMPLOYABILITY & SKILLS · BUILDING

Subject Taxonomy & Standardization

NO INITIATIVE NUMBER · EMPLOYABILITY & SKILLS · BUILDING

Data Platform Governance & Migration

NO INITIATIVE NUMBER · DATA & ANALYTICS · BUILDING

Data-Led Engagement Pilot (University of London)

NO INITIATIVE NUMBER · DATA & ANALYTICS · BUILDING

ENROL & Unified Modelling

NO INITIATIVE NUMBER · DATA & ANALYTICS · BUILDING

Job Title Taxonomy

NO INITIATIVE NUMBER · EMPLOYABILITY & SKILLS · BUILDING

Employability & Skills Progress: Decided to retain the existing product occupation IDs rather than adopt new QSIDs directly; will instead map these IDs to QSIDs for Cerebrum. Current mining run is about a week from completion.

QAS Flows/ISS

IN-15 · DATA TEAM (GSF) · GLOBAL STUDENT FLOWS (GSF) · SCOPING

Prism subjects model rebuilt; ORB ratio gap-filling, revised global totals, Baltic forecasts and Tier 4 QA checks. GSF team This week: Subject titles crosswalked to QS taxonomy; model architecture rebuilt; IPF rebalancing analysis complete; StudyPortals fees data collected (~200k programmes). Country-level accuracy (TVD) improved from 17.5 to around 6–7 once the layers were rebuilt with the new data, a ~60% improvement; changing the IPF seed as well moved university-level TVD from 27.3 to 10.0 for universities with data, at the cost of a worse estimate for universities without observed data. GSF team This week: Gap-filling revised to the ratio method; global totals revised (2025 global total = 7.67M). GSF team This week: New forecasts for Lithuania, Latvia and Estonia.

QAS LMI Curriculum

IN-14 · DATA TEAM (LMI) · LABOUR MARKET INTELLIGENCE (LMI) · SCOPING

AI Exposure Framework Layer 2 localisation; penetration-scoring indicators finalised; country clustering narrowed to 60 indicators; regional guardrails and country mapping. LMI team This week: Refined the Layer 2 country localisation methodology for the QS AI Exposure Framework, including the indicator lists and pillars to better capture country readiness, occupational deployment dependencies, and country–occupation interactions. LMI team This week: Finalised the indicator lists across all 15 penetration buckets and drafted imputation methods for selected buckets. Completed Gibrat's Law testing across population, employment, and occupation levels, which showed no evidence of systematic size-related bias in assigned CAGRs.

Rankings Modelling — Alumni Impact & Career Alignment

NO INITIATIVE NUMBER · EMPLOYABILITY & SKILLS · BUILDING

Data & Analytics

OTHER WORK · NOT LINKED TO AN INITIATIVE

ENROL and propensity modelling: D&A Modelling team Progress: The course-of-interest modelling framework was merged into the main ENROL codebase, trained against production data and deployed across active clients. This establishes the technical route for course-level modelling despite the underlying source-data constraints. Data-led Engagements: D&A team Progress: The University of London pilot was reframed to avoid unreliable model-based prioritisation. The replacement experiment will compare morning and afternoon calling using the LLB offer cohort. The campaign segment has been prepared, and Data Science will create two randomised groups for execution.

Employability & Skills

OTHER WORK · NOT LINKED TO AN INITIATIVE

Rankings Modelling – Alumni Impact: Employability & Skills Progress: Finalised restructuring/sourcing of all lists under Sam's new spec. Reviewed every list for whether it can be sourced from the profile dataset. Began exploration of economic knowledge and technology impact indicators this sprint. Rankings Modelling – Career Alignment + Graduate Employment Rate: Employability & Skills Progress: Finalised subject standardisation across the profile dataset, unlocking career alignment, employment alignment, degree-to-occupation rate, and subject-occupation relationships. Advanced highly-skilled employment rate modelling. Snowflake Migration: Employability & Skills Progress: Finalised migration of profile data into Snowflake.


2027 Data and Engineering Delivery Plan

SECTION 3 OF 6

Core

4 initiatives reported

2 prototype
2 building

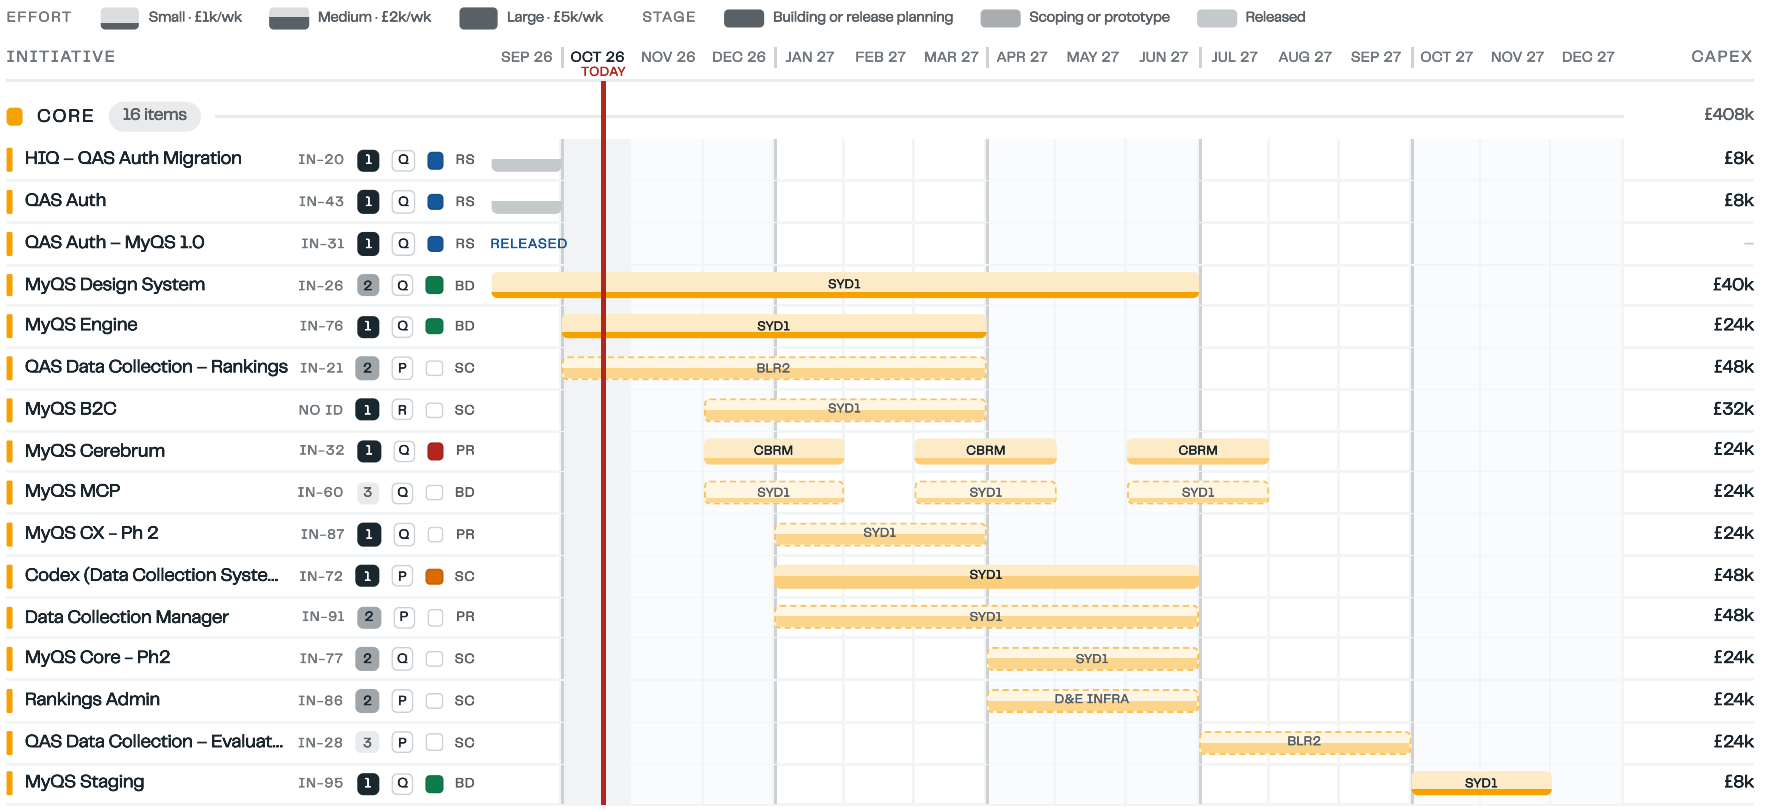

MyQS Cerebrum

IN-32 · SYD1 · DATA & ANALYTICS · PROTOTYPE

institution registry in the QS Supergraph on staging and production. Data Team: Courses live; Awards, Skills, Student Flows and Alumni released as governed datasets; Rankings flowing by region; OnePerson roadmap completed. The institution registry is now part of the QS data graph on both staging and production, so every app can ask one place for institutions, rankings and reputation together; the embargo list is readable by QS administrators only. D&A Platform team Progress: Courses shipped, completing delivery from the original four producers. Programmes, courses, intakes and fees are now published, with multilingual text preservation, duplicate programme handling, stable matching and human review for genuinely ambiguous records.

MyQS CX – Ph 2

IN-87 · SYD1 · PROTOTYPE

access-event search by actor, Ranking Master in the account type picker, switches read at sign-in. CX admins can search access events by who did them, choose Ranking Master in the account type picker (locked where it cannot be set), and the app reads its feature switches at sign-in.

MyQS Staging

IN-95 · SYD1 · BUILDING

first two production release flags live; shared release checks across all front ends; release and rollback procedure written down. The first two production switches are live (CX embargo dates and bulk import), a revert was rehearsed in staging first, and CX now learns its switches at sign-in so a flip needs no release. Every QS front end now runs the same release checks and records each production release; every connection to QS services requires modern encryption; the production release and rollback procedure is written down.

MyQS Design System

IN-26 · SYD1 · BUILDING

Rankings Template new design live; rankings board loading states, paging and sorting; resizable heatmap columns. The Rankings Template's new design is live — focus view, highlights overview, index by indicator, indicator view and the institution panel; the rankings board shows loading states card by card and its tables page and sort from source; the heatmap's columns can be resized; MyQS opens on the account band in production.

SYD1

OTHER WORK · NOT LINKED TO AN INITIATIVE

HolonIQ / HolonOS: Customer accounts see Regions benchmark columns in production; slow queries are capped in production; the statistics service no longer crashes on empty metric lists and recovers from cache errors. QS Auth: Staging sign-up is open again, but only to people already invited to an account — the blanket staff-email rule is withdrawn.

Data & Analytics

RISKS AND DECISIONS

Risks and decisions. Confirm the remediation owner and expected route for the University of London course and intake defect before London inference is reconsidered. Confirm the scope decision for the first Alumni Impact iteration if the current analytical approach cannot be delivered reliably.


Sector Intelligence 4 initiatives

SECTION 4 OF 6

Sector Intelligence

4 initiatives reported

1 scoping
2 prototype
1 building

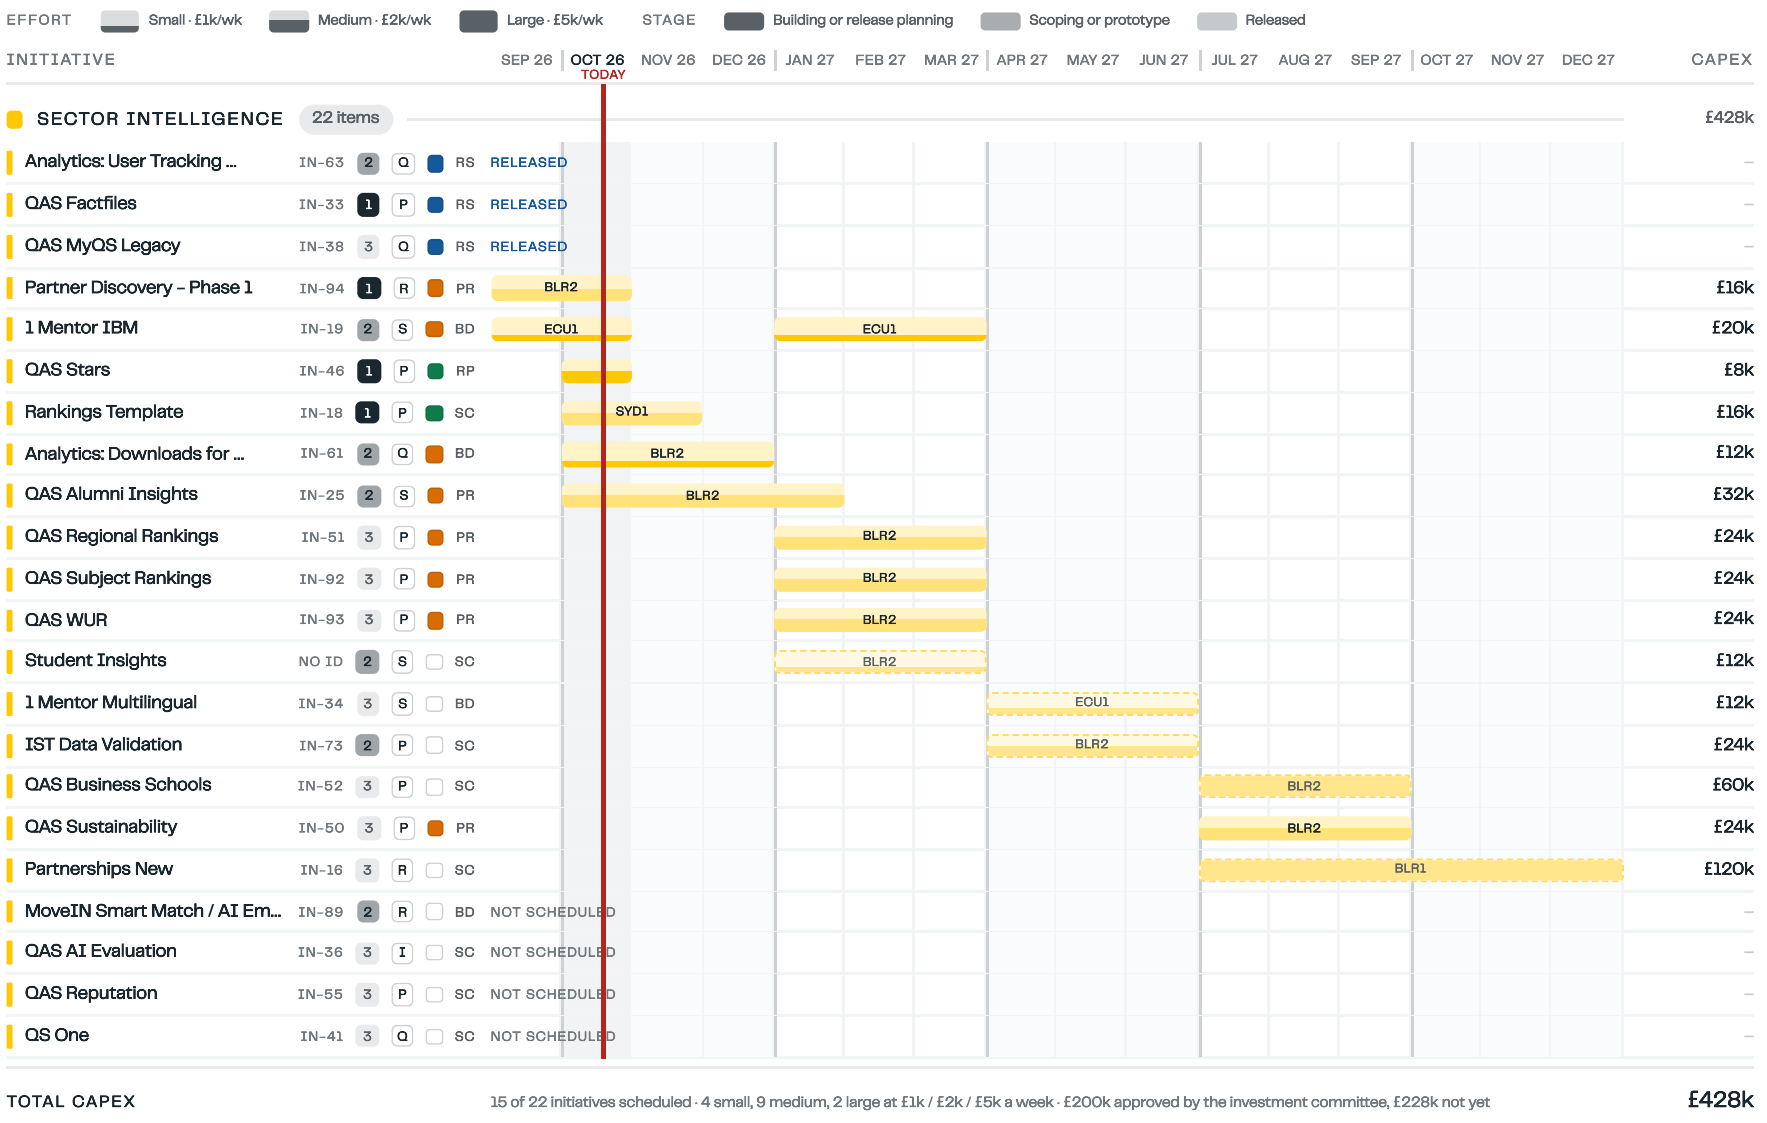

TOTAL CAPEX — 15 of 22 initiatives scheduled · 4 small, 9 medium, 2 large at £1k / £2k / £5k a week · £200k approved by the investment committee, £228k not yet — £428k

Partner Discovery – Phase 1

IN-94 · BLR2 · PROTOTYPE

one opportunity visibility rule across roles, consistent ownership filters, single interest view; QA completed. Unified opportunity visibility across roles: all users including admins see every published opportunity at their institution, while drafts/unpublished stay visible only to creators or linked users. “Mine”, “Linked” and “All” ownership filters now apply consistently across roles. Added “all” toggle on institution profile for contributors. Consolidated incoming/outgoing interest views into a single section. Refined plan usage view and institution banner. Tidied up navigation so menu items appear for the right users.

Rankings Template

IN-18 · SYD1 · SCOPING

rankings carry a category that drives visibility; zero-downtime data publishing. Publishing new data to production now interrupts users for seconds rather than ten minutes; rankings carry a category that drives who may see them; Alumni Insight’s institution ids are aligned with the registry; the old loading path is retired so there is one way in.

MoveIN Smart Match / AI Email

IN-89 · MOVEIN · BUILDING

AI Usage Dashboard; AI beta labels, template walkthrough, branding controls and latest brand settings through UAT. dashboard delivered, showing per-client usage, result quality and cost in $/£, with export for client and executive reporting. “Beta” labels on the AI features set clearer expectations and should reduce support questions. a guided walkthrough for first-time users should speed adoption and on-brand results. users can adjust email colours, spacing and image cropping themselves, so branding matches faster without technical help. AI emails now pick up each client’s latest logo, images and brand colours, removing manual rework.

QAS Alumni Insights

IN-25 · SYD1 · EMPLOYABILITY & SKILLS · PROTOTYPE

Alumni Insight institution ids aligned with the registry. Publishing new data to production now interrupts users for seconds rather than ten minutes; rankings carry a category that drives who may see them; Alumni Insight’s institution ids are aligned with the registry; the old loading path is retired so there is one way in. Employability & Skills Progress: No major updates this period.

BLR2

OTHER WORK · NOT LINKED TO AN INITIATIVE

MyQS / Rankings: Fixed an issue where an indicator with no available score was incorrectly highlighted as an institution's "best indicator"; only genuinely ranked/scored indicators now surface. Applied the same correction across both the Rankings overview and the Partner Discovery partner-ranking view. Updated Asia region ranking insight figures (recorded citations, nominations, and related metrics) to reflect correct values.

BLR1

OTHER WORK · NOT LINKED TO AN INITIATIVE

HUB2 Investigations: Initiated analysis of ongoing data and audit-related investigations, reviewing historical records, profile data, and available system information to establish scope and identify potential resolution paths. HUB2 Programme Audit: Began review of programme update activity and audit requirements to validate available change history and support investigation findings. QAS Learning Initiative: Started building a demo rankings application within the QAS shell to develop end-to-end understanding of the platform, data flow, and application architecture.

ECU1 and ECU2

OTHER WORK · NOT LINKED TO AN INITIATIVE

Mixpanel event tracking. Bug fixes: The "all" selector dropdown not working correctly. PLAR deliverables completed: Configurable login page text and contact info.

MoveIN

OTHER WORK · NOT LINKED TO AN INITIATIVE

Business Continuity Mock Drill: business continuity test run and mock drill completed, confirming QS can recover services if disruption occurs. Automated BCP Deployment: automated deployment prepared for business continuity, so services can be deployed quickly if ever needed. SharePoint Merged Documents: merged documents open immediately in SharePoint, saving staff a refresh step. Single-Portal Navigation: clients with a single portal now get the same full navigation as multi-portal clients. Import Program Field: admins can again set a fixed "Program" value in data imports, avoiding manual corrections.

MoveON

OTHER WORK · NOT LINKED TO AN INITIATIVE

Advanced Publisher–MoveON API security: Development is finished and in code review, then it goes to QA with MoveON. Publisher performance for two clients: Pages take about 62–66s to load on Live, compared with about 4–9s on staging with the same data. That points to the Live environment, but the root cause isn't confirmed yet. Reporting charts improvements: Started. It's in analysis. Multi-server database setup: In analysis. It depends on infrastructure work. Advanced seat assignment (MVP): It was added partway through the sprint. One part is in development and the other is still in analysis, and no code has been committed yet. API security hardening: Development and code review are done, and it's waiting for QA to start.

MIMO (MoveON and MoveIN)

OTHER WORK · NOT LINKED TO AN INITIATIVE

Completed REST API and Advanced Publisher SSL renewals across all live environments and improved automated deployment prerequisites. Executed database compliance-check commands and prepared outputs for the external penetration-testing team. Assessment findings and remediation will be handled separately.

BLR1

RISKS AND DECISIONS

Risks and decisions. Limited historical records. Limited availability of historical change logs or legacy records may constrain the depth of analysis for ongoing investigations.

ECU1 and ECU2

RISKS AND DECISIONS

Risks and decisions. Hackathon timing managed. Last week, the hackathon was considered a risk due to the tight timeline. However, the team was able to manage it successfully thanks to the implementation of AI-driven methodologies, which helped complete all PLAR tasks intended for production.

MoveON

RISKS AND DECISIONS

Risks and decisions. End-to-end testing dependency. The security changes can't be tested end to end until the MoveON-side changes are done. Top risk to escalate: publisher performance. Both clients have chased, and one says it's very urgent. Both have agreed to let QS use their real data for the investigation. Mitigation: addition of custom logs to trace the issue, as the Infra team confirmed that there are no slow query logs. Blockers: both open items are waiting on code review before QA can start.


2027 Data and Engineering Delivery Plan

SECTION 5 OF 6

D&E

2 initiatives reported

1 prototype
1 released

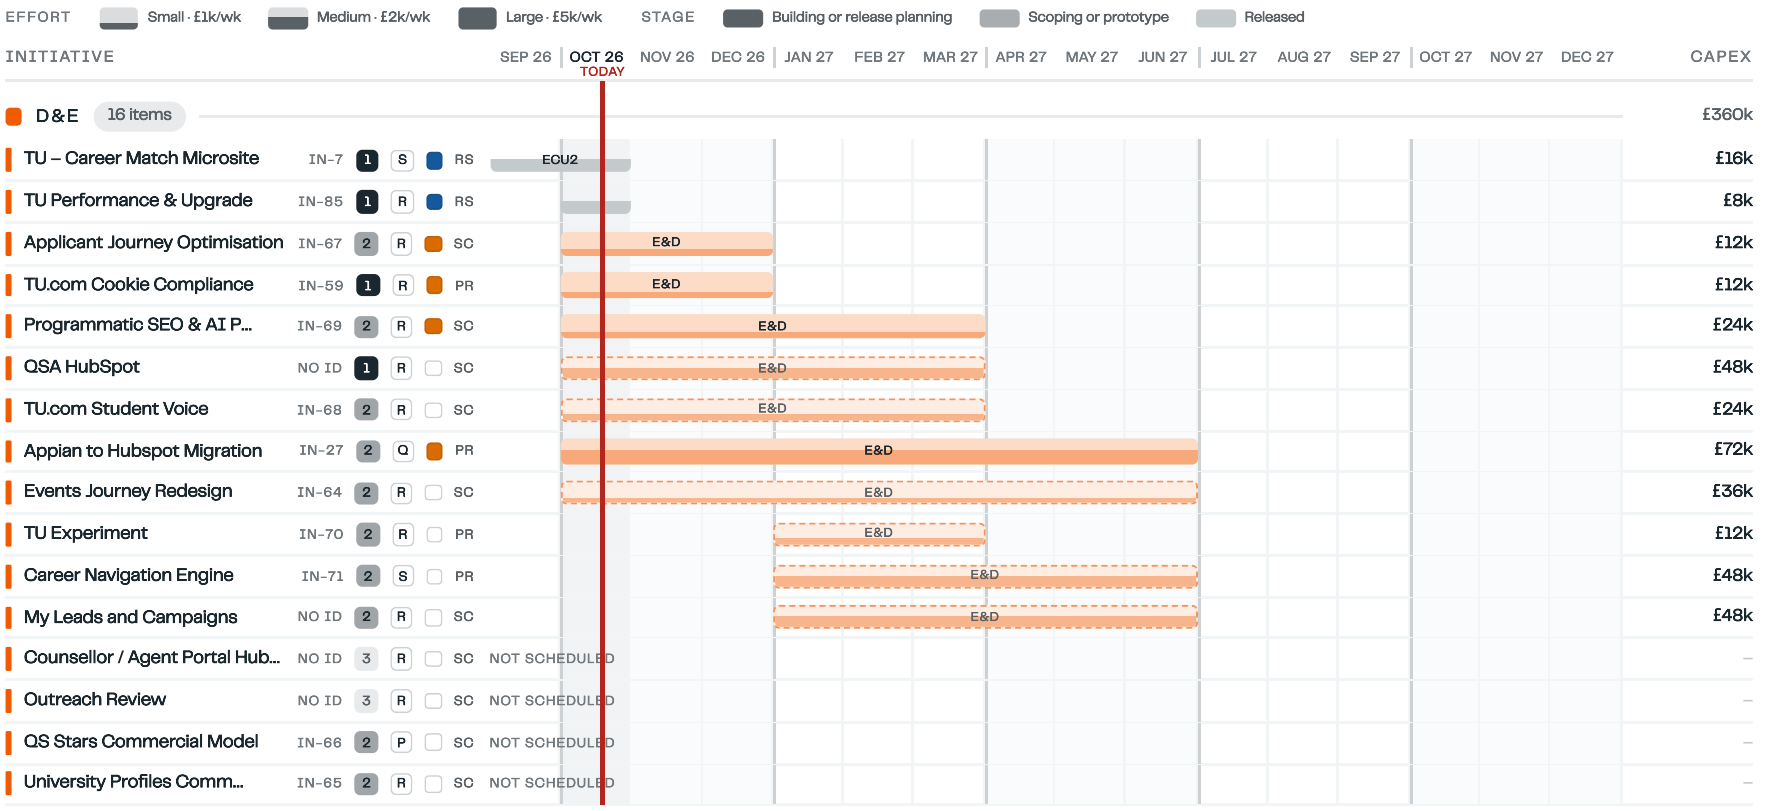

TOTAL CAPEX — 12 of 16 initiatives scheduled · 6 small, 6 medium at £1k / £2k / £5k a week · £144k approved by the investment committee, £216k not yet — £360k

TU Performance & Upgrade

IN-85 · DIGITAL AND EVENTS · D&E · RELEASED

TU homepage performance and Drupal clean-up released; Drupal 11 production upgrade postponed. Infrastructure: PHP 8.4 and Drupal 11.4.8 in TU and TM prelive. A decision has been made to postpone the upgrade; there were minor UI issues that were reported and needed fixing. When the team reached the cut-off date, it felt this would be risky. Completed TU/TM prelive upgrades, validated the custom tracing module and finished dev6aws containerisation. This has been released.

Appian to Hubspot Migration

IN-27 · QS APPLY · QS APPLY (APPIAN) · PROTOTYPE

current-state Appian process flow diagrams and consolidated pain points. created flow diagrams to document the existing Appian processes and functionality, supporting the migration analysis. consolidated the pain points captured during stakeholder workshops into a single document to facilitate review, prioritisation, and future-state planning.

Digital and Events

OTHER WORK · NOT LINKED TO AN INITIATIVE

Convert CMT module from React to Drupal: This has been released. Agenda builder: This has been released. Finance page: Backend work is underway as planned. Emails redesign: Tickets in sprint are progressing as planned. Marcomms Dashboard: The main dashboard is completed; other sections will be picked up in the upcoming sprint.

QS Apply (Appian)

OTHER WORK · NOT LINKED TO AN INITIATIVE

Deactivated EM/PAM Visibility: updated the Application and Applicant Dashboards to display deactivated EM/PAM users. The changes have been deployed to the TEST environment. Applicant Created Date Filter: fixed the Applicant Created Date filter issue. The fix has been deployed to the TEST environment. HubSpot API Failure: investigated an API failure caused by an invalid HubSpot Agent ID.

D&E

OTHER WORK · NOT LINKED TO AN INITIATIVE

Completed Tableau platform preparation and reviewed licence usage and renewal requirements. HUB1: rolled back last week's production OS upgrade to the previous servers after issues emerged. Investigation is ongoing before reattempting the upgrade. Reviewed September AWS costs, removed obsolete stopped VMs and analysed Cloudflare bot traffic to inform security tuning. Rovo–Microsoft Teams integration: validated Jira issue creation and commenting using supplied transcript content. Automatic transcript retrieval remains unresolved and has been escalated to CORP-IT.

2027 Data and Engineering Delivery Plan

Digital and Events

RISKS AND DECISIONS

Risks and decisions. Drupal sprint release. Because of the new rankings release in the upcoming week and the hackathon, it was decided to postpone this to 19 October. Redesign of QS Apply page. Waiting for clear requirements and form changes — still pending.

D&E

RISKS AND DECISIONS


Risks and decisions. HUB1 on legacy servers. HUB1 is back on legacy Ubuntu 18 production servers following the rollback. The underlying issue must be resolved before the upgraded servers can return to service.

SECTION 6 OF 6

University Services

3 initiatives reported

1 prototype
2 building

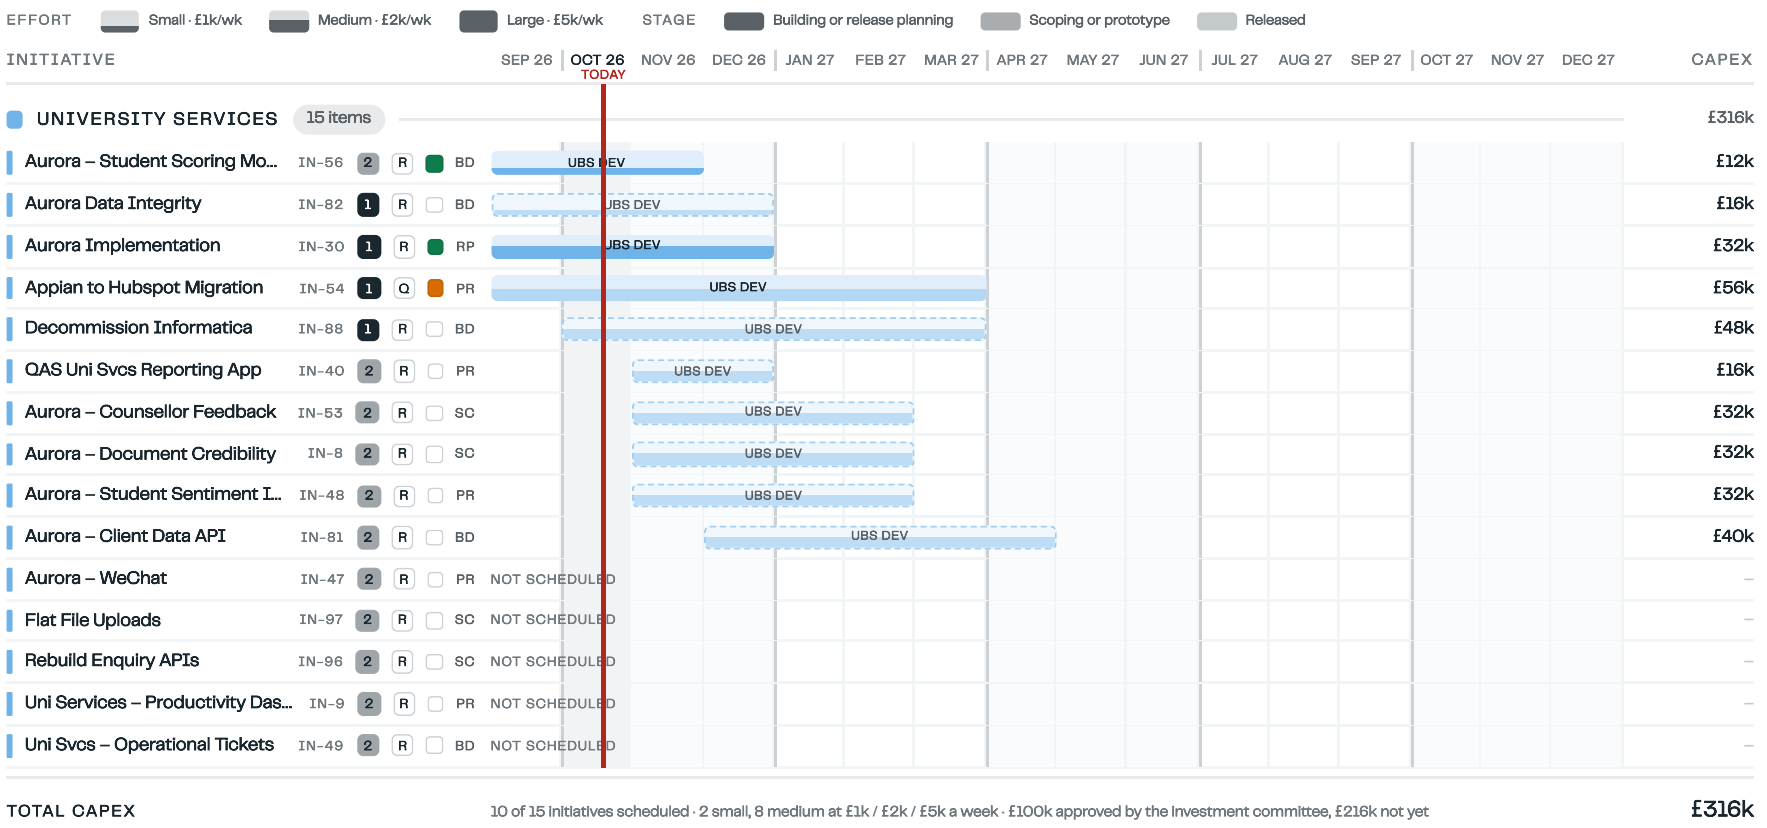

Appian to Hubspot Migration

IN-54 · UBS DEVELOPMENT · QS APPLY (APPIAN) · PROTOTYPE

enquiry-form replacements (Keele, RCA, Griffith International, ACU) and ESI replacement (Stirling). QS Apply: migration discovery documentation. created flow diagrams to document the existing Appian processes and functionality, supporting the migration analysis. consolidated the pain points captured during stakeholder workshops into a single document to facilitate review, prioritisation, and future-state planning. Stirling development work has been completed and tested. It is now undergoing changes for auto ticket creation and the new tag contact structure. Identified and fixed the error when promoting Contact Matching from production to sandbox.

Aurora Data Integrity

IN-82 · DATA TEAM · DATA & ANALYTICS · BUILDING

313,000 unparseable intake rows identified across six institutions; audit rules extended; Synergy2 fixes and journey history released. D&A team Progress: The team identified 313,000 COI rows across six institutions whose intake text cannot currently be parsed to dates. Audit rules were extended for cleaned-up records, portal-property inconsistencies and potential test contacts. Marketing email events, deferred and Student Declined journey history, and further Synergy2 fixes were released. The cross-functional task-force model is reported to be improving coordination.

Decommission Informatica

IN-88 · UBS DEVELOPMENT · BUILDING

S3 flat file (Griffith International, Edith Cowan University, Brighton), Keystone (RCA signed off, Edith Cowan University) and York integration. Continued working on the Informatica York Integration to pull data from Dynamics, following new data mappings agreed in discussion with Mohit and Sean. Griffith International's replacement is awaiting deployment, pending the API replacement. RCA has been signed off. Deployment is pending completion of the API replacement.

CX Systems

OTHER WORK · NOT LINKED TO AN INITIATIVE

Number porting: progressed porting of UK, US, AU and NZ numbers from Twilio to Aircall. Sakari: followed up on outstanding issues and requirements. Niswey: discussed the call-based workflow issue and QS Events subscription. WhatsApp: fixed the WhatsApp template issue. Meta: liaised with Meta Support regarding the Australian number issue for WhatsApp onboarding. China IVRs: coordinated with managers on China IVR requirements. SIP: set up a test number and conducted SIP tests, with further follow-ups on China and India SIP implementation. QS Events: resolved the Sakari Helpdesk authentication issue. Aircall: onboarded new users. Callbacks: continued working on Sakari and Vira automations for callbacks. Chatbots: completed chatbot handovers.

UBS

OTHER WORK · NOT LINKED TO AN INITIATIVE

Progressed FSx capacity reductions and Dialogflow backups ahead of retirement. Provisioned S3 user access and created a new Snowflake database for the Data Science team. Purchased a new domain for Digital Outreach.

UBS Development

RISKS AND DECISIONS

Risks and decisions. UoL licensing. One institution's test environment (UoL) is missing required licensing to proceed with development. Simon Pennington is arranging access. HubSpot x HubSpot data model. Clare is awaiting the Data Model from Daniel before development on the HubSpot x HubSpot integration can begin. LSBU on hold. Informatica (S3 Flat File) replacement: LSBU development is on hold while awaiting the tender outcome. Stirling UTM fields.

CX Systems

RISKS AND DECISIONS

Risks and decisions. AI Chatbots. Implementation is delayed, impacting progress on planned chatbot activities.

Data & Analytics

RISKS AND DECISIONS

Risks and decisions. Confirm the remediation owner and expected route for the University of London course and intake defect before London inference is reconsidered. Confirm the scope decision for the first Alumni Impact iteration if the current analytical approach cannot be delivered reliably.
