WEEK 42 · 12–16 OCTOBER 2026

2027 Data and Engineering Delivery Plan

# Week 42 Delivery Report

What moved this week, initiative by initiative, with the delivery schedule it sits in.

Cyber & Infra · Data · Core · Sector Intelligence · D&E · University Services

## THE WEEK AT A GLANCE

### Cyber & Infra 2 INITIATIVES

**Outcomes.** 2 initiatives moved, led by Strengthen Cyber Security, MIMO Infra Remediation. CyberCon 2026 Melbourne: attended CyberCon over three days, gaining exposure to emerging thinking, practices and technologies across cybersecurity, privacy, incident response and resilience.

**Risks & decisions.** AI-related data handling. The two data security events this week highlight the continuing risk of sensitive and personal data being uploaded to generative AI services.

### Data 3 INITIATIVES

**Outcomes.** 3 initiatives moved, led by QAS Flows/ISS, QAS LMI Curriculum, Wider QS Intelligence (Project Compass). This week's primary focus was on updating Bledi Taska on the workings of LMI and starting to synthesise and consolidate the assets, workstreams, projects etc.

**Risks & decisions.** Nothing raised this week.

### Core 3 INITIATIVES

**Outcomes.** 3 initiatives moved, led by MyQS Cerebrum, MyQS CX – Ph 2, MyQS Design System. The new entity store is in production.

**Risks & decisions.** Nothing raised this week.

### Sector Intelligence 1 INITIATIVE

**Outcomes.** 1 initiatives moved, led by MoveIN Smart Match / AI Email. MoveIN now offers a smoother user experience with easier AI email creation, simpler branding options, improved navigation, and quicker document access.

**Risks & decisions.** Progress remains on track across current sprint commitments. No risks or decisions are currently pending. The security changes are being tested end to end and QA is in progress. Top risk to escalate: publisher performance.

### D&E 2 INITIATIVES

**Outcomes.** 2 initiatives moved, led by TU Performance & Upgrade, Appian to Hubspot Migration. International Trade (ITR) and Arab rankings have been released and all are working as expected. The team continues to address Appian production support issues while progressing with the Appian Migration initiative.

**Risks & decisions.** Drupal sprint release. Because of the new rankings release this week and the hackathon, it was decided to postpone this to 19 October. D&E: Live TU and TM PHP and Drupal upgrades remain on hold pending developer confirmation and approval.

### University Services 3 INITIATIVES

**Outcomes.** 3 initiatives moved, led by Appian to Hubspot Migration, Aurora Data Integrity, Decommission Informatica. The Appian dev team has continued work on developing integration replacements for enquiry forms within HubSpot.


**Risks & decisions.** One institution's test environment (UoL) is missing required licensing to proceed with development. Simon Pennington is arranging access.


# Contents

Delivery schedule 3
Engineering activity 4
Cyber & Infra 5
Data 7
Core 10
Sector Intelligence 12
D&E 16
University Services 19

# 2027 Data and Engineering Delivery Plan


## Delivery schedule 109 initiatives

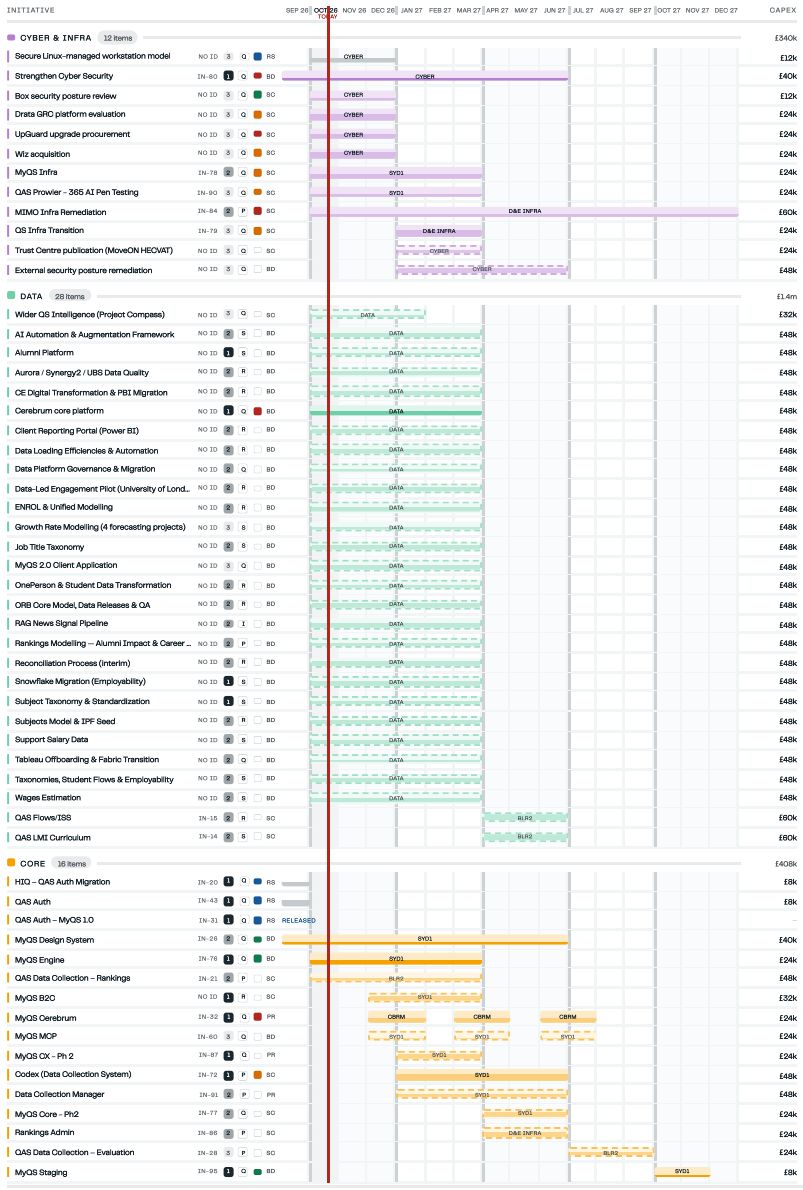

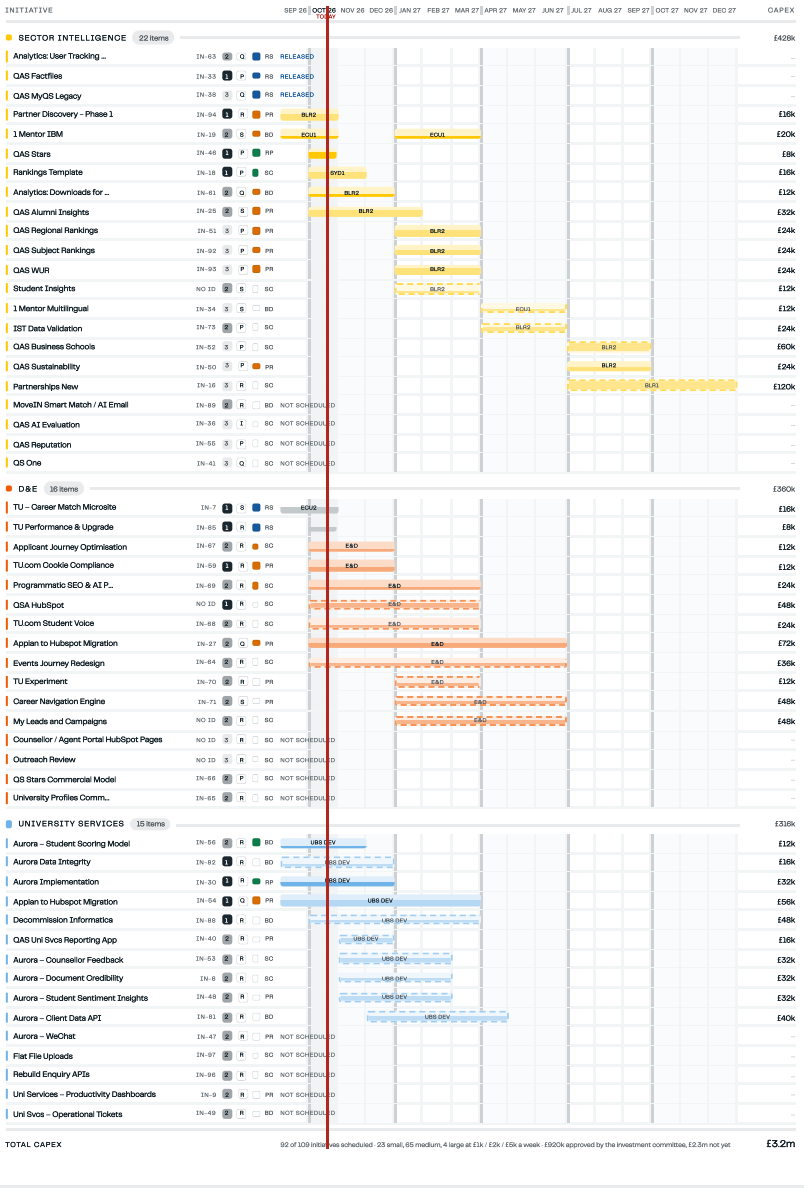
## Productivity Heatmap NOV 24 – OCT 26

Lines of code committed a day.

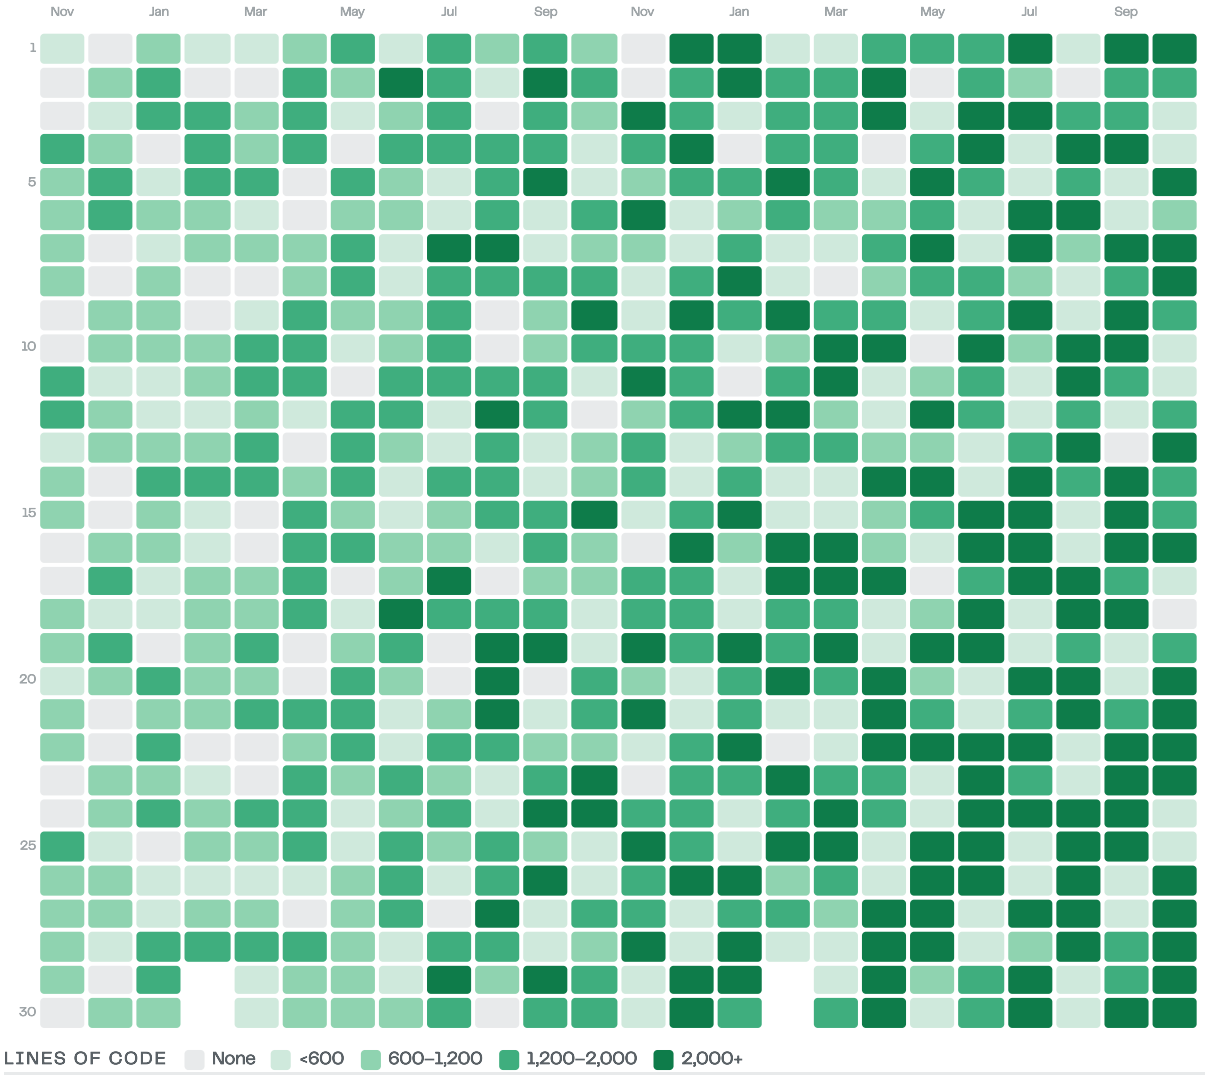


## AI Code Intensity NOV 24 – OCT 26

Share of committed code written by AI.

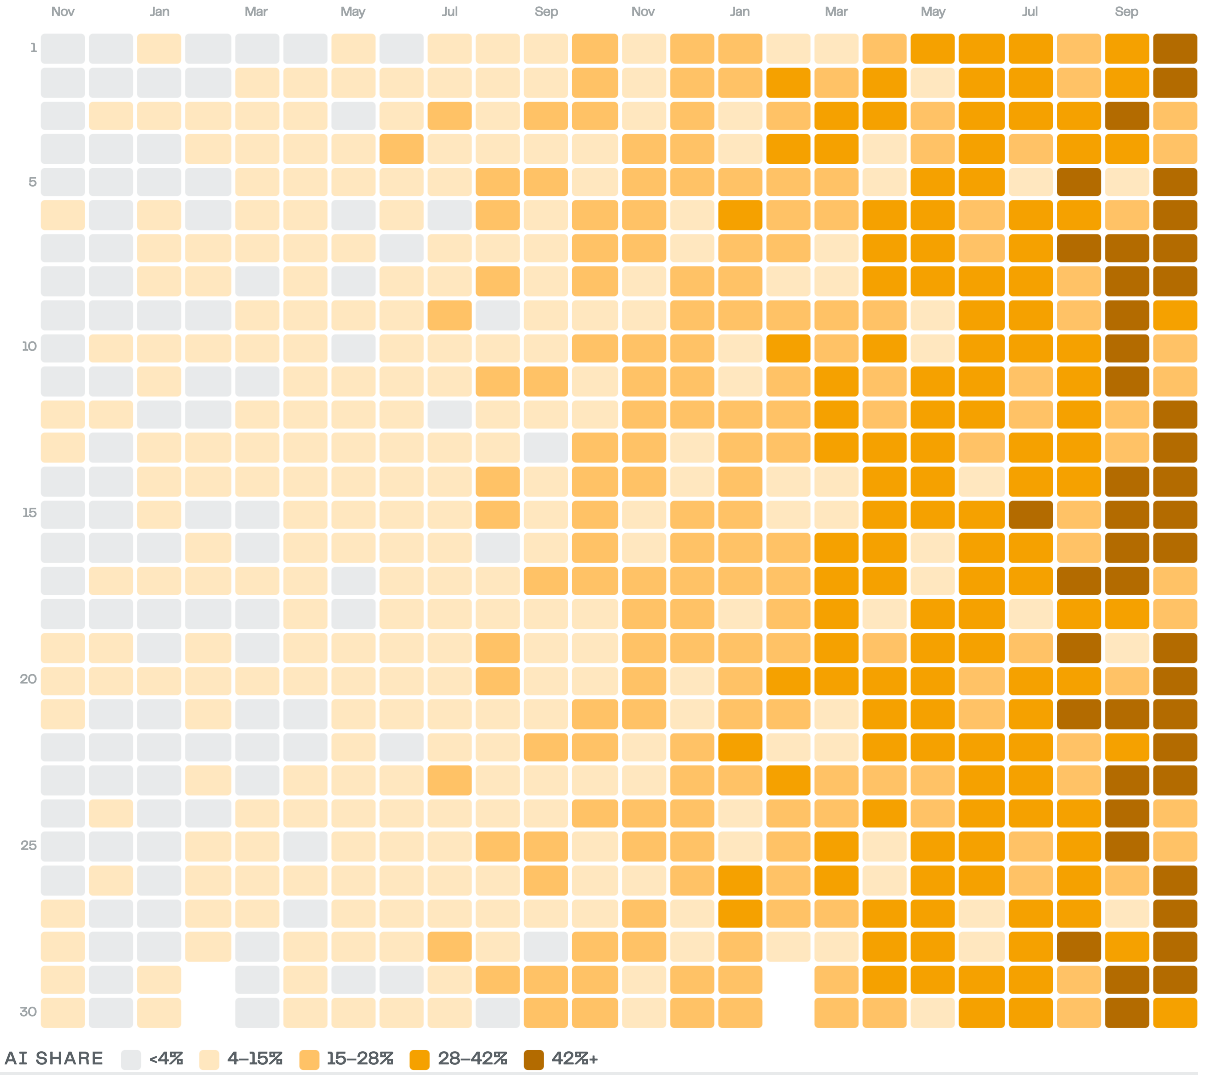


SECTION 1 OF 6

# Cyber & Infra

2 initiatives reported

1 scoping
1 building

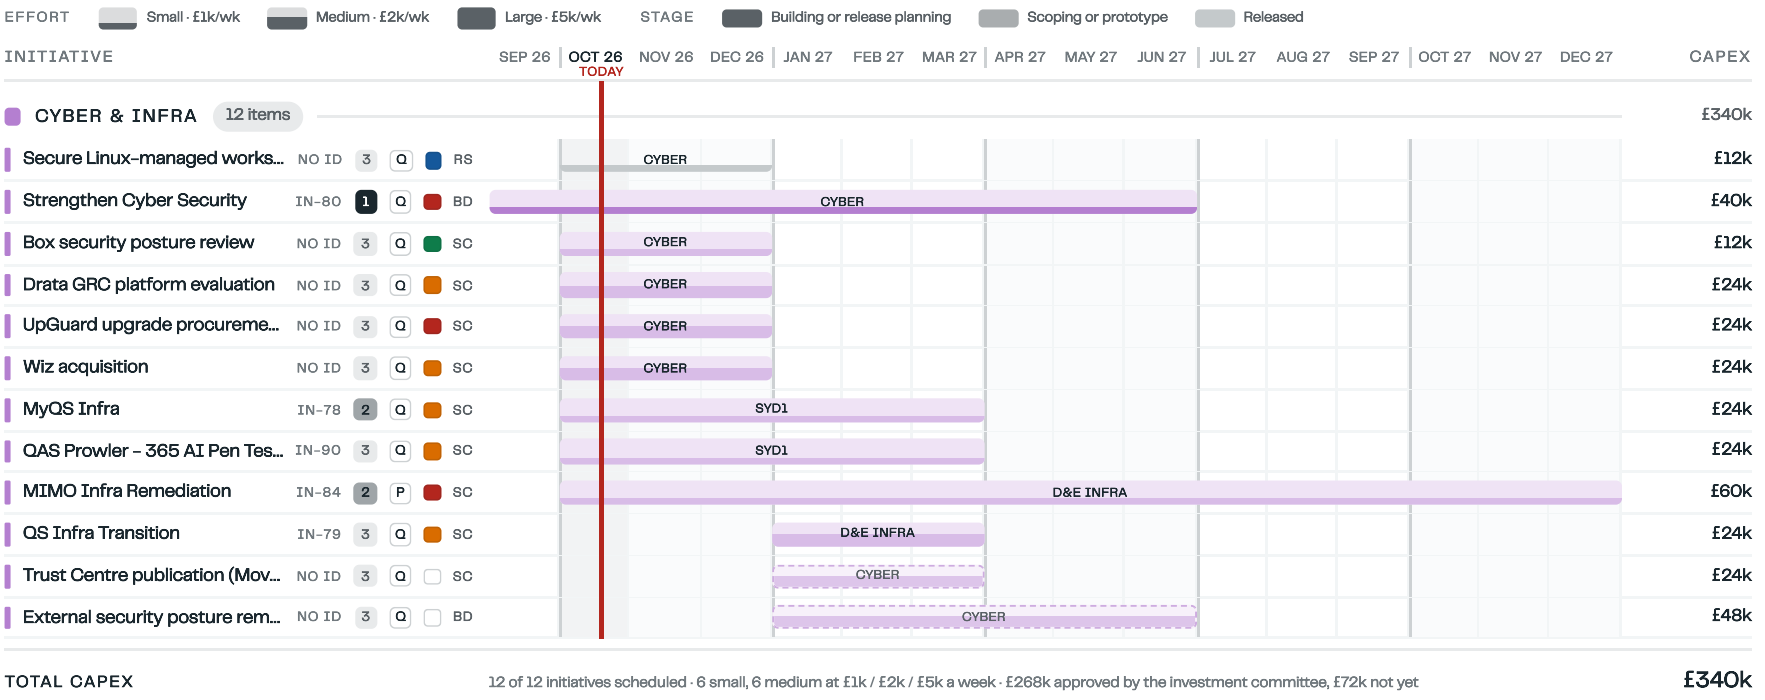


TOTAL CAPEX — 12 of 12 initiatives scheduled · 6 small, 6 medium at £1k / £2k / £5k a week · £268k approved by the investment committee, £72k not yet — £340k

## Strengthen Cyber Security

IN-80 · CYBER · BUILDING

Advanced Publisher internal security assessment completed; MoveIN and 1Mentor internal assessments initiated; MoveIN external penetration test concluded with remediation items; 1Mentor penetration test report under review. Completed the internal security assessment for MoveON – Advanced Publisher and shared the final report with relevant stakeholders. Initiated internal security assessments for MoveIN and 1Mentor. Kick-off meetings are being arranged to formally commence the assessment activities. External penetration testing has concluded, the final report has been distributed, and Jira remediation items have been created to drive identified findings through to resolution. Received the web application penetration testing report and commenced Cybersecurity review of the findings.

## MIMO Infra Remediation

IN-84 · INFRASTRUCTURE · MIMO (MOVEON AND MOVEIN) · SCOPING

MoveON recovery readiness ahead of the DR exercise; MoveIN BCP exercise completed; replacement Telemaxx MySQL server provisioned; Docker-based JasperReports builds; MoveIN Demo Elasticsearch upgrade. Improved provisioning and restoration automation during recovery preparation, including EFS configuration, server hardening, database-backup fixes and rsync restoration. Resolved login issues and identified further deployment inconsistencies. Standardised Docker-based JasperReports builds, validated report rendering and documented release retention and rollback procedures. Provisioned the replacement Telemaxx MySQL server as part of the EOL migration initiative. Completed the BCP exercise; recovery documentation is being finalised.

## Cyber

OTHER WORK · NOT LINKED TO AN INITIATIVE

AI data security events: Triaged two data security events detected through CrowdStrike involving PII being uploaded to generative AI services. The affected users were engaged as part of the response, with the events providing further practical insight into how AI-related data risks are emerging within QS. Cyber Awareness Month (CAM26): Published Cyber Awareness Month content to Inside QS/SharePoint, providing employees with practical cybersecurity awareness information and supporting October's wider awareness activities.

## Cyber

RISKS AND DECISIONS

Risks and decisions. AI-related data handling. The two data security events this week highlight the continuing risk of sensitive and personal data being uploaded to generative AI services. These events reinforce the need for a combination of technical controls, visibility and employee awareness as AI adoption grows.

# 2027 Data and Engineering Delivery Plan




SECTION 2 OF 6

# Data

3 initiatives reported

3 scoping

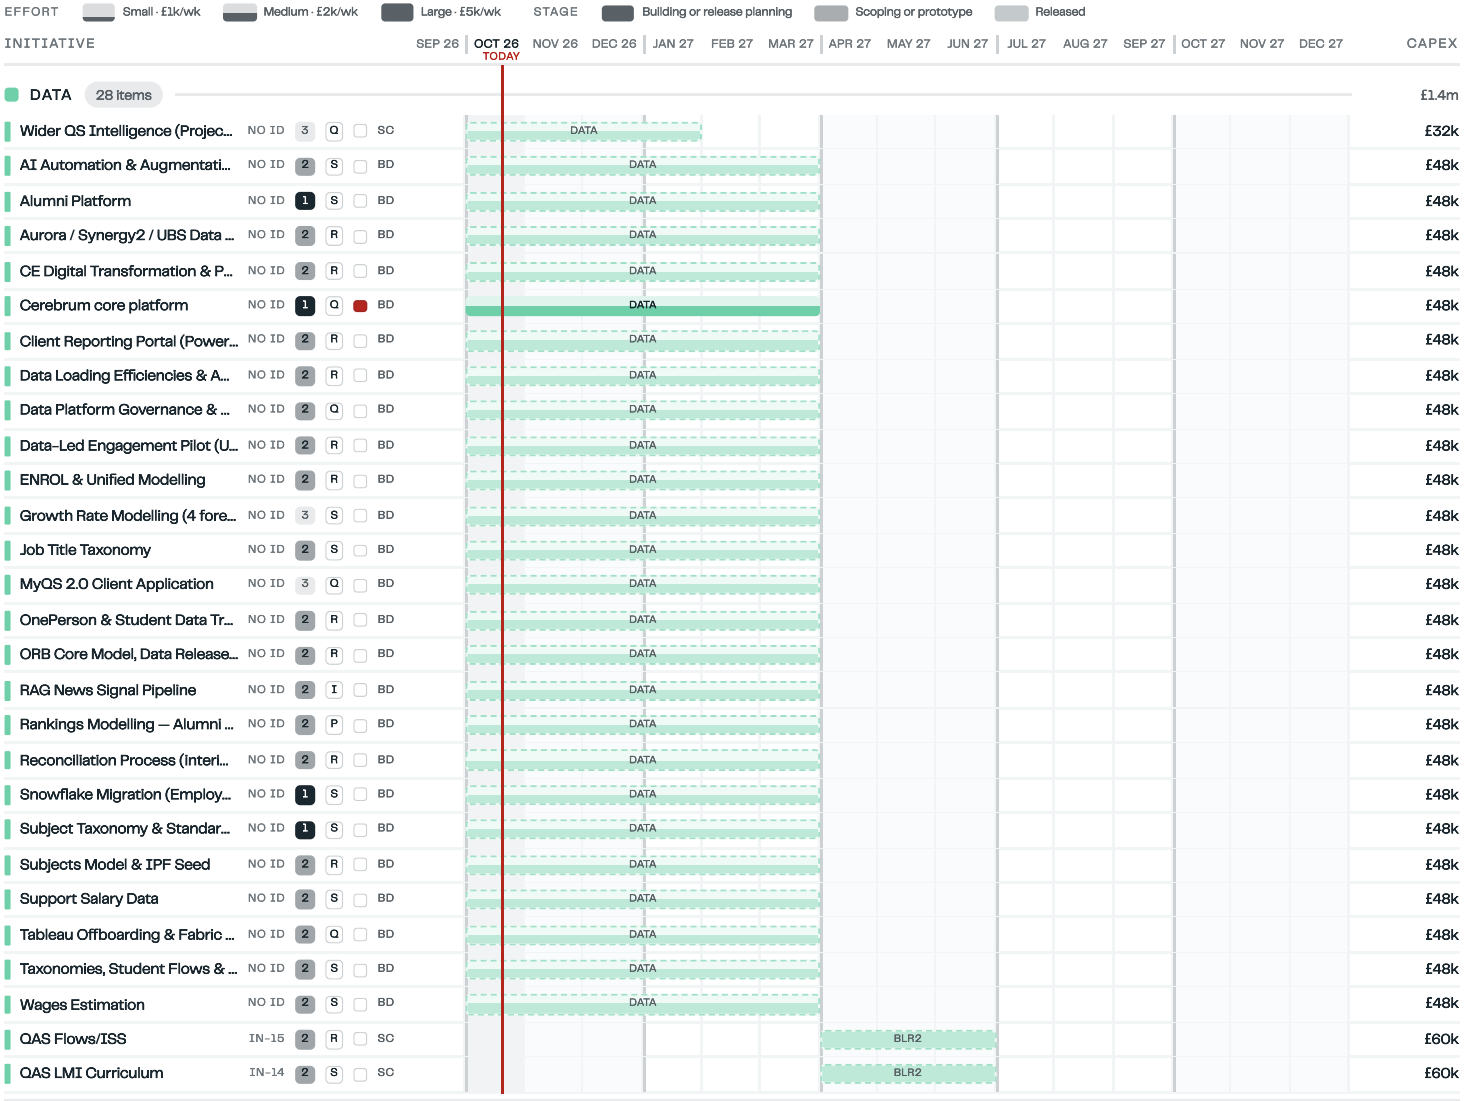

## QAS Flows/ISS

IN-15 · DATA TEAM (GSF) · GLOBAL STUDENT FLOWS (GSF) · SCOPING

Prism second-layer error down about 10% with leakage and year-mixing removed; universities model production forecasts reproduced and retrain checked; government university data for 40 countries; Orb Malaysia and regional rulebook reworks. About 10% lower error in the second layer: the country-level international student numbers by source country and subject layer now captures how an origin's subject preferences differ by destination, with a separate adjustment for each origin–destination pair. Regional data was leaking into the second layer and inflating its measured accuracy; it has been removed, so results reflect real performance. Each country pair now takes all its subject shares from a single year.

## QAS LMI Curriculum

IN-14 · DATA TEAM (LMI) · LABOUR MARKET INTELLIGENCE (LMI) · SCOPING

AI Exposure Framework Layer 1 and 2 pilot; regional guardrails with 2025 employment estimates for 150 countries; OPAL automation; India data sourcing; ILO-based regional scalar bounds validated across 83 countries. Did a pilot implementation for a few occupations and countries for the Layer 1 and the Layer 2 country localisation methodology for the QS AI Exposure Framework. Evaluated forecasting methods for regional employment guardrails, selecting carry-forward after back testing five alternatives. Tested historical data recency, added reliability flags, and preserved observed 2025 occupation data. Generated 2025 employment estimates for all 150 countries. Implementing an automated process of updating countries with deep-dive country outputs. Working on India LMI Data — Data Sourcing, Crosswalks.

## Wider QS Intelligence (Project Compass)

NO INITIATIVE NUMBER · BUSINESS INTELLIGENCE (BI) · SCOPING

No material change this week. The project remains paused while capacity is directed to client access, end-of-cycle analysis and data corrections. Groundwork and source-owner walkthroughs remain complete, but there is still no restart date. Watch: The project will continue to drift unless a restart point is agreed after the current delivery peak.

## Data & Analytics

OTHER WORK · NOT LINKED TO AN INITIATIVE

Rankings & Data Operations: International Trade results were published with no issues reported. The second Arab Rankings fact file and results were published with no major issues. Sustainability Rankings were re-issued after a bug was identified, and the fact files are ready for distribution. Europe Rankings analysis and data work continued. Subject Rankings produced a first draft, continued movement to live subject mappings, and created a new navigation report ahead of sign-off. Employability/Skills strengthened the graduate employment rate component and produced a first draft. Country Fact Files reached approximately 80% completion, and the GME-based product prototype continued with historical data tables nearly ready.

## Business Intelligence (BI)

OTHER WORK · NOT LINKED TO AN INITIATIVE

University Services Client Reporting Portal (Power BI): The 15 October go/no-go confirmed that the final MVP reports, agreed filters, design changes and consolidated engagement view were ready. The eight-client pilot cohort and client user base were confirmed for Griffith International, ACU, Stirling, Keele, Durham, RCA, Birmingham and Exeter. Power BI role testing progressed, but the Microsoft security groups had not yet been created at the session. Lucy is liaising with IT on whitelisting and security-group creation, the remaining dependencies before external access can go live. Region and sub-region standards still require a decision, but this is not considered a launch blocker.

# 2027 Data and Engineering Delivery Plan




SECTION 3 OF 6

## Core

3 initiatives reported

2 prototype
1 building

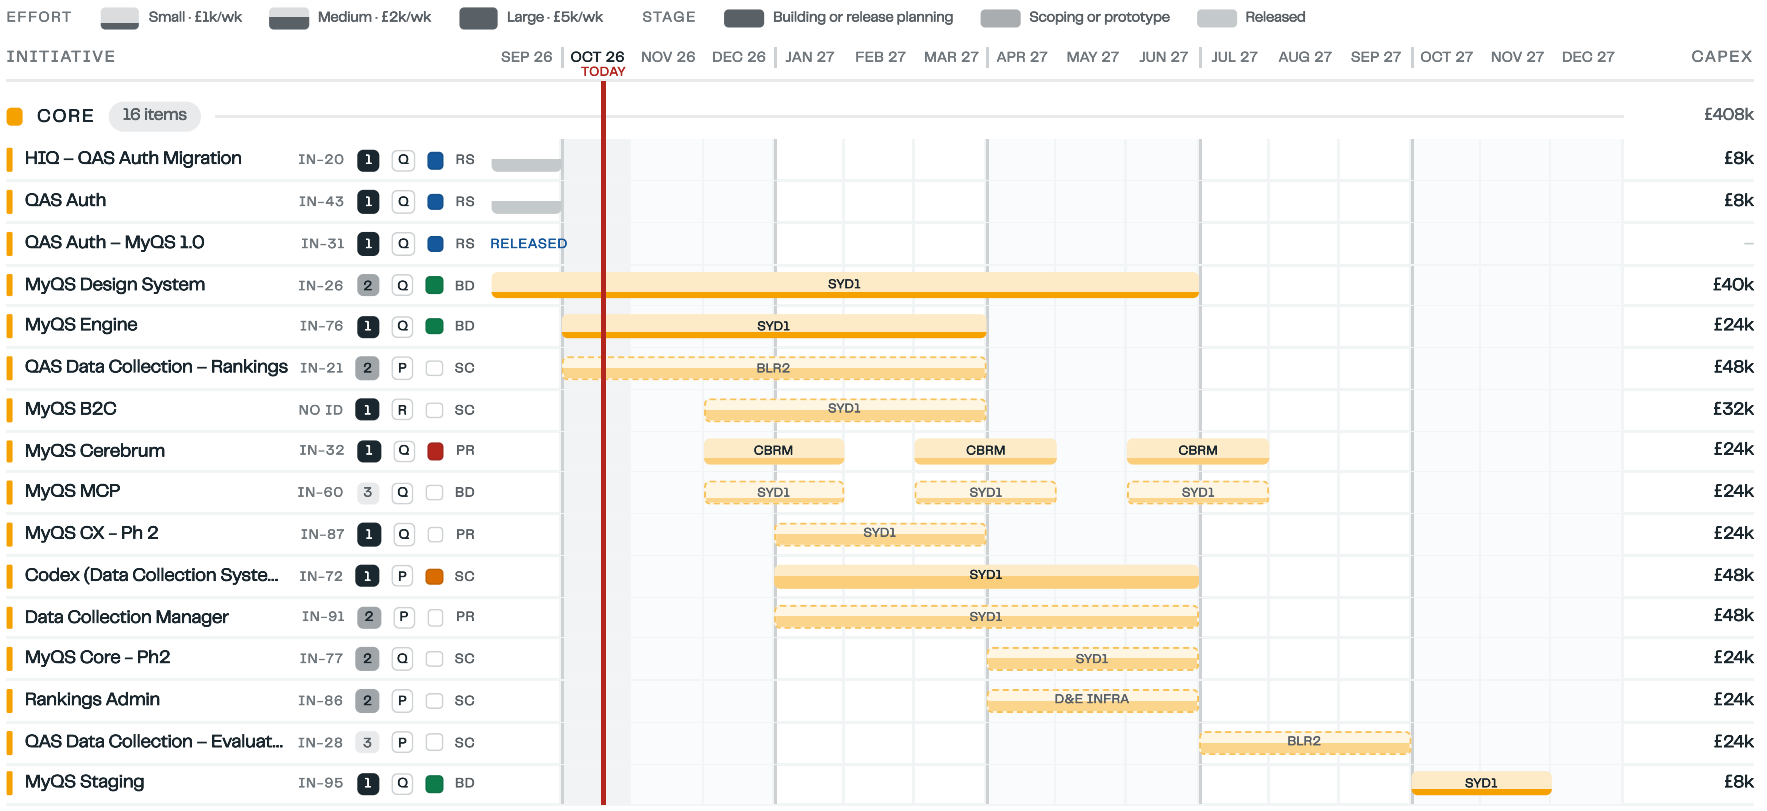


TOTAL CAPEX — 15 of 16 initiatives scheduled · 5 small, 10 medium at £1k / £2k / £5k a week · £160k approved by the investment committee, £248k not yet — £408k

## MyQS Cerebrum

IN-32 · SYD1 · DATA & ANALYTICS · PROTOTYPE

new entity store in production. Data Team: programme mapper completed; data explorer; ranking ingestion; Snowflake and DBT ingestion including Global Student Flows. The new entity store is in production: the cutover was rehearsed, checked for parity against staging, and recorded as the runbook for the next one. The programme mapper was completed. The domain-oriented data explorer progressed with live taxonomy, geography, institution and rankings data, making Cerebrum content easier to discover and explore. Ranking ingestion was advanced so missing releases can be created without duplicating existing releases. Data Core also moved towards Snowflake- and database-backed ingestion through DBT, and a database access route was established for Global Student Flows.

## MyQS CX – Ph 2

IN-87 · SYD1 · PROTOTYPE

sign-in switches, Ranking Master account type and access-event search in production; failed user creation reported to the admin and platform team. Switches at sign-in, the Ranking Master account type and search of access events by who did them are now in production; when a new user cannot be created, the admin sees the reason and the platform team is told.

## MyQS Design System

IN-26 · SYD1 · BUILDING

design releases through the reviewed path, three shipped; Rankings Template loading states, entitlement masking and logic fixes. Design releases now go out through the same reviewed path as every other product — three shipped this week; the product is named MyQS consistently everywhere; app cards read correctly to screen readers; the onboarding journey is now measured as product analytics. Rankings draw their own loading states, ranks are masked where the account is not entitled, pages make fewer reads, and six logic errors were fixed in a readability pass.

## SYD1

OTHER WORK · NOT LINKED TO AN INITIATIVE

Data & Engineering Portfolio: A new app for QS staff is live as a staging alpha: every engineering team, its people and its work in one place, reached from the app launcher like any other product. HolonIQ / HolonOS: Nomination-country figures now read only the overall subject-area slice, so the WUR Highlights cards show the right numbers. QS Nerv prototype: Draws the QS Graph as an explorable map in the browser and answers questions as a cited briefing, every figure traced to its source, with a landing page and phone layouts.

Sector Intelligence 1 initiative

SECTION 4 OF 6

# Sector Intelligence

1 initiative reported

1 building

EFFORT Small · £1k/wk · Medium · £2k/wk · Large · £5k/wk STAGE Building or release planning · Scoping or prototype · Released

| INITIATIVE | | | | | | SEP 26 | OCT 26 TODAY | NOV 26 | DEC 26 | JAN 27 | FEB 27 | MAR 27 | APR 27 | MAY 27 | JUN 27 | JUL 27 | AUG 27 | SEP 27 | OCT 27 | NOV 27 | DEC 27 | CAPEX |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| **SECTOR INTELLIGENCE** | 22 items | | | | | | | | | | | | | | | | | | | | | £428k |
| Analytics: User Tracking … | IN-63 | 2 | Q | RS | RELEASED | | | | | | | | | | | | | | | | | – |
| QAS Factfiles | IN-33 | 1 | P | RS | RELEASED | | | | | | | | | | | | | | | | | – |
| QAS MyQS Legacy | IN-38 | 3 | Q | RS | RELEASED | | | | | | | | | | | | | | | | | – |
| Partner Discovery – Phase 1 | IN-94 | 1 | R | PR | | BLR2 | | | | | | | | | | | | | | | | £16k |
| 1 Mentor IBM | IN-19 | 2 | S | BD | | ECU1 | | | | ECU1 | | | | | | | | | | | | £20k |
| QAS Stars | IN-46 | 1 | P | RP | | | | | | | | | | | | | | | | | | £8k |
| Rankings Template | IN-18 | 1 | P | SC | | | SYD1 | | | | | | | | | | | | | | | £16k |
| Analytics: Downloads for … | IN-61 | 2 | Q | BD | | | BLR2 | | | | | | | | | | | | | | | £12k |
| QAS Alumni Insights | IN-25 | 2 | S | PR | | | BLR2 | | | | | | | | | | | | | | | £32k |
| QAS Regional Rankings | IN-51 | 3 | P | PR | | | | | | BLR2 | | | | | | | | | | | | £24k |
| QAS Subject Rankings | IN-92 | 3 | P | PR | | | | | | BLR2 | | | | | | | | | | | | £24k |
| QAS WUR | IN-93 | 3 | P | PR | | | | | | BLR2 | | | | | | | | | | | | £24k |
| Student Insights | NO ID | 2 | S | SC | | | | | | BLR2 | | | | | | | | | | | | £12k |
| 1 Mentor Multilingual | IN-34 | 3 | S | BD | | | | | | | | | ECU1 | | | | | | | | | £12k |
| IST Data Validation | IN-73 | 2 | P | SC | | | | | | | | | BLR2 | | | | | | | | | £24k |
| QAS Business Schools | IN-52 | 3 | P | SC | | | | | | | | | | | | BLR2 | | | | | | £60k |
| QAS Sustainability | IN-50 | 3 | P | PR | | | | | | | | | | | | BLR2 | | | | | | £24k |
| Partnerships New | IN-16 | 3 | R | SC | | | | | | | | | | | | BLR1 | | | | | | £120k |
| MoveIN Smart Match / AI Em… | IN-89 | 2 | R | BD | NOT SCHEDULED | | | | | | | | | | | | | | | | | – |
| QAS AI Evaluation | IN-36 | 3 | I | SC | NOT SCHEDULED | | | | | | | | | | | | | | | | | – |
| QAS Reputation | IN-55 | 3 | P | SC | NOT SCHEDULED | | | | | | | | | | | | | | | | | – |
| QS One | IN-41 | 3 | Q | SC | NOT SCHEDULED | | | | | | | | | | | | | | | | | – |

TOTAL CAPEX — 15 of 22 initiatives scheduled · 4 small, 9 medium, 2 large at £1k / £2k / £5k a week · £200k approved by the investment committee, £228k not yet — £428k

## MoveIN Smart Match / AI Email

IN-89 · MOVEIN · BUILDING

AI beta labels, email template walkthrough, email branding controls and latest brand settings in AI emails. AI features now carry “Beta” labels, setting clearer expectations and reducing support questions. First-time users get a guided tour, helping them adopt the tool faster and produce on-brand emails. Users can adjust colours, spacing and image cropping themselves, so branding matches faster without technical help. AI emails now use each client's current logo, images and colours, removing manual rework.

## BLR2

OTHER WORK · NOT LINKED TO AN INITIATIVE

QAS stack practice: Developers built demo apps on the QAS stack to build familiarity, including a demo data submission app and a demo rankings app.

## BLR1

OTHER WORK · NOT LINKED TO AN INITIATIVE

HUB2 Investigations: Completed investigation activities, with findings. HUB2 Programme Audit: Completed audit review and validation of programme update history to support investigation outcomes. QAS Learning Initiative: Continued development of the rankings demo application, strengthening understanding of QAS architecture, rankings data flow, and application lifecycle. HUB2 Scheduled Publishing POC: Started discovery and proof-of-concept work for scheduled institution profile publishing, evaluating user experience, scheduling architecture, publishing workflows, and operational considerations to support off-peak publishing.

## ECU1 and ECU2

OTHER WORK · NOT LINKED TO AN INITIATIVE

Demos from each participant in the hackathon. [BUG] University of Toronto | Learner | Career Goal percentage does not refresh after Skill update. Dependency Injection — Student Type. [BUG] Filters are not displayed in Skills — Learner Mobile B2C. [BUG] An access-scope issue on a learner endpoint could return records beyond the user's own institution. Found by the QA team during regression testing and fixed in production. Implement Atomic Design for AtomSlider, AtomSwitch, and AtomRating — pilot-dashboards. Learning Paths — Nothing is displayed in Suggestions or Related Paths [Compensar Propulsor].

## MoveIN

OTHER WORK · NOT LINKED TO AN INITIATIVE

Higher AI allowance: Live MoveIN clients' monthly AI allowance rises from 100K to 500K tokens, so teams can use the AI email builder and Smart Match assistant all month without hitting the limit. SharePoint merged documents: Merged documents now open immediately, saving staff a refresh step. Single-portal navigation: Clients with one portal now get the same full navigation as multi-portal clients. Import "Program" field: Admins can again set a fixed Program value during data imports, avoiding manual corrections for Import config in form setup. Business continuity test: A test run confirmed services can be recovered if disruption occurs.

## MoveON

OTHER WORK · NOT LINKED TO AN INITIATIVE

Advanced Publisher–MoveON API security: Development is finished and code review and QA are in progress. Publisher performance for two clients: Pages take about 62–66s to load on Live, compared with about 4–9s on staging with the same data. That points to the Live environment, but the root cause isn't confirmed yet. Advanced seat assignment (MVP): Development in progress. API security hardening: In QA and planned to be deployed next week. Cloudflare false-positive fix: Development is done and QA is in progress. The developer worked on code review improvements of last week's work. Workflow validations for bulk configurator and usability enhancements on Configurator: Development in progress for the above functionalities.

## MIMO (MoveON and MoveIN)

OTHER WORK · NOT LINKED TO AN INITIATIVE

DS Server 5.0.1: Deployed DS Server 5.0.1 in Docker in AWS Canada and prepared the equivalent configuration for France. SSL auto-renewal: Extended SSL auto-renewal automation to France, with offline verification and rollback tests passing. Database compliance outputs: Supplied database compliance-command outputs to the external penetration-testing team across MongoDB and MySQL RDS environments. Uptime reporting and support: Completed September uptime reporting and France Demo inventory and backup work. Supported Advanced Publisher troubleshooting, client SSO fixes and development-requested data-copy and anonymisation activities.

## BLR1

RISKS AND DECISIONS

Risks and decisions. Progress remains on track across current sprint commitments.

## ECU1 and ECU2

RISKS AND DECISIONS

Risks and decisions. No risks or decisions are currently pending.

## MoveON

RISKS AND DECISIONS

Risks and decisions. The security changes are being tested end to end and QA is in progress. Top risk to escalate: publisher performance. Both clients have chased, and one says it's very urgent. Both have agreed to let QS use their real data for the investigation. Mitigation: addition of custom logs to trace the issue, as the Infra team confirmed that there are no slow query logs.

# 2027 Data and Engineering Delivery Plan




SECTION 5 OF 6

## D&E

2 initiatives reported

1 prototype
1 released

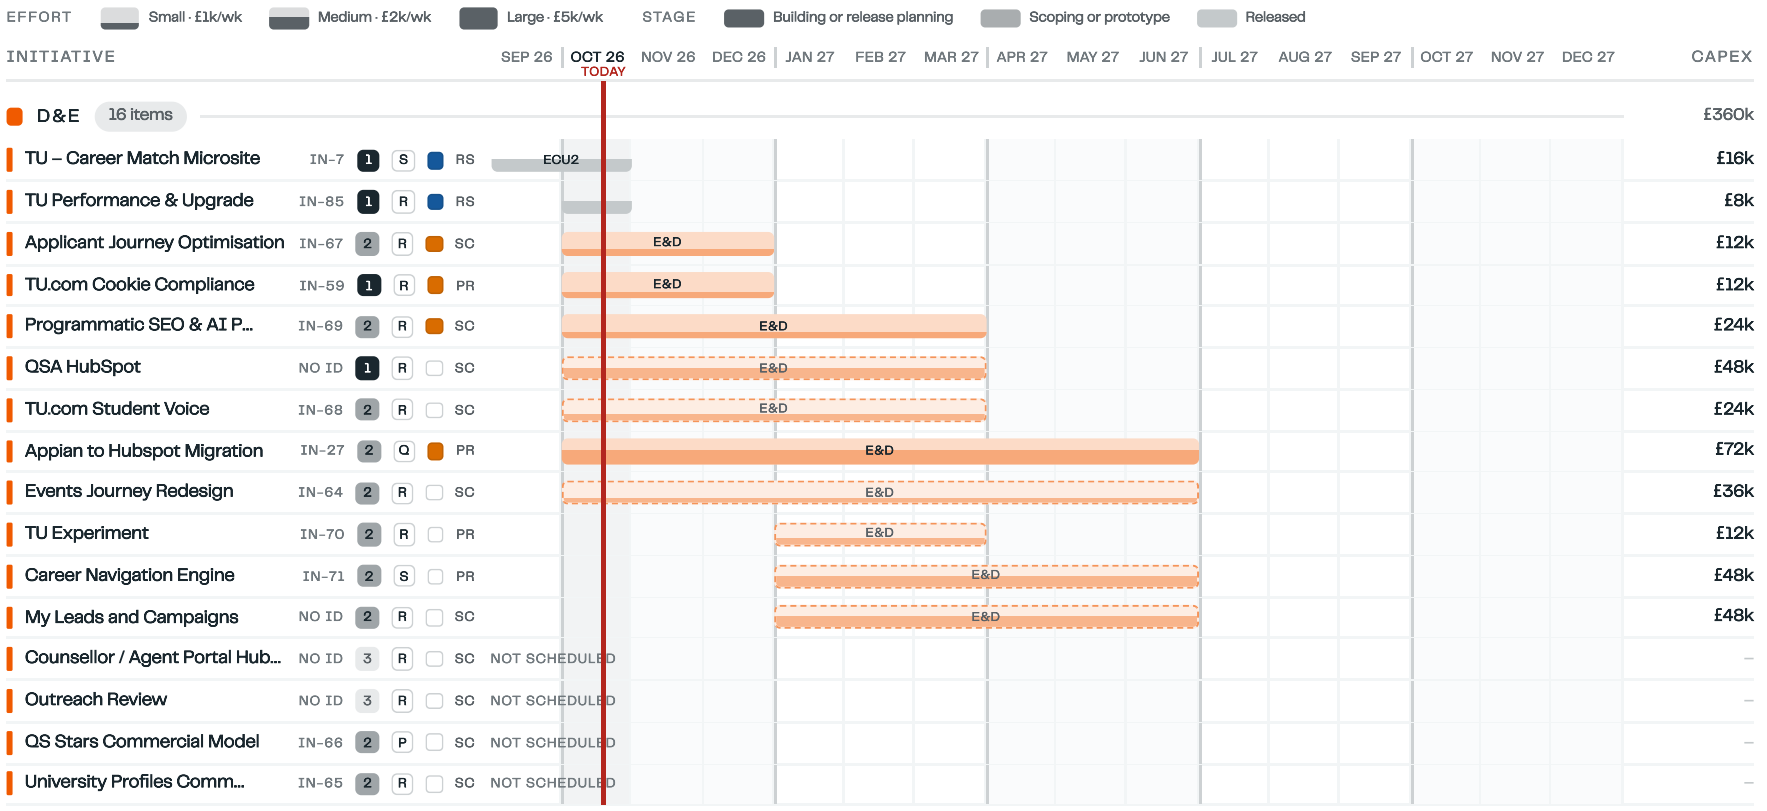


TOTAL CAPEX — 12 of 16 initiatives scheduled · 6 small, 6 medium at £1k / £2k / £5k a week · £144k approved by the investment committee, £216k not yet — £360k

## TU Performance & Upgrade

IN-85 · DIGITAL AND EVENTS · RELEASED

Drupal 11 tested; the 19 October release ran into an issue and is rescheduled to 21 October. All tested and ready to go live this Monday. Update 19 October: the release ran into an issue and has been rescheduled to Wednesday 21 October.

## Appian to Hubspot Migration

IN-27 · QS APPLY · QS APPLY (APPIAN) · PROTOTYPE

workshop findings consolidated into a master document; technical assessment of migration solutions. Consolidated the documents and findings from stakeholder workshops into a single master document to provide a unified reference for the migration initiative. Met with the Technology team to analyse potential migration solutions, discuss technical considerations, and evaluate the approach for migrating the existing Appian functionality.

## Digital and Events

OTHER WORK · NOT LINKED TO AN INITIATIVE

Finance page: BE work is blocked due to a change in business requirements. FE is starting as planned for the sections where no changes are expected. Emails redesign: Testing is being finalised for release on Monday. Marcomms Dashboard: Event-specific pages are under development. Client App: Improvements and fixes reported are done; this is currently in testing.

## QS Apply (Appian)

OTHER WORK · NOT LINKED TO AN INITIATIVE

Applicant and Application Count Discrepancy: Investigated discrepancies in applicant and application counts caused by an error in PAM/SAM assignment. PAM/SAM Reassignment: Performed a manual database update to correct the reassigned PAM and SAM details and address the assignment issue.

## D&E

OTHER WORK · NOT LINKED TO AN INITIATIVE

HUB1 switch-back: Corrected the HUB1 deployment configuration behind MongoDB connection failures and completed the switch back to the upgraded OS and container environment. GitHub Actions preparation: Progressed GitHub Actions-based deployment preparation for HUB1. Tableau server: Prepared the replacement Tableau server, backups and required drivers. Coordinated validation by the teams using Tableau and received their confirmation. Solr server reboot RCA: Completed the production Solr server reboot RCA and documented corrective and preventive actions. Rovo–Microsoft Teams authorisation: Worked with CORP-IT on Rovo–Microsoft Teams authorisation. The authorisation prompt is resolved, but automatic transcript retrieval remains unavailable.

## Digital and Events

RISKS AND DECISIONS

Risks and decisions. Drupal sprint release. Because of the new rankings release this week and the hackathon, it was decided to postpone this to 19 October.

## D&E

RISKS AND DECISIONS

Risks and decisions. D&E: Live TU and TM PHP and Drupal upgrades remain on hold pending developer confirmation and approval.

SECTION 6 OF 6

# University Services

3 initiatives reported

1 prototype
2 building

EFFORT Small · £1k/wk · Medium · £2k/wk · Large · £5k/wk STAGE Building or release planning · Scoping or prototype · Released

| INITIATIVE | | | | | | SEP 26 | OCT 26 TODAY | NOV 26 | DEC 26 | JAN 27 | FEB 27 | MAR 27 | APR 27 | MAY 27 | JUN 27 | JUL 27 | AUG 27 | SEP 27 | OCT 27 | NOV 27 | DEC 27 | CAPEX |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| UNIVERSITY SERVICES | 15 items | | | | | | | | | | | | | | | | | | | | | £316k |
| Aurora – Student Scoring Mo… | IN-56 | 2 | R | BD | | UBS DEV | | | | | | | | | | | | | | | | £12k |
| Aurora Data Integrity | IN-82 | 1 | R | BD | | UBS DEV | | | | | | | | | | | | | | | | £16k |
| Aurora Implementation | IN-30 | 1 | R | RP | | UBS DEV | | | | | | | | | | | | | | | | £32k |
| Appian to Hubspot Migration | IN-54 | 1 | Q | PR | | UBS DEV | | | | | | | | | | | | | | | | £56k |
| Decommission Informatica | IN-88 | 1 | R | BD | | UBS DEV | | | | | | | | | | | | | | | | £48k |
| QAS Uni Svcs Reporting App | IN-40 | 2 | R | PR | | UBS DEV | | | | | | | | | | | | | | | | £16k |
| Aurora – Counsellor Feedback | IN-53 | 2 | R | SC | | UBS DEV | | | | | | | | | | | | | | | | £32k |
| Aurora – Document Credibility | IN-8 | 2 | R | SC | | UBS DEV | | | | | | | | | | | | | | | | £32k |
| Aurora – Student Sentiment I… | IN-48 | 2 | R | PR | | UBS DEV | | | | | | | | | | | | | | | | £32k |
| Aurora – Client Data API | IN-81 | 2 | R | BD | | UBS DEV | | | | | | | | | | | | | | | | £40k |
| Aurora – WeChat | IN-47 | 2 | R | PR | NOT SCHEDULED | | | | | | | | | | | | | | | | | – |
| Flat File Uploads | IN-97 | 2 | R | SC | NOT SCHEDULED | | | | | | | | | | | | | | | | | – |
| Rebuild Enquiry APIs | IN-96 | 2 | R | SC | NOT SCHEDULED | | | | | | | | | | | | | | | | | – |
| Uni Services – Productivity Das… | IN-9 | 2 | R | PR | NOT SCHEDULED | | | | | | | | | | | | | | | | | – |
| Uni Svcs – Operational Tickets | IN-49 | 2 | R | BD | NOT SCHEDULED | | | | | | | | | | | | | | | | | – |
| TOTAL CAPEX | 10 of 15 initiatives scheduled · 2 small, 8 medium at £1k / £2k / £5k a week · £100k approved by the investment committee, £216k not yet | | | | | | | | | | | | | | | | | | | | | £316k |

## Appian to Hubspot Migration

IN-54 · UBS DEVELOPMENT · QS APPLY (APPIAN) · UBS · PROTOTYPE

enquiry-form replacements (Keele, RCA, Griffith International, ACU) and ESI replacement (Stirling). QS Apply: migration discovery and technical assessment. Infrastructure: extraction scripts for the HubSpot migration. Consolidated the documents and findings from stakeholder workshops into a single master document to provide a unified reference for the migration initiative. Met with the Technology team to analyse potential migration solutions, discuss technical considerations, and evaluate the approach for migrating the existing Appian functionality. Stirling development has completed changes for auto ticket creation and the new tag contact association, and is now testing the new changes for error notification. Progressed UAT FSx configuration and updated extraction scripts for the HubSpot migration.

## Aurora Data Integrity

IN-82 · DATA TEAM (BI) · BUSINESS INTELLIGENCE (BI) · BUILDING

HubSpot data quality status-history corrections and COI fixes; Synergy2 pipeline flow restored and web-form classification agreed. Status-history correction work remains incomplete and requires validation across the remaining student stages. Missing intake and faculty issues on COIs were being addressed; missing COI loads and date-entered inquiry cases remain under review. Web forms will be classified as communications in the Contact Source or Tag History structure. Initial web-form migration will prioritise Stirling, Griffith International and King's, followed by QA before wider rollout. Synergy2 pipeline flow was restored after the 12 October issue. Web forms will be classified as Communications with a Webform category and submission date.

## Decommission Informatica

IN-88 · UBS DEVELOPMENT · BUILDING

S3 flat file (Griffith International, Edith Cowan University, Brighton), Keystone (RCA signed off, Edith Cowan University in development); LSBU on hold. No updates this week for York. Griffith International's replacement is awaiting deployment, pending the API replacement. RCA has been signed off. Deployment is pending completion of the API replacement.

## UBS Development

OTHER WORK · NOT LINKED TO AN INITIATIVE

Appian support: Investigated an issue where PAM and SAM were automatically assigned to all external counsellors rather than a single agency. The issue was caused by an incorrect query for the counsellors and agents that were migrated. No further errors have occurred since the incident, and all counsellors have been updated with the correct PAM and SAM.

## CX Systems

OTHER WORK · NOT LINKED TO AN INITIATIVE

China SIP: Conducted SIP testing and investigated calling issues. Aircall: Coordinated with the Engineering team on reported bugs and the India calling issue. Student Success: Communicated SIP implementation updates and the India calling outage to Student Success managers. Macquarie University: Progressed the SMS setup. QS Events: Coordinated with Niswey and QS Events on the WhatsApp setup. KCL: Implemented IVR changes and investigated call-routing behaviour. Sunway: Updated the IVR configuration. UK Number Porting: Progressed the porting of UK numbers to Aircall. US Number Porting: Unmasked and tested US numbers ported from Twilio to Aircall. WhatsApp Automation: Worked on automating WhatsApp replies for missed calls.

## UBS

OTHER WORK · NOT LINKED TO AN INITIATIVE

User offboarding and domain configuration: Completed user offboarding, mailbox safe-sender updates and new-domain configuration.

## UBS Development

RISKS AND DECISIONS

Risks and decisions. One institution's test environment (UoL) is missing required licensing to proceed with development. Simon Pennington is arranging access. Clare is awaiting the Data Model from Daniel before development on the HubSpot x HubSpot integration can begin for UTS College. Badrul to finalise Agent Tag mappings for Brighton. Badrul, Rez and Clare to review Data Model change requests (UTM and Student Type) and advise on how this data should be captured in HubSpot for Stirling.

## CX Systems

RISKS AND DECISIONS

Risks and decisions. QS Events Niswey Vira. Awaiting finalisation of the Niswey Vira subscription agreement between QS and Niswey.
